

Job Name: 26-1635 - KYTC Oldham Co (261505)

Job Location: Peewee Valley, KY

Contractor: Cleary Construction, Inc.

Plant: 100

7/24/2026 2:05:43 PM

Tech: Jared - F

PC: T. Ryan



Structure ID: 13829-16 CBIA-1

P3 BX2436-08R24

BOX RISER 8inW T/G

P5) 24" x 120" - CB INLET KY A 10' TOP RIGHT F/G - 10"

P4) 24" x 120" - CB INLET KY A 10' BOTTOM RIGHT T/G - 18"

P3) 24" x 36" - BOX RISER 8inW T/G - 24"

P2) 36" x 48" - CB FT REDUCER 24"x36" HOLE T/F - 8"

P1) 36" x 48" - BOX BASE 8inW, 8inF, Variable Ht F/n - 43"

1) CASTING - HOE KY-206 F/C (KY CBI A)

1) 36" x 48" - Conseal CS-102 1.00"

2) 24" x 36" - Conseal CS-102 1.00"

1) Hole - 40

1) Hole - 28

1) Hole - 34

1) Hole - 6

3398 lb

5270 lb

2449 lb

1654 lb

6092 lb

206 lb

0 lb

0 lb

0 lb

0 lb

0 lb

0 lb

Structure Total: 19069 lb

Structure Notes:

** KYTC STATE PROJECT **

1. PER KYTC CBI TYPE A / ASTM C913 SPEC'S.

2. CONCRETE = 4,000 PI AT 28 DAYS.

3. CASTING BY ICAST (HOE KY-206 F/C (KY CBI A)).

REINFORCING PER ASTM A615 (GRADE 60).

- TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W.

- TRANS. SLAB (As .62) #5 BARS AT 6" C.C.E.W (DBL MAT)

- WALLS (As .31) #5 BARS AT 12" C.C.E.W.

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Rim: 755.5'

Rim to Invert: 8.85'

Slack: 3.2"

Sump: 0"

Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)


(P5)

(P4)

(P3) <<

(P2)

(P1)

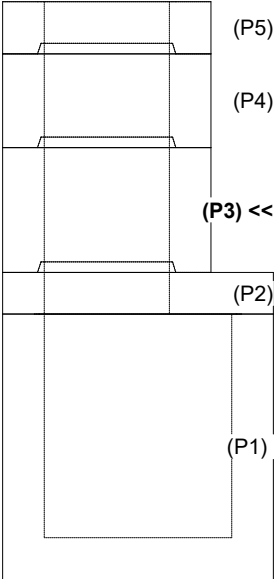


INSIDE WALL DIMENSIONS

Front

Right (36")

Back (24")

Left



(P3)

EXT

24"

Coating (Int):

Coating (Ext):

Seam Up: Tongue

Seam Dn: Groove

Wall Thickness: 8"

Floor Height: 0"

Height (Int): 24"

Height (Ext): 24"

Weight (Net): 2449 lb

Volume (Net): 0.63cu.yd
