



Job Name: 26-1635 - KYTC Oldham Co (261505) Job Location: Pee wee Valley, KY Contractor: Cleary Construction, Inc.				Plant: 100 7/24/2026 2:03:44 PM		Tech: Jared - F PC: T. Ryan				
Structure ID: 13990-17 CBIA-2										
P1 BX3636-08BAVF BOX BASE 8inW, 8inF, Variable Ht F/n										
P4) 24" x 120" - CB INLET KY A 10' TOP RIGHT F/G - 10" P3) 24" x 120" - CB INLET KY A 10' BOTTOM RIGHT T/G - 18" P2) 36" x 36" - CB TRANSITION SLAB 24"X36" HOLE T/F - 8" P1) 36" x 36" - BOX BASE 8inW, 8inF, Variable Ht F/n - 34" 1) CASTING - HOE KY-206 F/C (KY CBIA) 1) 36" x 36" - Conseal CS-102 1.00" 1) 24" x 36" - Conseal CS-102 1.00" 2) Hole - 28 1) Hole - 6						3398 lb 5270 lb 1235 lb 4987 lb 206 lb 0 lb 0 lb 0 lb 0 lb Structure Total: 15096 lb		Structure Notes: . ** KYTC STATE PROJECT ** 1. PER KYTC CBI TYPE A / ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PI AT 28 DAYS. 3. CASTING BY ICAST (HOE KY-206 F/C (KY CBI A)). REINFORCING PER ASTM A615 (GRADE 60). - TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W. - TRANS. SLAB (As .62) #5 BARS AT 6" C.C.E.W (DBL MAT) - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.		
Rim: 757.04' Rim to Invert: 6.09' Slack: 3.08" Sump: 0" Step Position:										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1	750.95'	0°	26"	24" CMP	25"	Hole 28	28"	28"	-2"	0"
Invert 2	751.03'	180°	26"	24" CMP	25"	Hole 28	28"	28"	-1"	0"
Invert 3	753.03'	180°	12"	4" HDPE (perf pipe)	4.8"	Hole 6	6"	6"	24"	-14"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

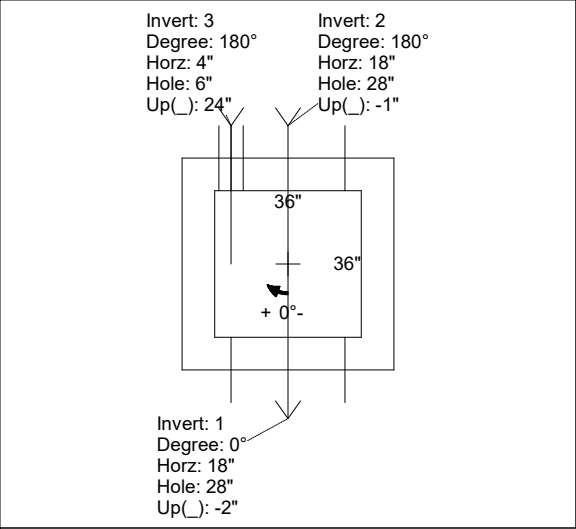

UPSIDE-DOWN VIEW (int. dimensions)

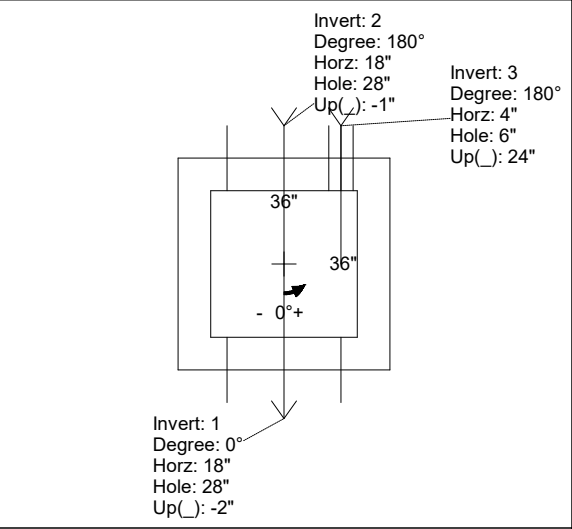

INSIDE WALL DIMENSIONS

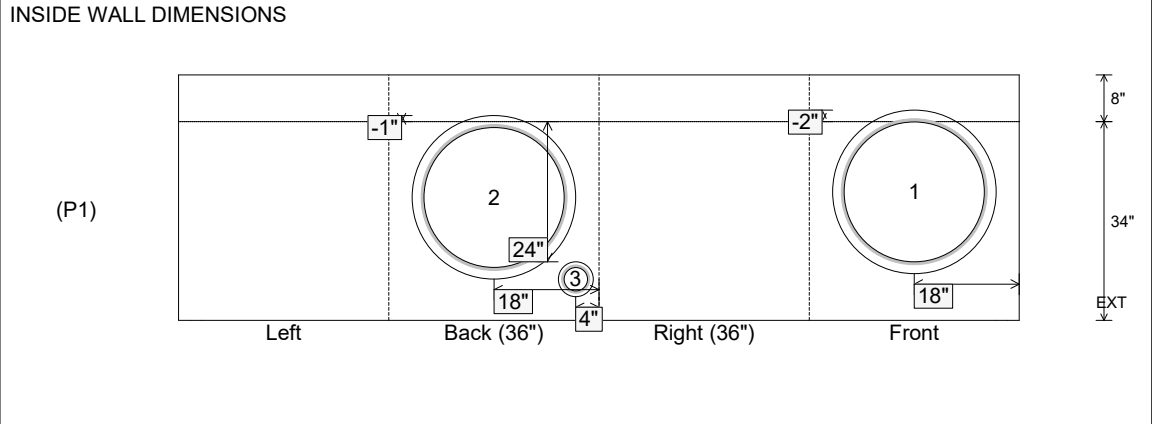

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 34" Height (Ext): 42"	Weight (Net): 4987 lb Volume (Net): 1.27cu.yd
----------------------------------	-------------------------------	--	--	--
