

Contractor: Cleary Construction, Inc.

TECH: Jared - F

Plant: 100



Size: 24" x 36"

Rim to Invert: 5.59'

Floor Height: 8"

Slack: 3.08"

**** KYTC STATE PROJECT ****

1. PER KYTC CBI TYPE A / ASTM C913 SPEC'S.
2. CONCRETE = 4,000 PI AT 28 DAYS.
3. CASTING BY ICAST (HOE KY-206 F/C (KY CBI A)).

REINFORCING PER ASTM A615 (GRADE 60).
 - TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W.
 - WALLS (As .31) #5 BARS AT 12" C.C.E.W.
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

STRUCTURE SUMMARY:

3400 lb

5270 lb

4087 lb

206 lb


0 | b

0 lb

0 | b



0 lb

Structure Total: 12963 lb

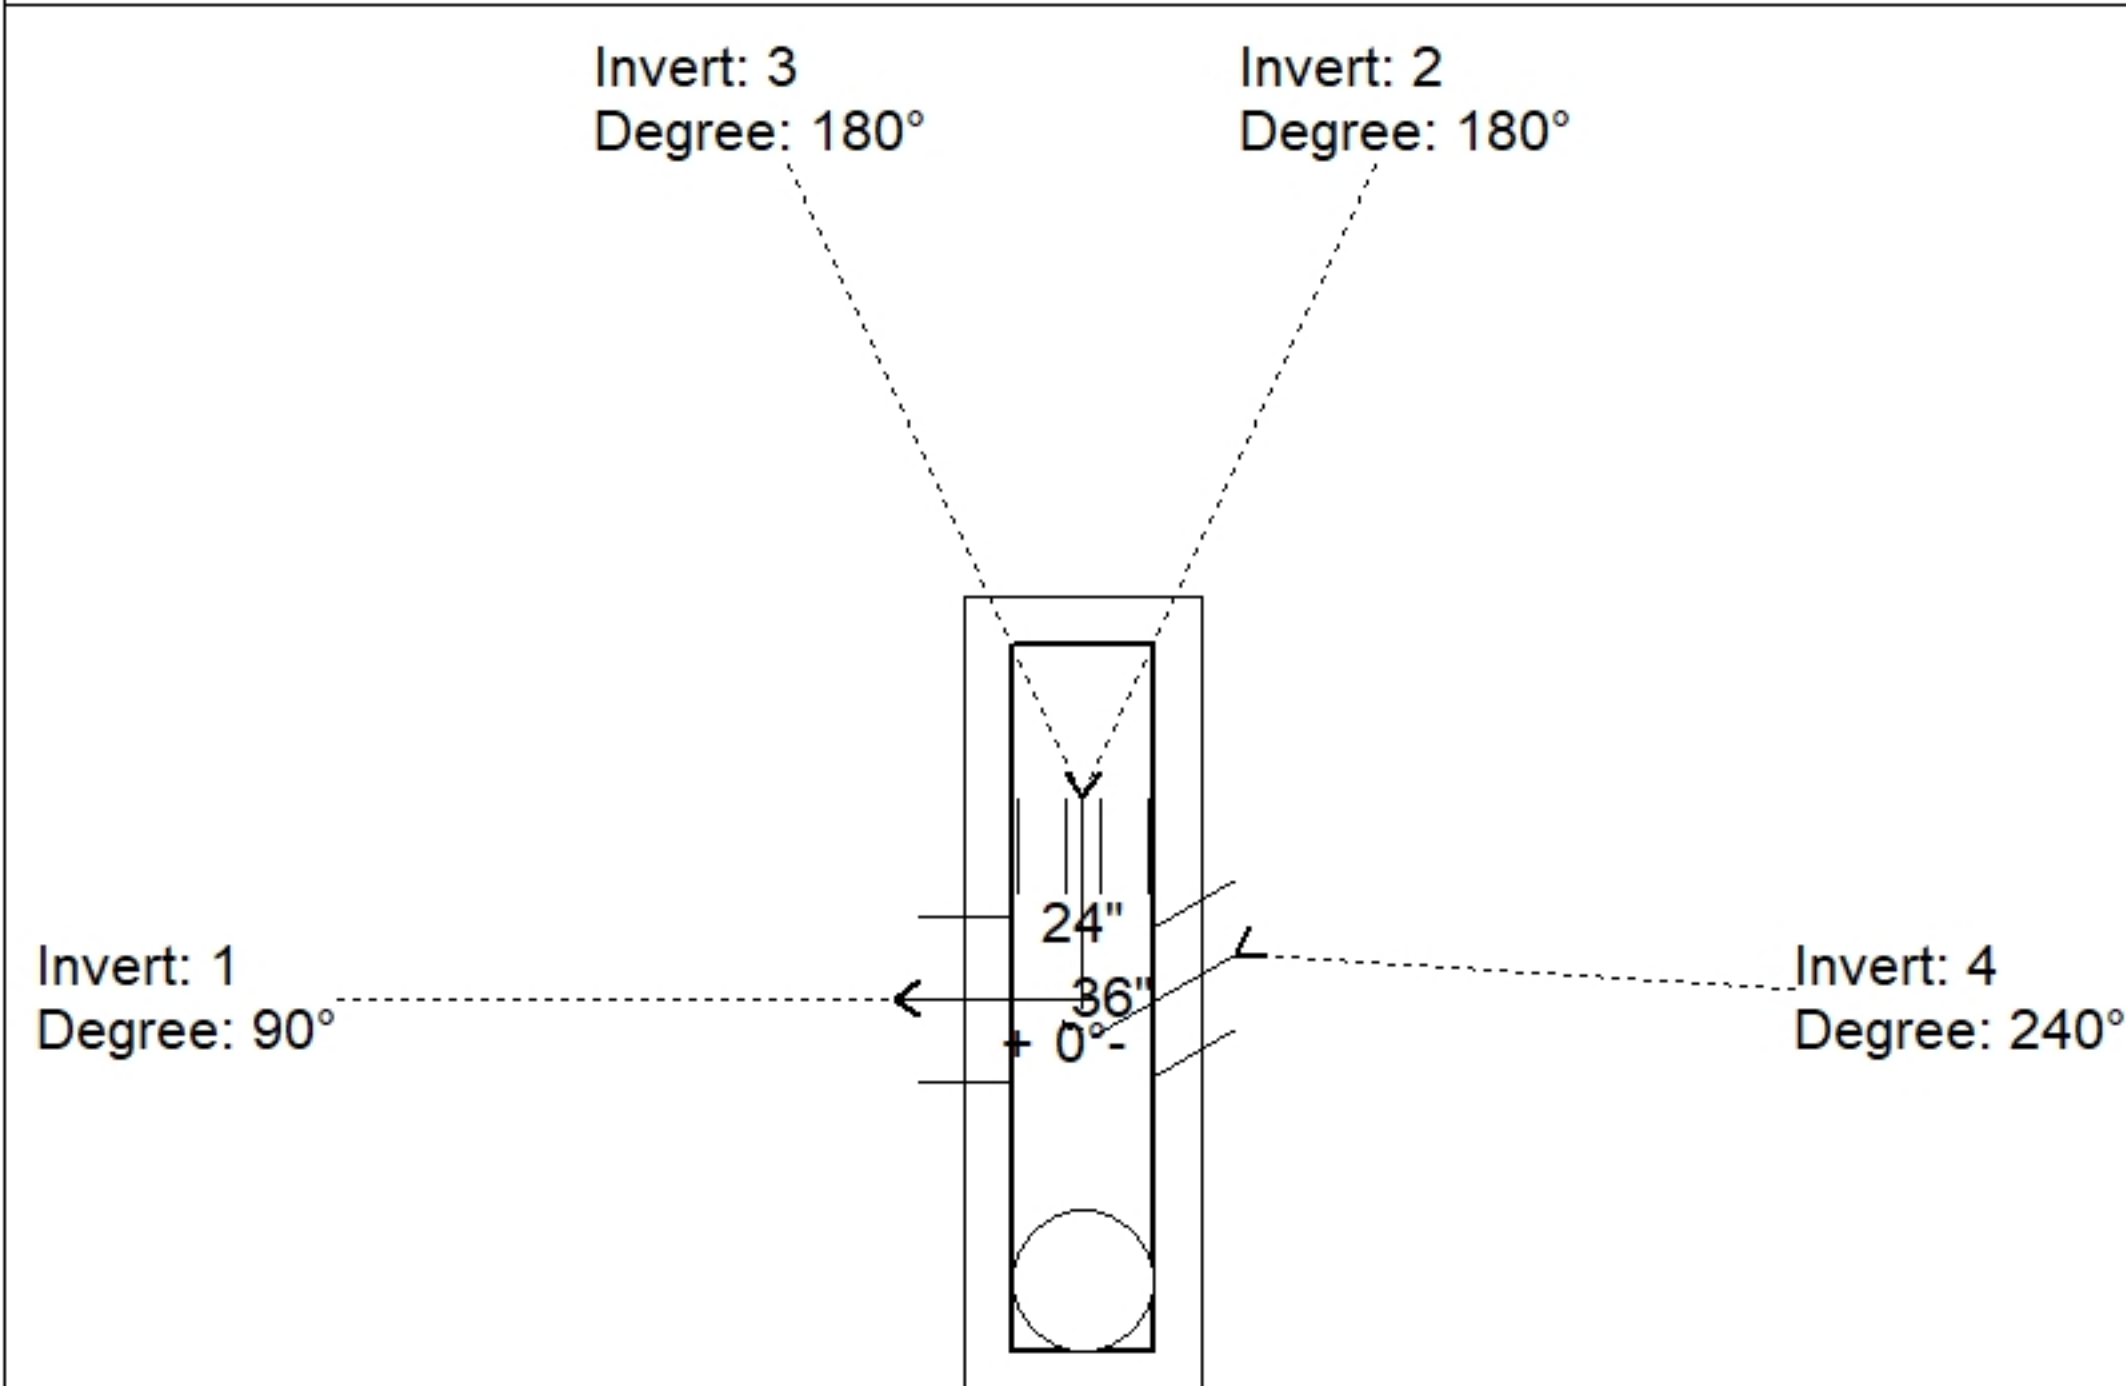

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	786.87'							
Reducer								
Invert 1	781.28'	90°	24" CMP	25"	28"	Hole 28	-2"	P1
Invert 2	781.36'	180°	18" CMP	19"	22"	Hole 22	-1.04"	P1
Invert 3	783.53'	180°	4" HDPE (perf pipe)	4.8"	6"	Hole 6	26"	P1
Invert 4	781.36'	240°	18" CMP	19"	22"	Hole 22	-1.04"	P1
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

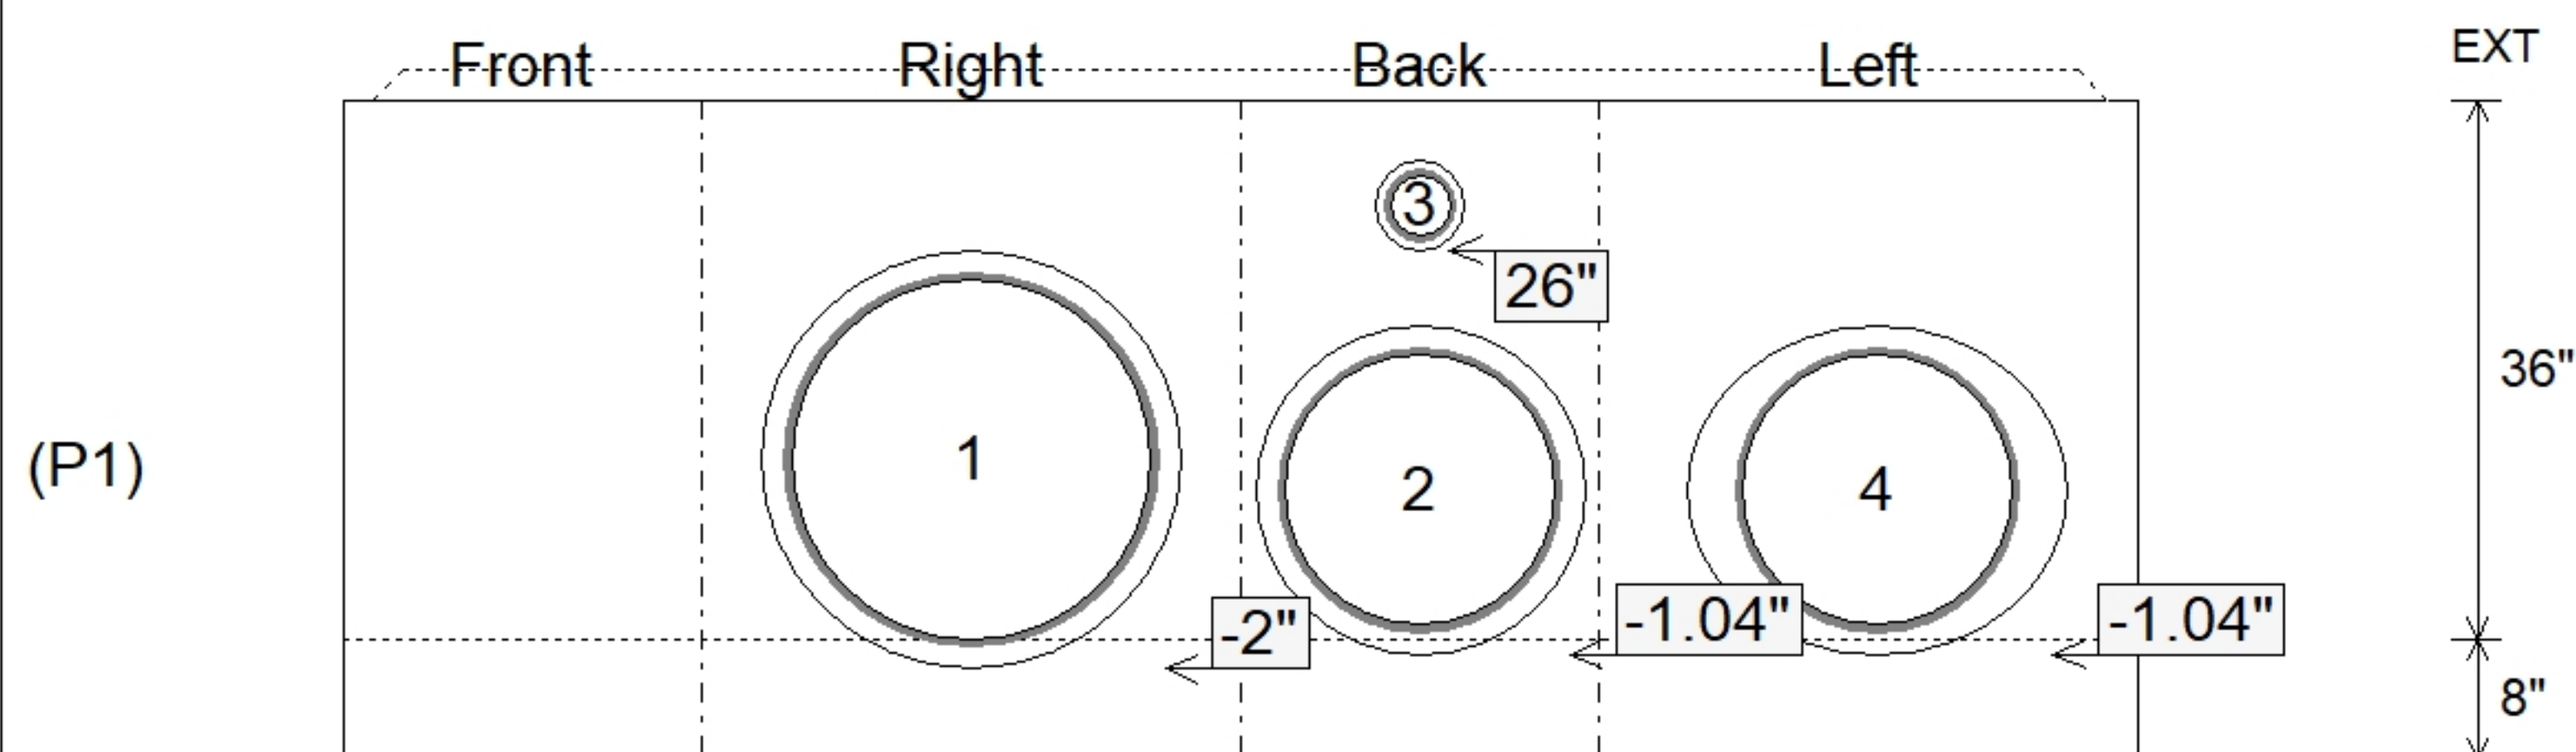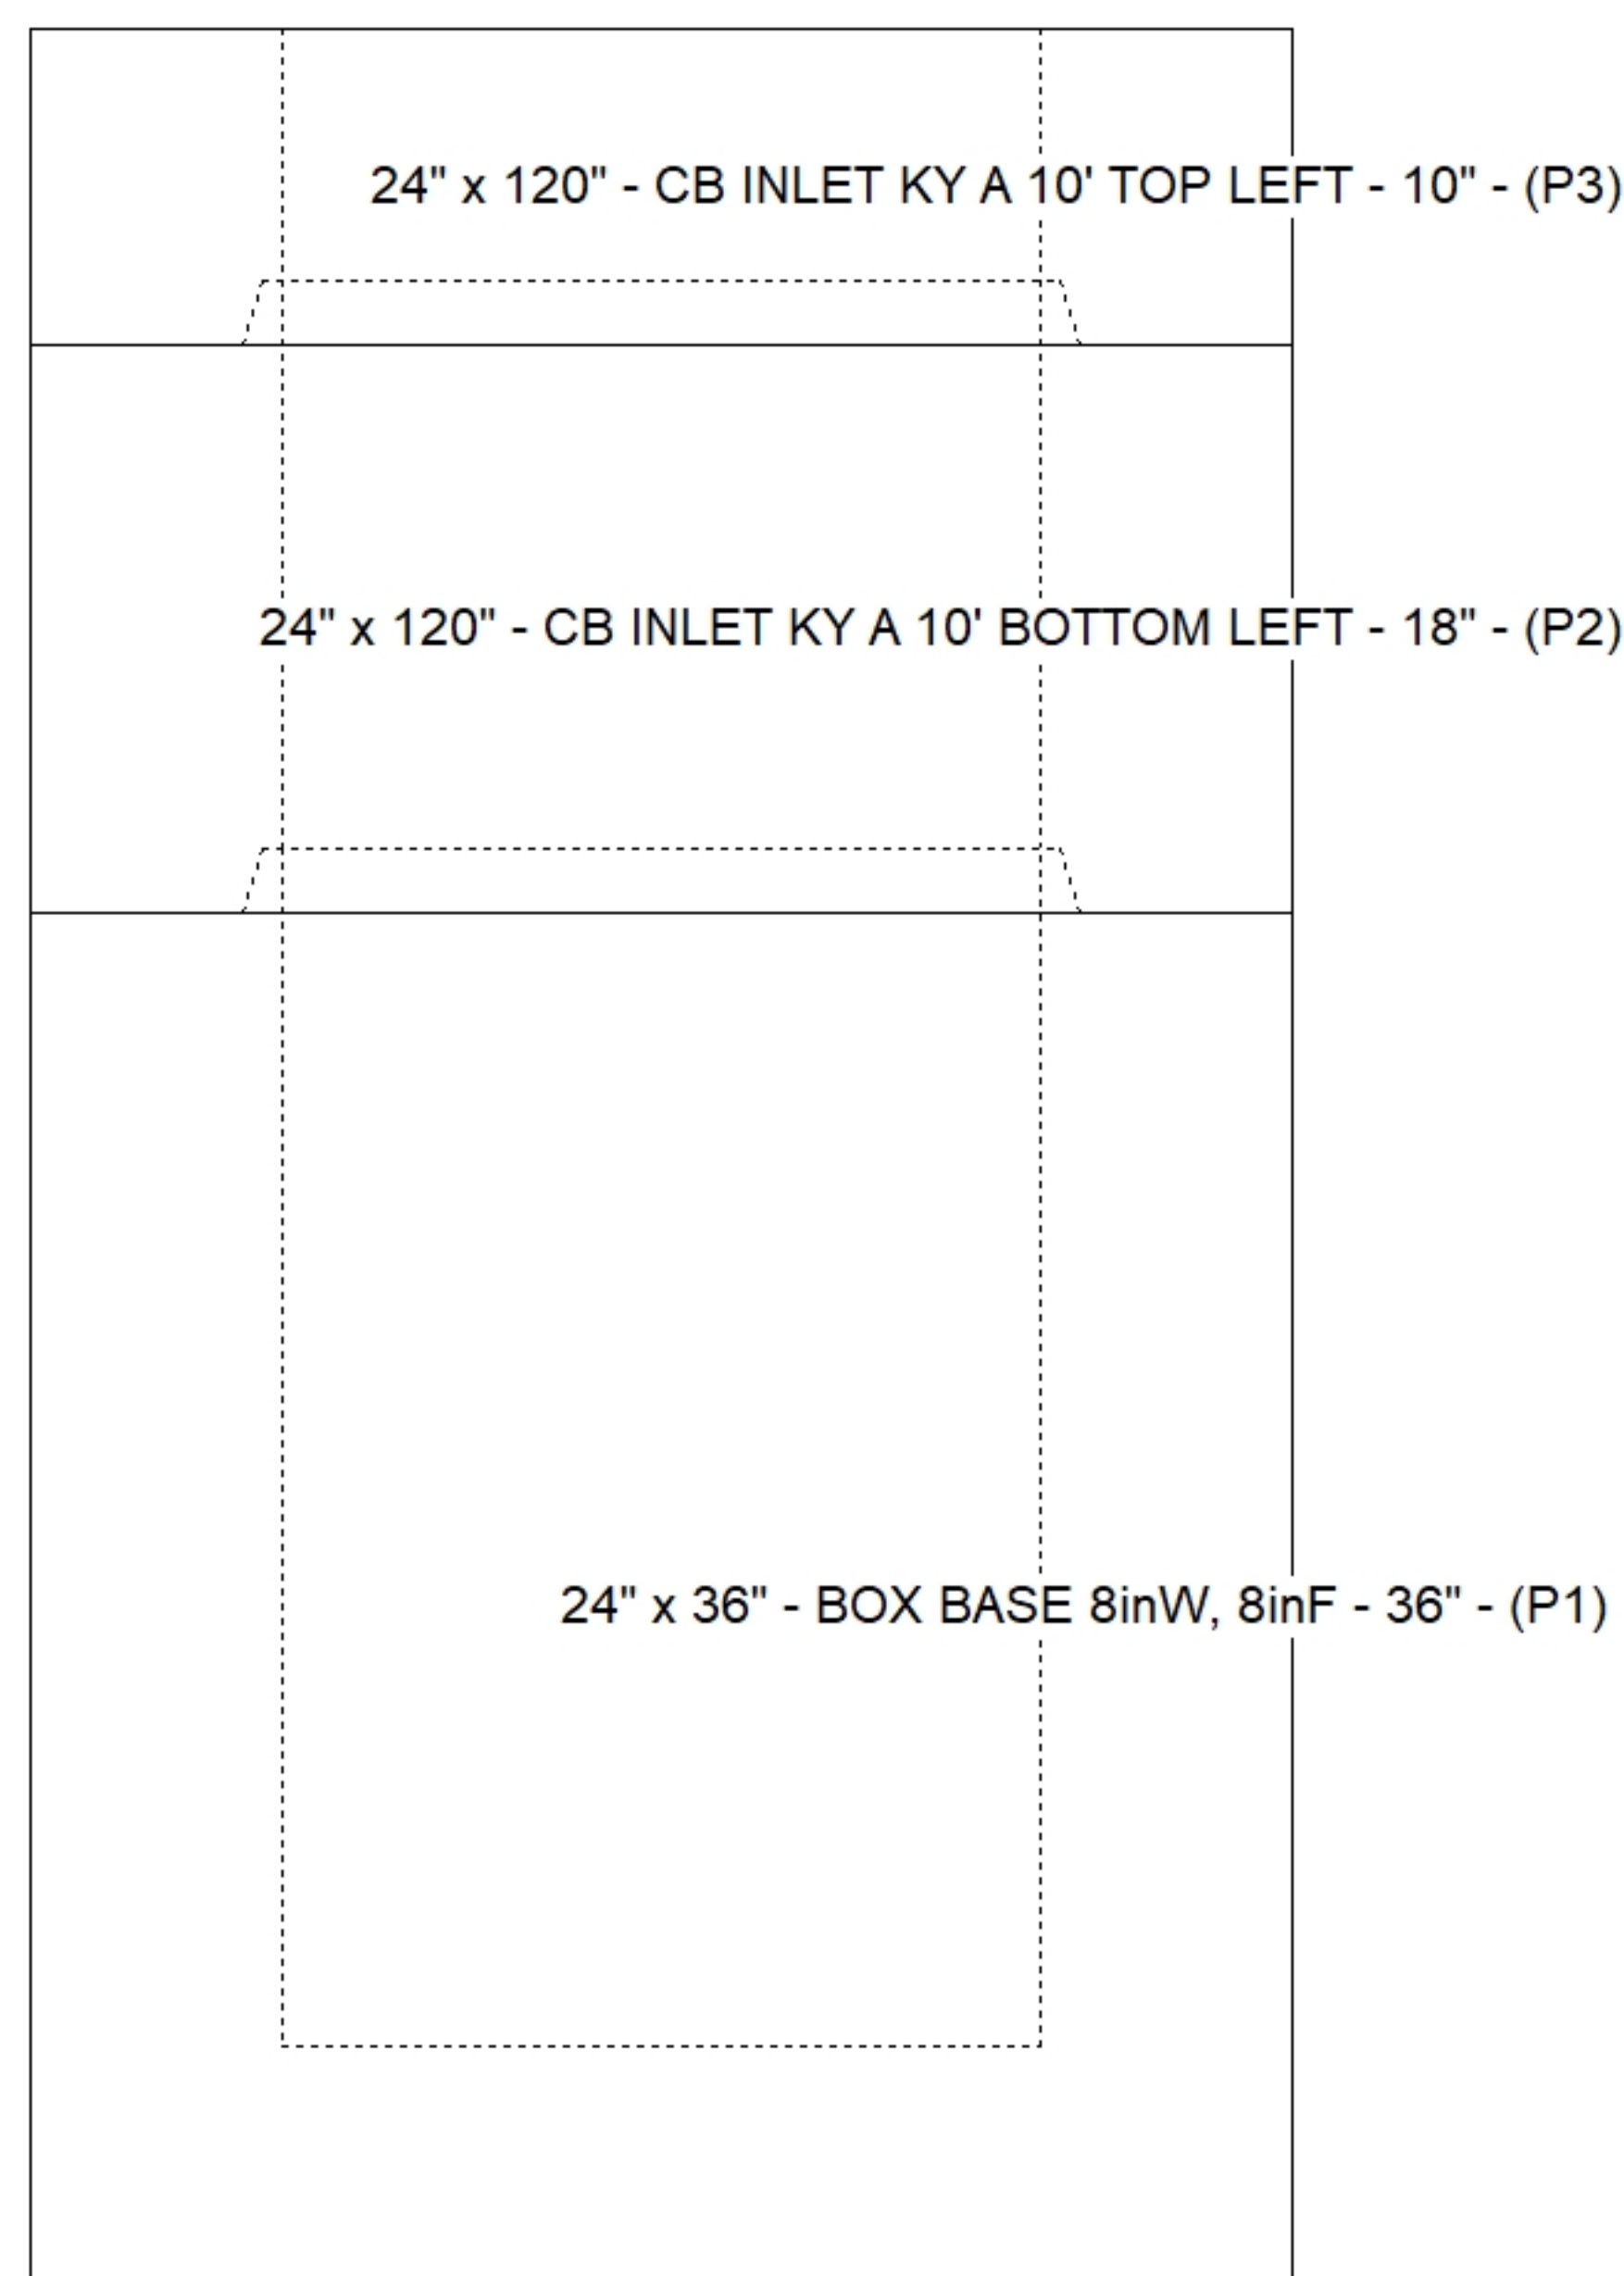

Submittal Drawing
7/28/2026 3:10:52 PM

SUBMITTAL
APPROVED BY:
