



Job Name: 26-1635 - KYTC Oldham Co (261505) Job Location: Pee wee Valley, KY Contractor: Cleary Construction, Inc.					Plant: 100 7/24/2026 2:04:01 PM		Tech: Jared - F PC: T. Ryan				
Structure ID: 15730-32 CBIA-30											
P1 BX2436-08BVF BOX BASE 8inW, 8inF, Variable Ht T/n											
P3) 24" x 120" - CB INLET KY A 10' TOP LEFT F/G - 10" P2) 24" x 120" - CB INLET KY A 10' BOTTOM LEFT T/G - 18" P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht T/n - 33" 1) CASTING - HOE KY-206 F/C (KY CBI A) 1) 24" x 36" - Conseal CS-102 1.00" 3) Hole - 22 1) Hole - 6						3400 lb 5270 lb 3979 lb 206 lb 0 lb 0 lb 0 lb ----- Structure Total: 12855 lb		Structure Notes: . ** KYTC STATE PROJECT ** 1. PER KYTC CBI TYPE A / ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PI AT 28 DAYS. 3. CASTING BY ICAST (HOE KY-206 F/C (KY CBI A)). REINFORCING PER ASTM A615 (GRADE 60). - TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W. - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 791.4' Rim to Invert: 5.34' Slack: 3.08" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1	786.06'	0°	20"	18" CMP	19"	Hole 22	22"	22"	-2"	0"	
Invert 2	786.14'	180°	20"	18" CMP	19"	Hole 22	22"	22"	-1"	0"	
Invert 3	788.06'	180°	12"	4" HDPE (perf pipe)	4.8"	Hole 6	6"	6"	23"	-8"	
Invert 4	786.14'	270°	26"	18" CMP	19"	Hole 22	22"	22"	-1"	0"	
Invert 5											
Invert 6											
Invert 7											
Invert 8											


RIGHT-SIDE UP VIEW (int. dimensions)

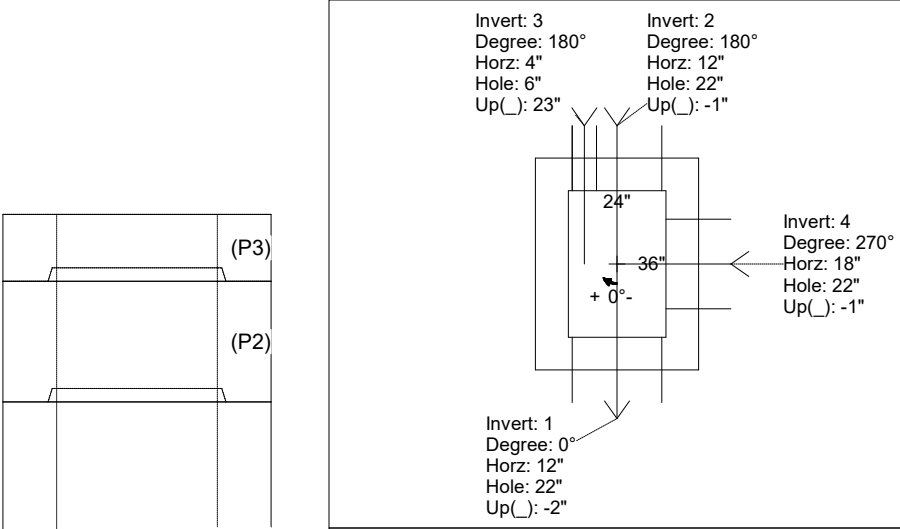

UPSIDE-DOWN VIEW (int. dimensions)

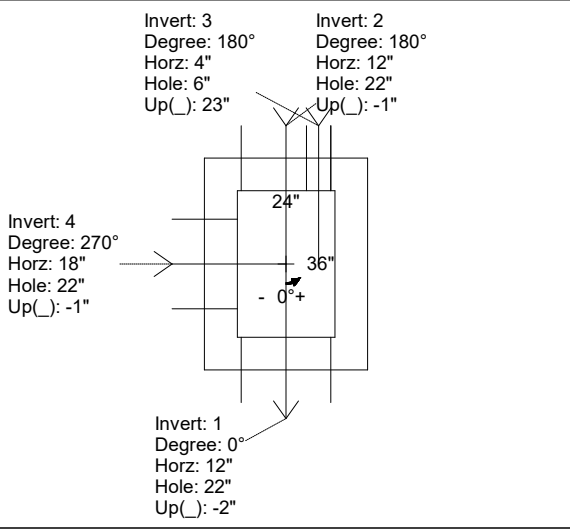

INSIDE WALL DIMENSIONS

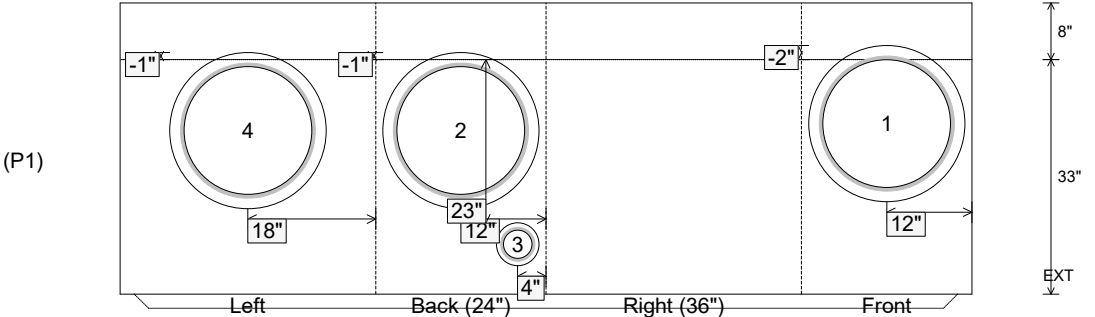

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 33" Height (Ext): 41"	Weight (Net): 3979 lb Volume (Net): 1.02cu.yd
----------------------------------	---------------------------------	--	--	--
