

Job Name: 26-1635 - KYTC Oldham Co (261505)

Job Location: Pee wee Valley, KY

Contractor: Cleary Construction, Inc.

Plant: 100

7/24/2026 2:04:22 PM

Tech: Jared - F

PC: T. Ryan



Structure ID: 16053-52 CBIA-13

P1 BX4848-08BAVF

BOX BASE 8inW, 8inF, Variable Ht F/n

P4) 24" x 120" - CB INLET KY A 10' TOP RIGHT F/G - 10"

P3) 24" x 120" - CB INLET KY A 10' BOTTOM RIGHT T/G - 18"

P2) 48" x 48" - CB FT REDUCER 24"X36" HOLE T/F - 8"

P1) 48" x 48" - BOX BASE 8inW, 8inF, Variable Ht F/n - 44"

1) CASTING - HOE KY-206 F/C (KY CBIA)

1) 48" x 48" - Conseal CS-102 1.00"

1) 24" x 36" - Conseal CS-102 1.00"

1) Hole - 40

2) Hole - 34

1) Hole - 6

3398 lb

5270 lb

2170 lb

7212 lb

206 lb

0 lb

0 lb

0 lb

0 lb

0 lb

Structure Total: 18255 lb

Structure Notes:

** KYTC STATE PROJECT **

1. PER KYTC CBI TYPE A / ASTM C913 SPEC'S.

2. CONCRETE = 4,000 PI AT 28 DAYS.

3. CASTING BY ICAST (HOE KY-206 F/C (KY CBI A)).

REINFORCING PER ASTM A615 (GRADE 60).

- TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W.

- TRANS. SLAB (As .62) #5 BARS AT 6" C.C.E.W (DBL MAT)


- WALLS (As .31) #5 BARS AT 12" C.C.E.W.

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


Rim: 793.94' Rim to Invert: 6.92' Slack: 3.04" Sump: 0" Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1	787.02'	105°	34.375"	36" CMP	37"	Hole 40	40"	41.411"	-2"	-6"
Invert 2	787.1'	195°	35.375"	30" CMP	31"	Hole 34	34"	35.199"	-1"	-5"
Invert 3	789.94'	180°	17"	4" HDPE (perf pipe)	4.8"	Hole 6	6"	6"	34"	-15"
Invert 4	787.1'	285°	35.375"	30" CMP	31"	Hole 34	34"	35.199"	-1"	-5"
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

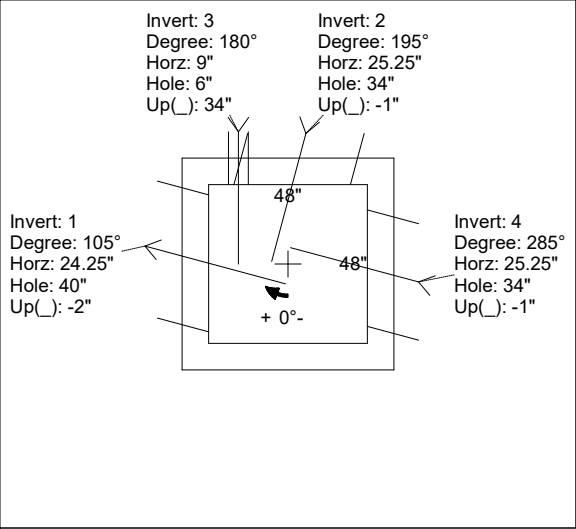

UPSIDE-DOWN VIEW (int. dimensions)

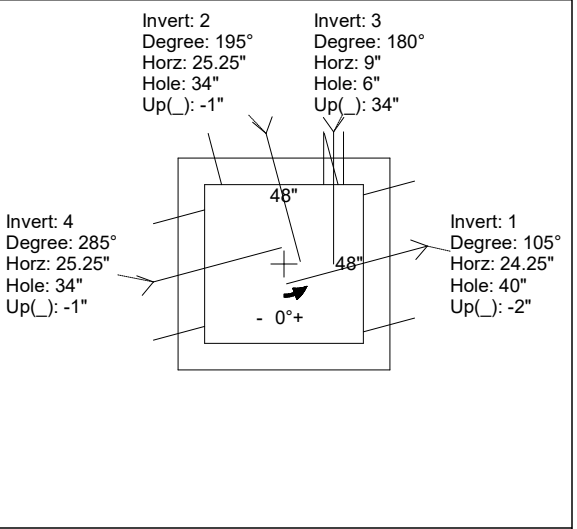

INSIDE WALL DIMENSIONS

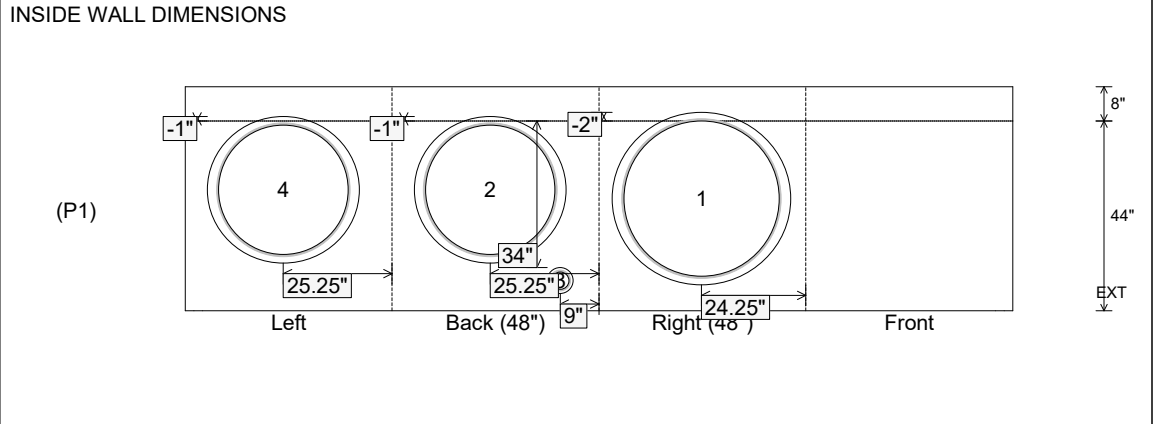

Coating (Int):

Coating (Ext):

Seam Up: Flat

Seam Dn: n/a

Wall Thickness: 8"

Floor Height: 8"

Height (Int): 44"

Height (Ext): 52"

Weight (Net): 7212 lb

Volume (Net): 1.84cu.yd
