

Job Name: 26-1635 - KYTC Oldham Co (261505)

Job Location: Pee wee Valley, KY

Contractor: Cleary Construction, Inc.

Plant: 100

7/27/2026 11:36:13 AM

Tech: Jared - F

PC: T. Ryan



Structure ID: 51051R-93 CBIA

P1 BX2436-08BVF

BOX BASE 8inW, 8inF, Variable Ht T/n

P3) 24" x 120" - CB INLET KY A 10' TOP SAG F/G - 10"

P2) 24" x 120" - CB INLET KY A 10' BOTTOM SAG T/G - 18"

P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht T/n - 37"

1) CASTING - HOE KY-206 F/C (KY CBI A)

1) 24" x 36" - Conseal CS-102 1.00"

2) Hole - 28

1) Hole - 16

1) Hole - 22

3398 lb

5270 lb

4044 lb

206 lb

0 lb

0 lb

0 lb

0 lb

Structure Total: 12918 lb

Structure Notes:

** KYTC STATE PROJECT **

1. PER KYTC CBI TYPE A / ASTM C913 SPEC'S.

2. CONCRETE = 4,000 PI AT 28 DAYS.

3. CASTING BY ICAST (HOE KY-206 F/C (KY CBI A)).

REINFORCING PER ASTM A615 (GRADE 60).

- TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W.

- WALLS (As .31) #5 BARS AT 12" C.C.E.W.

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Rim: 794.74'

Rim to Invert: 5.71'


Slack: 3.52"

Sump: 0"


Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1	789.03'	90°	26"	24" CMP	25"	Hole 28	28"	28"	-2"	0"
Invert 2	789.03'	180°	20"	24" CMP	25"	Hole 28	28"	26"	-2"	0"
Invert 3	789.03'	245°	22.25"	12" CMP	13"	Hole 16	16"	17.654"	-2"	5"
Invert 4	789.03'	0°	20"	18" CMP	19"	Hole 22	22"	22"	-2"	0"
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

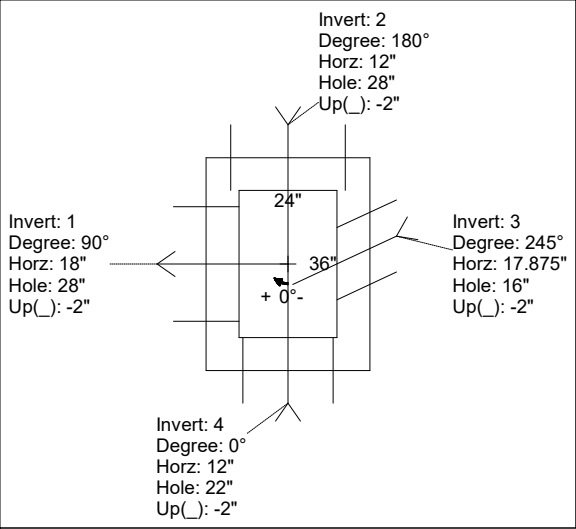


UPSIDE-DOWN VIEW (int. dimensions)

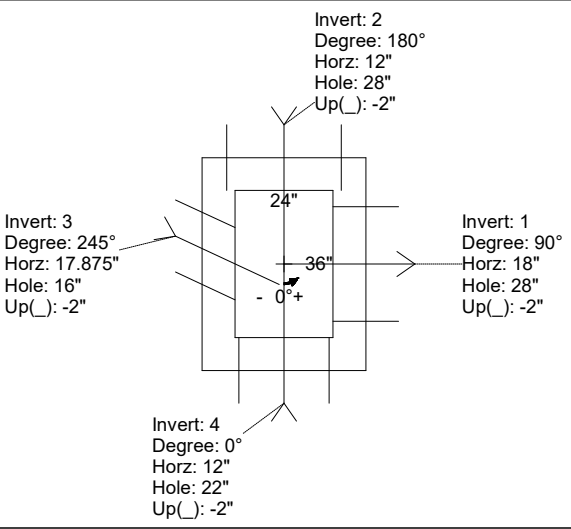


(P3)

(P2)

(P1) <<

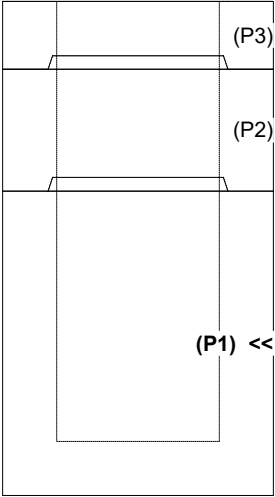

INSIDE WALL DIMENSIONS

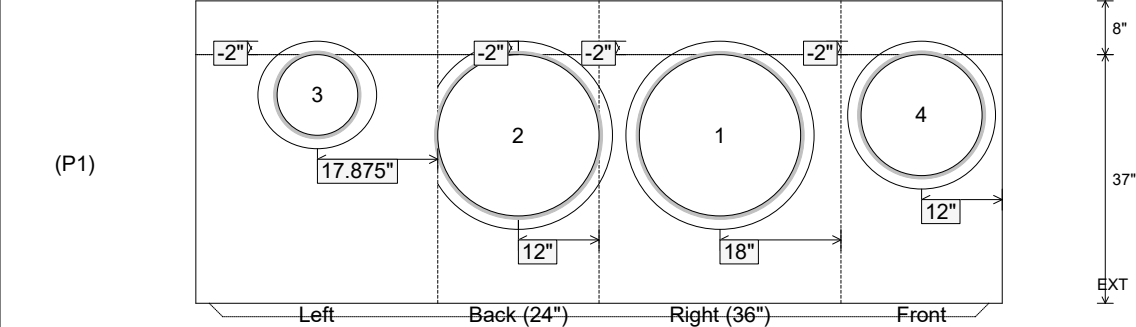

Coating (Int):

Coating (Ext):

Seam Up: Tongue

Seam Dn: n/a

Wall Thickness: 8"

Floor Height: 8"

Height (Int): 37"

Height (Ext): 45"

Weight (Net): 4044 lb

Volume (Net): 1.03cu.yd
