




Job Name: 26-1635 - KYTC Oldham Co (261505) Job Location: Pee wee Valley, KY Contractor: Cleary Construction, Inc.					Plant: 100 8/14/2026 1:20:40 PM		Tech: Jared - F PC: T. Ryan				
Structure ID: 35972-132 DBI13G											
P1 BX3232-08BAVF		BOX BASE 8inW, 8inF, Variable Ht F/n									
P3) 15" x 27" - P.I.P. - BY OTHERS - 8" P2) 32" x 32" - CB FLAT TOP 8"W w/15"x27" HOLE F/F - 8" P1) 32" x 32" - BOX BASE 8inW, 8inF, Variable Ht F/n - 44" 1) 32" x 32" - Conseal CS-102 1.00" 1) 15" x 27" - Conseal CS-102 1.00" 2) Hole - 20 2) Hole - 4					0 lb 1275 lb 5770 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 7044 lb		Structure Notes: **KYTC STATE PROJECT** 1. KYTC DBI TYPE 13G / ASTM C-913 SPEC'S. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. STUB #5 BARS 6" OUT TOP OF SLAB (SPA@12"C/C). 4. CASTING SUPPLIED BY OTHERS (HOE KY-230-G F/G (GRADE)). REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. (DBL MAT). - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 801.5'		Rim to Invert: 5.02'		Slack: 0.24"		Sump: 0"		Step Position:			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	796.48'	40°	31.125"	15" CMP	16"	Hole 20	20"	26.108"	-2.5"	-10"	
Invert 2	796.48'	180°	24"	15" CMP	16"	Hole 20	20"	20"	-2.5"	0"	
Invert 3	799.48'	90°	24"	4" WEEP HOLE	4"	Hole 4	4"	4"	36"	0"	
Invert 4	799.48'	270°	24"	4" WEEP HOLE	4"	Hole 4	4"	4"	36"	0"	
Invert 5											
Invert 6											
Invert 7											
Invert 8											

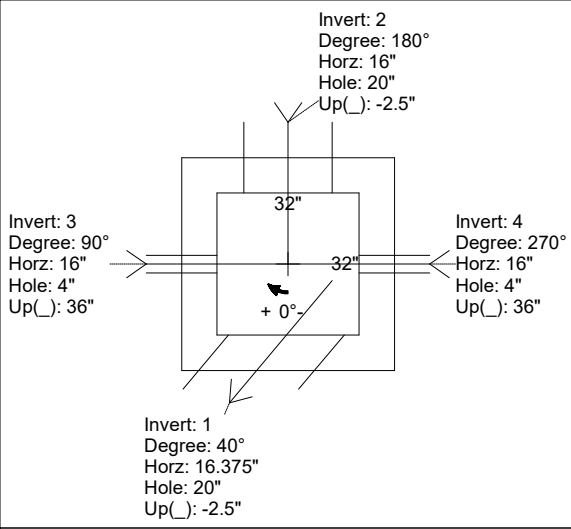


RIGHT-SIDE UP VIEW (int. dimensions)

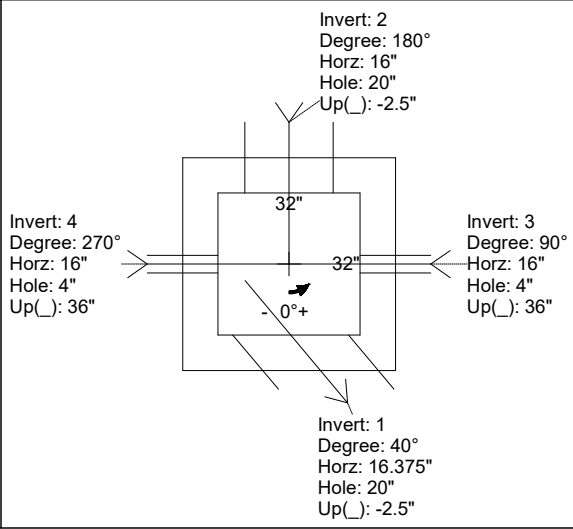

UPSIDE-DOWN VIEW (int. dimensions)

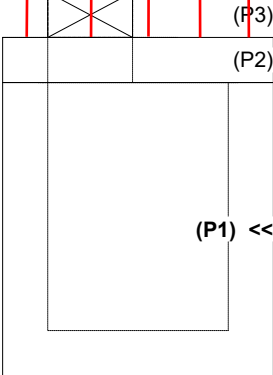

(P1) <<

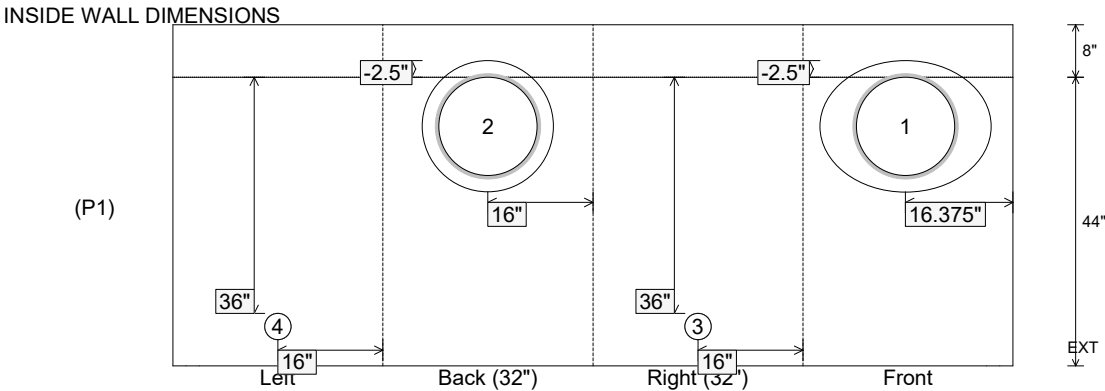

INSIDE WALL DIMENSIONS

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 44" Height (Ext): 52"	Weight (Net): 5770 lb Volume (Net): 1.47cu.yd
----------------------------------	-------------------------------	--	--	--
