



Job Name: 26-1635 - KYTC Oldham Co (261505) Job Location: Pee wee Valley, KY Contractor: Cleary Construction, Inc.					Plant: 100 8/12/2026 11:10:34 AM		Tech: Jared - F PC: T. Ryan				
Structure ID: 37980-130 DBI6F											
P2		BX3648-08R30		BOX RISER 8inW F/G							
P3) 36" x 48" - P.I.P. - BY OTHERS - 8" P2) 36" x 48" - BOX RISER 8inW F/G - 30" P1) 36" x 48" - BOX BASE 8inW, 8inF T/n - 48" 2) 36" x 48" - Conseal CS-102 1.00" 1) Hole - 18					0 lb 4028 lb 8508 lb 0 lb 0 lb ----- 12535 lb		Structure Notes: . **KYTC STATE PROJECT** 1. KYTC DBI TYPE 6F / ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. STUB #5 BARS 20" OUT TOP OF WALLS (SPA@12"C/C) 4. CASTING SUPPLIED BY OTHERS (HOE KY-426 TY.6F F/G). REINFORCING PER ASTM A615(GRADE 60). - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 762.93' Rim to Invert: 7.23' Slack: 0.76" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											


#5 DOWELS @ 12" O.C.
STUBBED 20" OUT THE
TOP OF THE WALLS

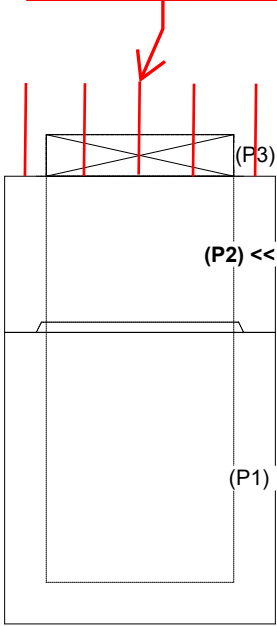

RIGHT-SIDE UP VIEW (int. dimensions)



INSIDE WALL DIMENSIONS

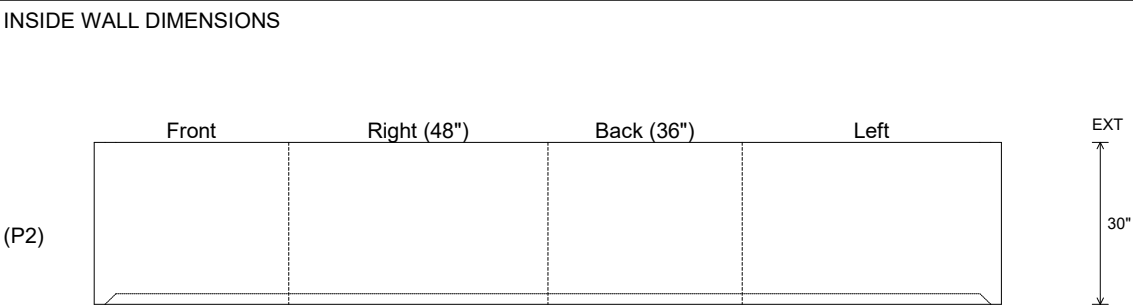

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 8" Floor Height: 0"	Height (Int): 30" Height (Ext): 30"	Weight (Net): 4028 lb Volume (Net): 1.03cu.yd
----------------------------------	----------------------------------	--	--	--
