




Job Name: 26-1635 - KYTC Oldham Co (261505) Job Location: Pee wee Valley, KY Contractor: Cleary Construction, Inc.					Plant: 100 8/14/2026 1:21:34 PM		Tech: Jared - F PC: T. Ryan				
Structure ID: 38900-133 DBI13G											
P2 BX2430-08R18		BOX RISER 8inW F/G									
P4) 15" x 27" - P.I.P. - BY OTHERS - 8" P3) 24" x 30" - CB FLAT TOP 8"W w/15"x27" HOLE F/F - 8" P2) 24" x 30" - BOX RISER 8inW F/G - 18" P1) 24" x 30" - BOX BASE 8inW, 8inF, Variable Ht T/n - 38" 2) 24" x 30" - Conseal CS-102 1.00" 1) 15" x 27" - Conseal CS-102 1.00" 1) Hole - 22 1) Hole - 20 2) Hole - 4						0 lb 963 lb 1675 lb 4340 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 6979 lb		Structure Notes: . **KYTC STATE PROJECT** 1. KYTC DBI TYPE 13G / ASTM C-913 SPEC'S. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. STUB #5 BARS 6" OUT TOP OF SLAB (SPA@12"C/C). 4. CASTING SUPPLIED BY OTHERS (HOE KY-230-G F/G (GRADE)). REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. (DOUBLE MAT) - WALLS (As .31) #5 BARS AT 12" C.C.E.W.. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 780.63'		Rim to Invert: 6'		Slack: 0"		Sump: 0"		Step Position:			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1											
Invert 2											
Invert 3	778.626'	90°	23"	4" WEEP HOLE	4"	Hole 4	4"	4"	8"	0"	
Invert 4	778.626'	270°	23"	4" WEEP HOLE	4"	Hole 4	4"	4"	8"	0"	
Invert 5											
Invert 6											
Invert 7											
Invert 8											

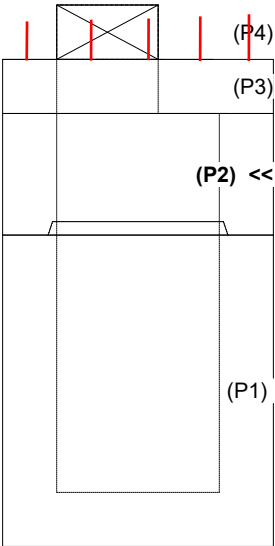

RIGHT-SIDE UP VIEW (int. dimensions)

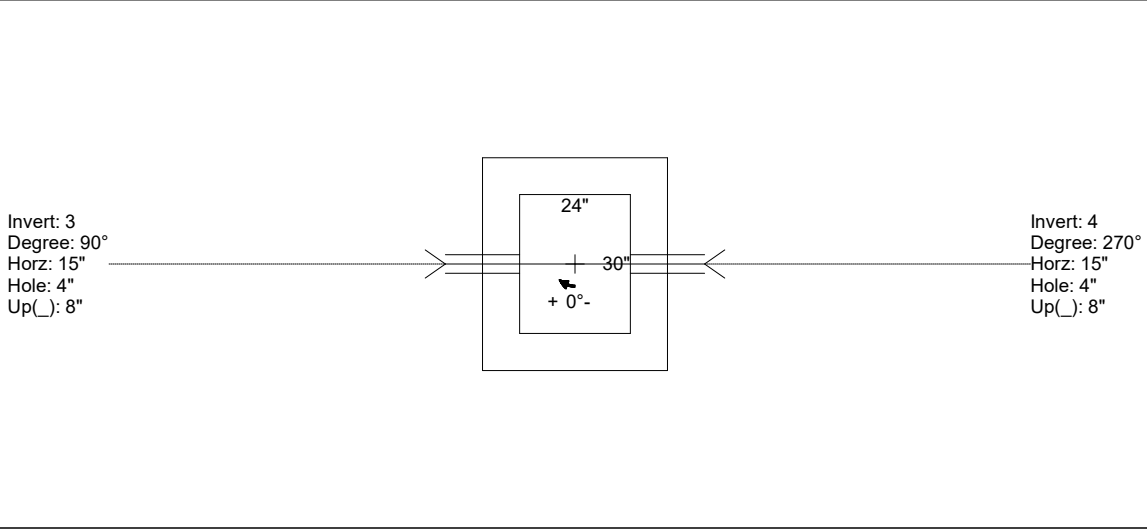

INSIDE WALL DIMENSIONS

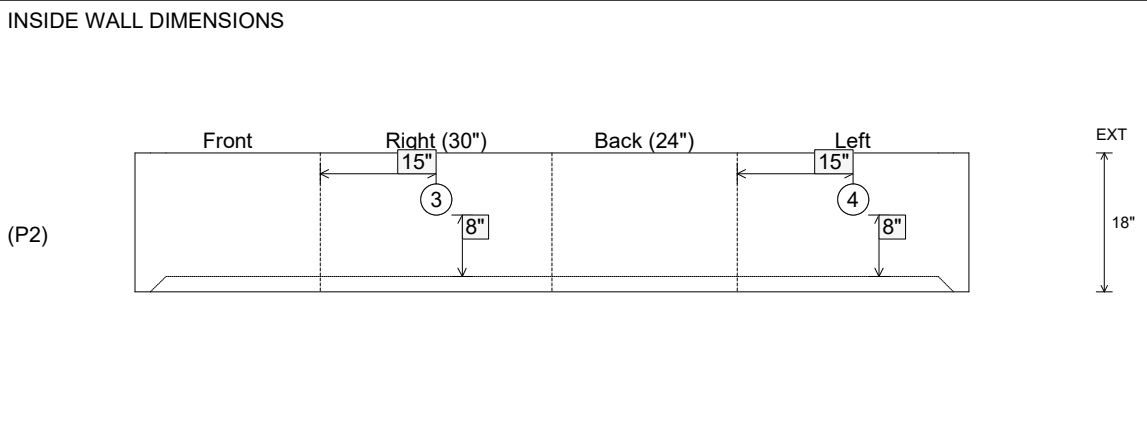

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 8" Floor Height: 0"	Height (Int): 18" Height (Ext): 18"	Weight (Net): 1675 lb Volume (Net): 0.43cu.yd
----------------------------------	----------------------------------	--	--	--
