

Contractor: Cleary Construction, Inc.

TECH: Jared - F

Plant: 100



Size: 24" x 30"

Rim to Invert: 5.56'

Floor Height: 8"

Slack: 2.72"

****KYTC STATE PROJECT****


1. KYTC DBI TYPE 13G / ASTM C-913 SPEC'S.
 2. CONCRETE = 4,000 PSI AT 28 DAYS.
 3. STUB #5 BARS 6" OUT TOP OF SLAB (SPA@12"C/C).
 4. CASTING SUPPLIED BY OTHERS (HOE KY-230-G F/G (GRADE)).
- REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. (DOUBLE MAT)
 - WALLS (As .31) #5 BARS AT 12" C.C.E.W..
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

STRUCTURE SUMMARY:


P3) 15" x 27" - P.I.P. - BY OTHERS - 8"
P2) 24" x 30" - CB FLAT TOP 8"W w/15"x27" HOLE - 8"
P1) 24" x 30" - BOX BASE 8inW, 8inF - 48"
1) 24" x 30" - Conseal CS-102 1.00"
1) 15" x 27" - Conseal CS-102 1.00"
2) Hole - 28
2) Hole - 4

0 lb
963 lb
5109 lb
0 lb
0 lb
0 lb
0 lb


Structure Total: 6073 lb

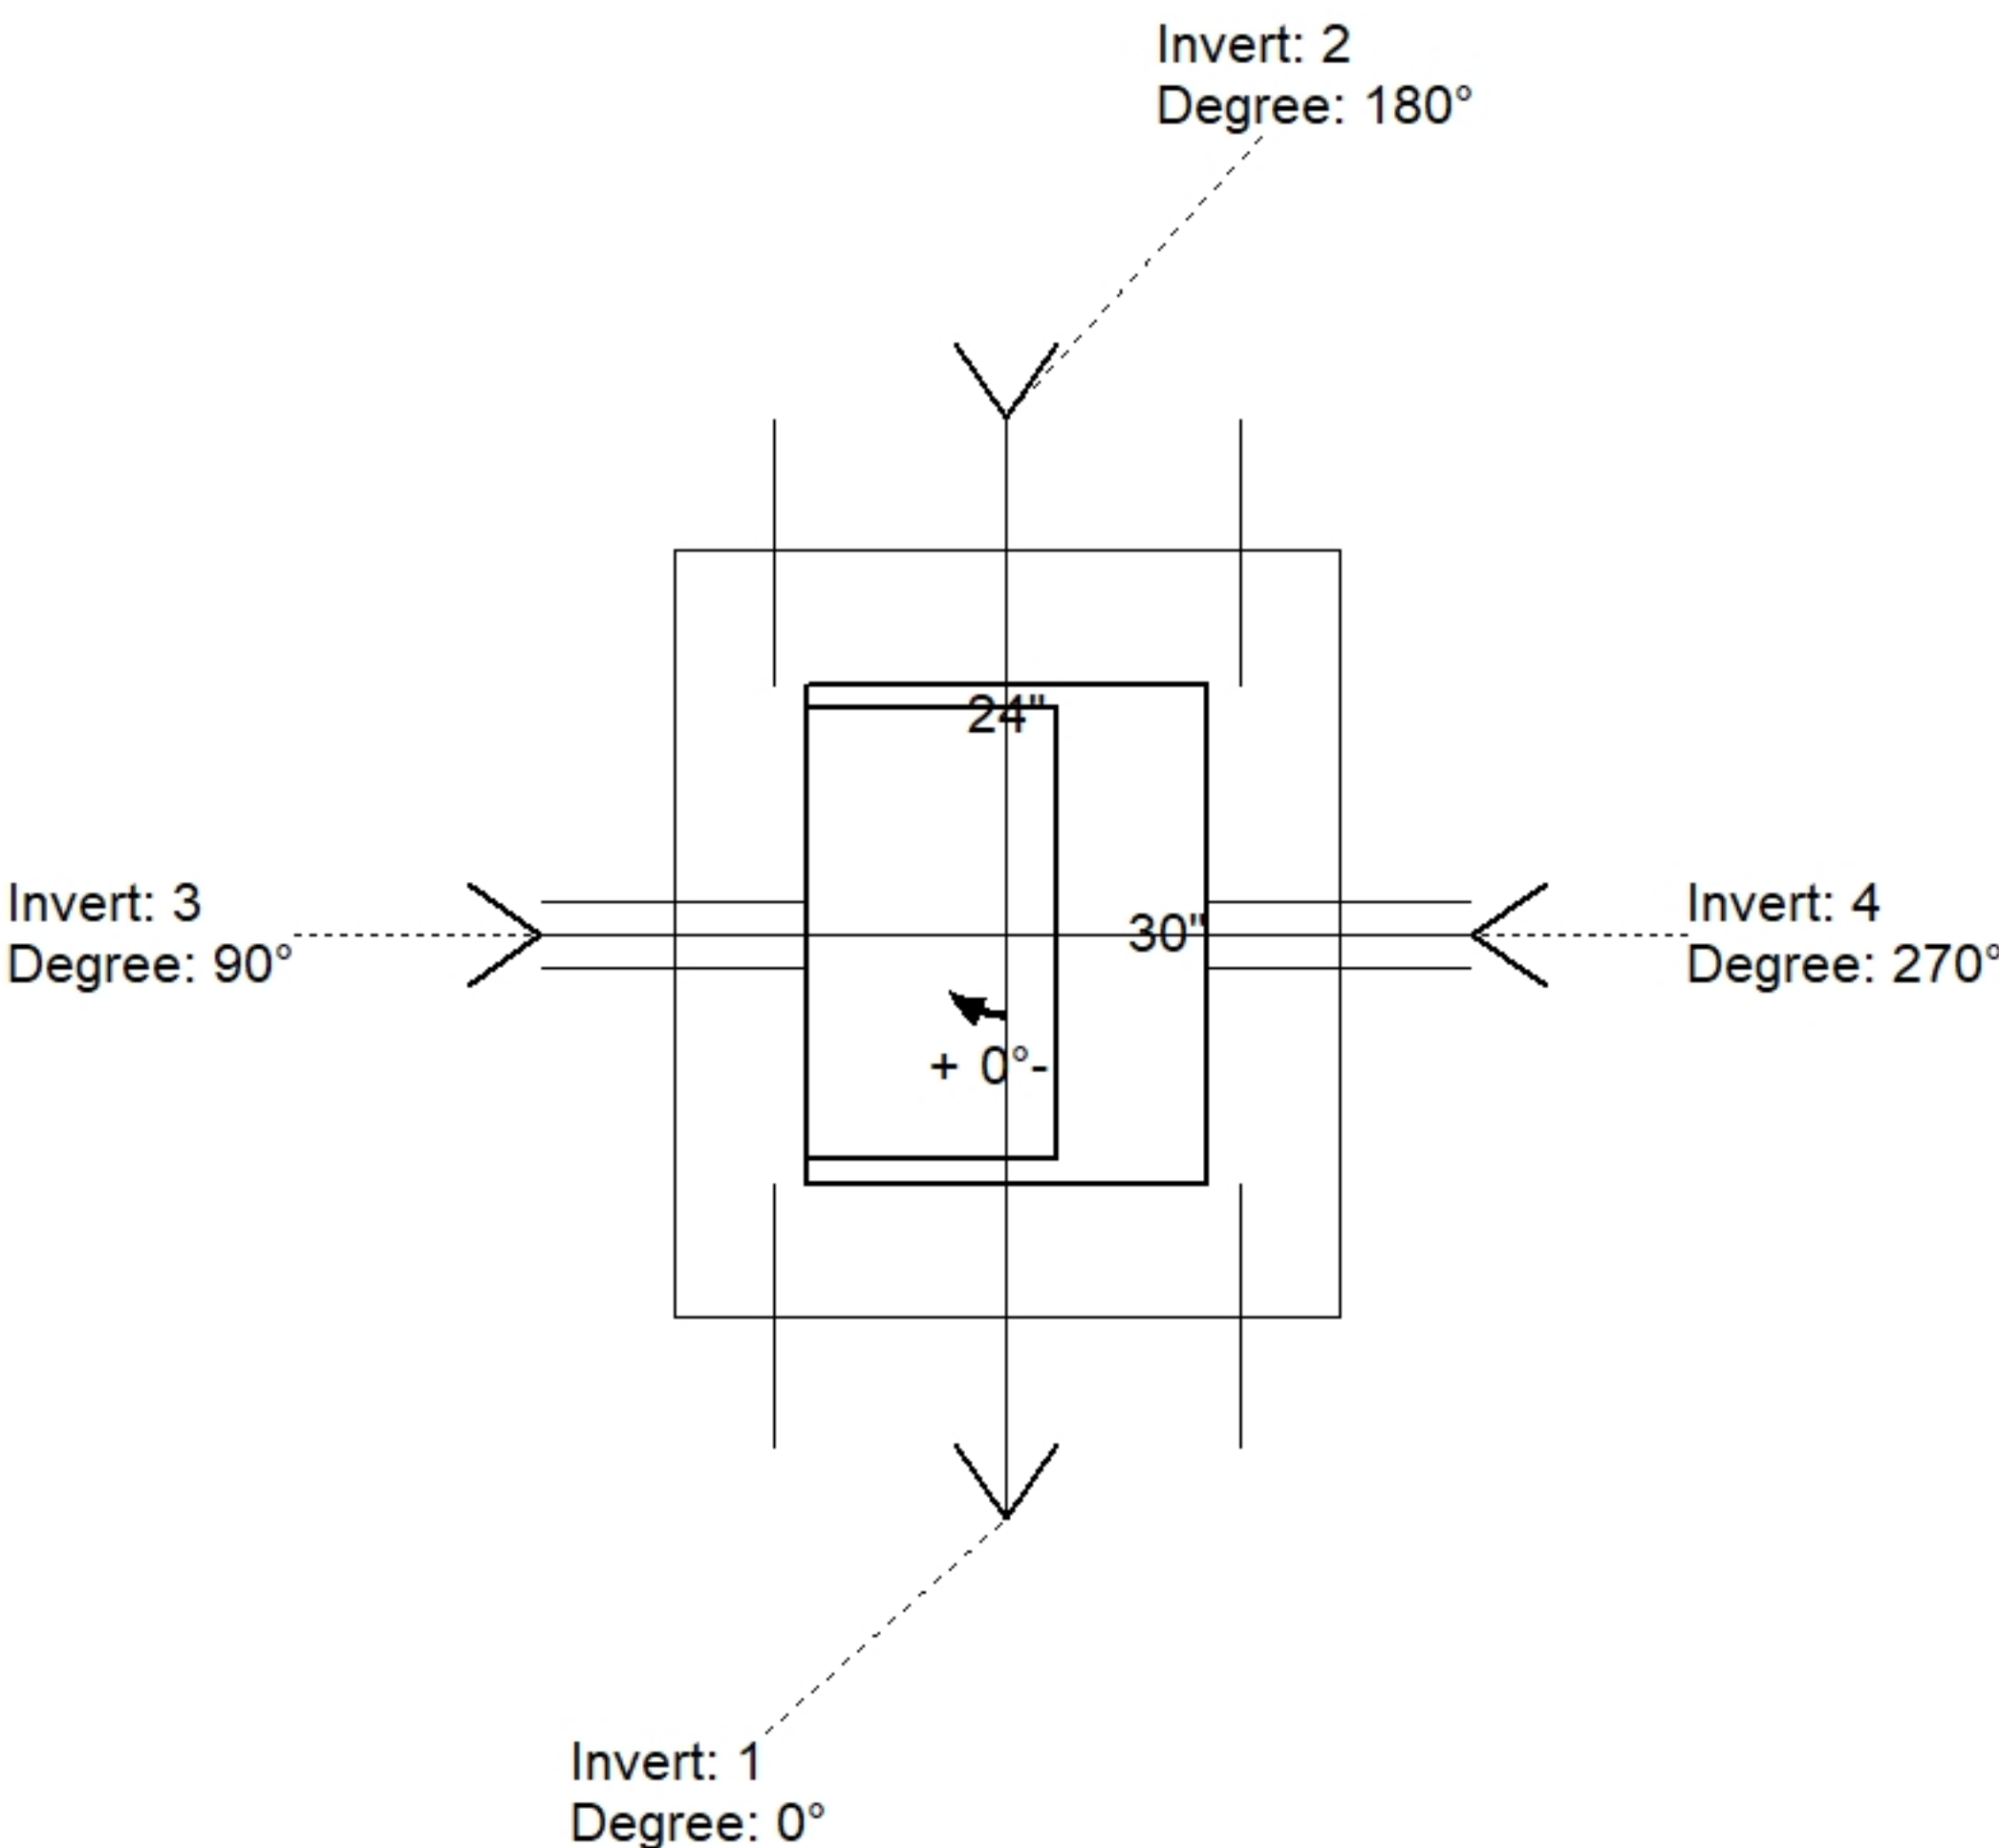

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	801.04'							
Reducer								
Invert 1	795.48'	0°	24" CMP	25"	28"	Hole 28	-2"	P1
Invert 2	795.48'	180°	24" CMP	25"	28"	Hole 28	-2"	P1
Invert 3	798.81'	90°	4" WEEP HOLE	4"	4"	Hole 4	39.96"	P1
Invert 4	798.81'	270°	4" WEEP HOLE	4"	4"	Hole 4	39.96"	P1
Invert 5								
Invert 6								
Invert 7								
Invert 8								

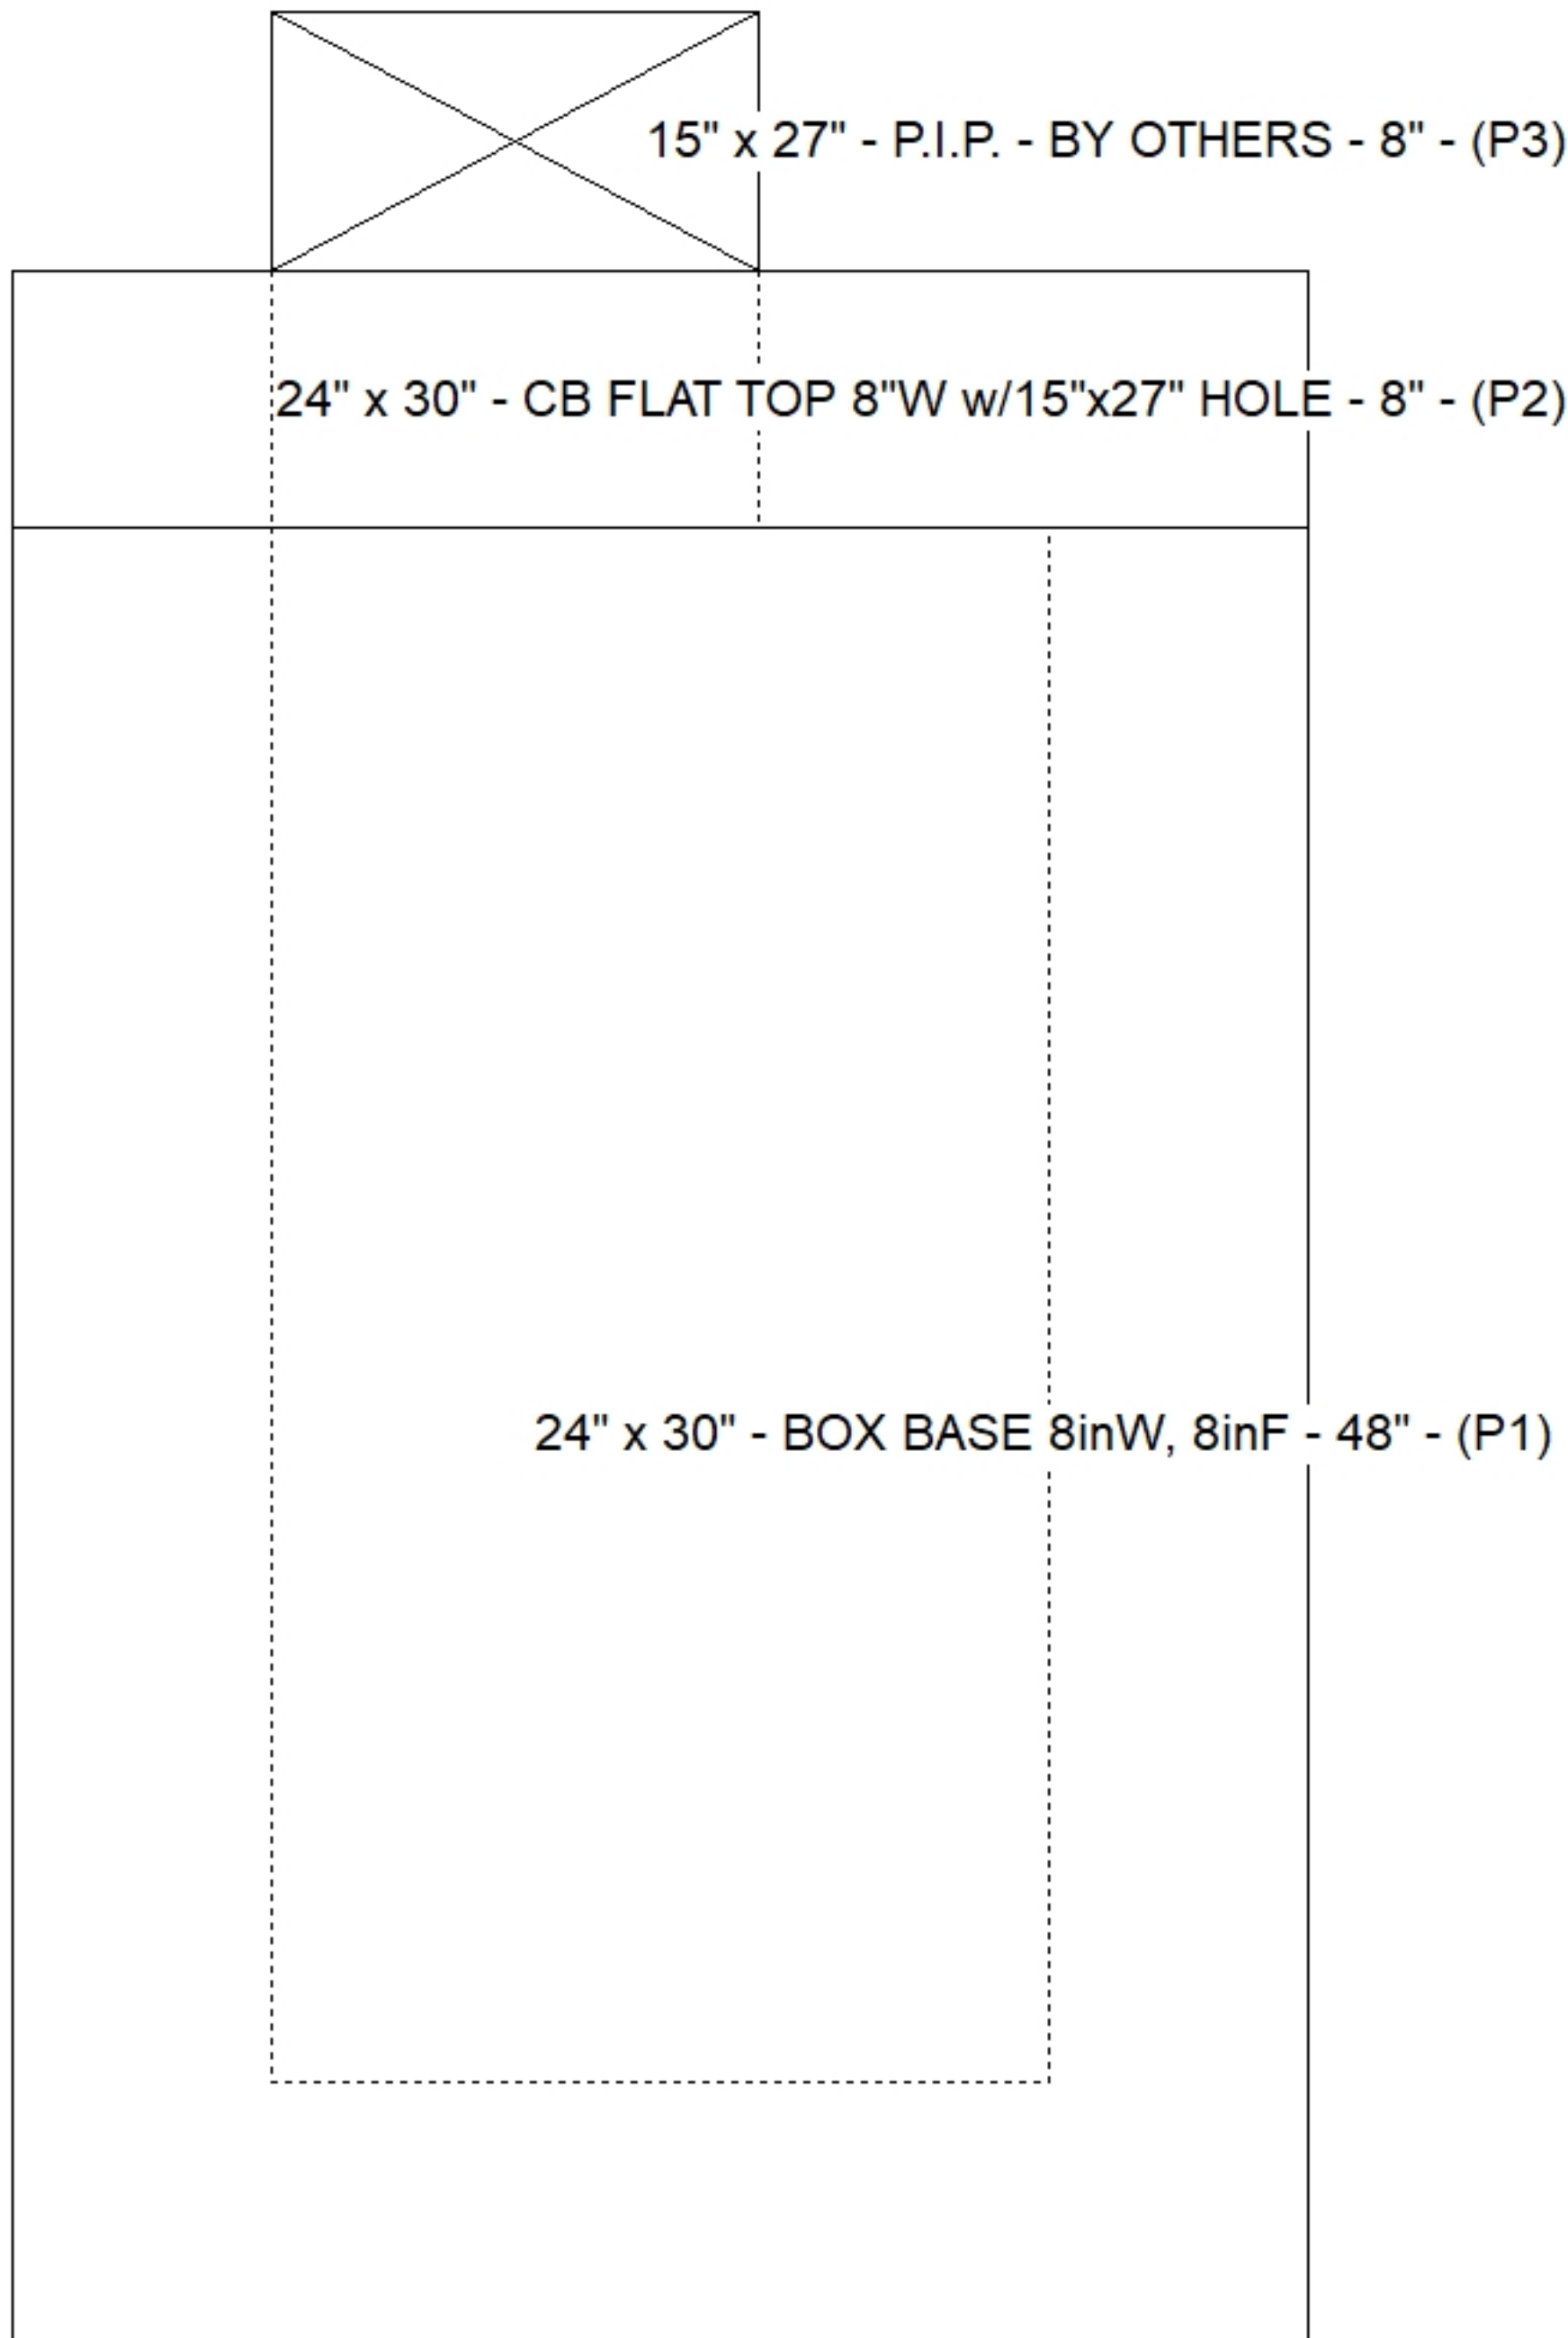

Default - Interior Dimensions

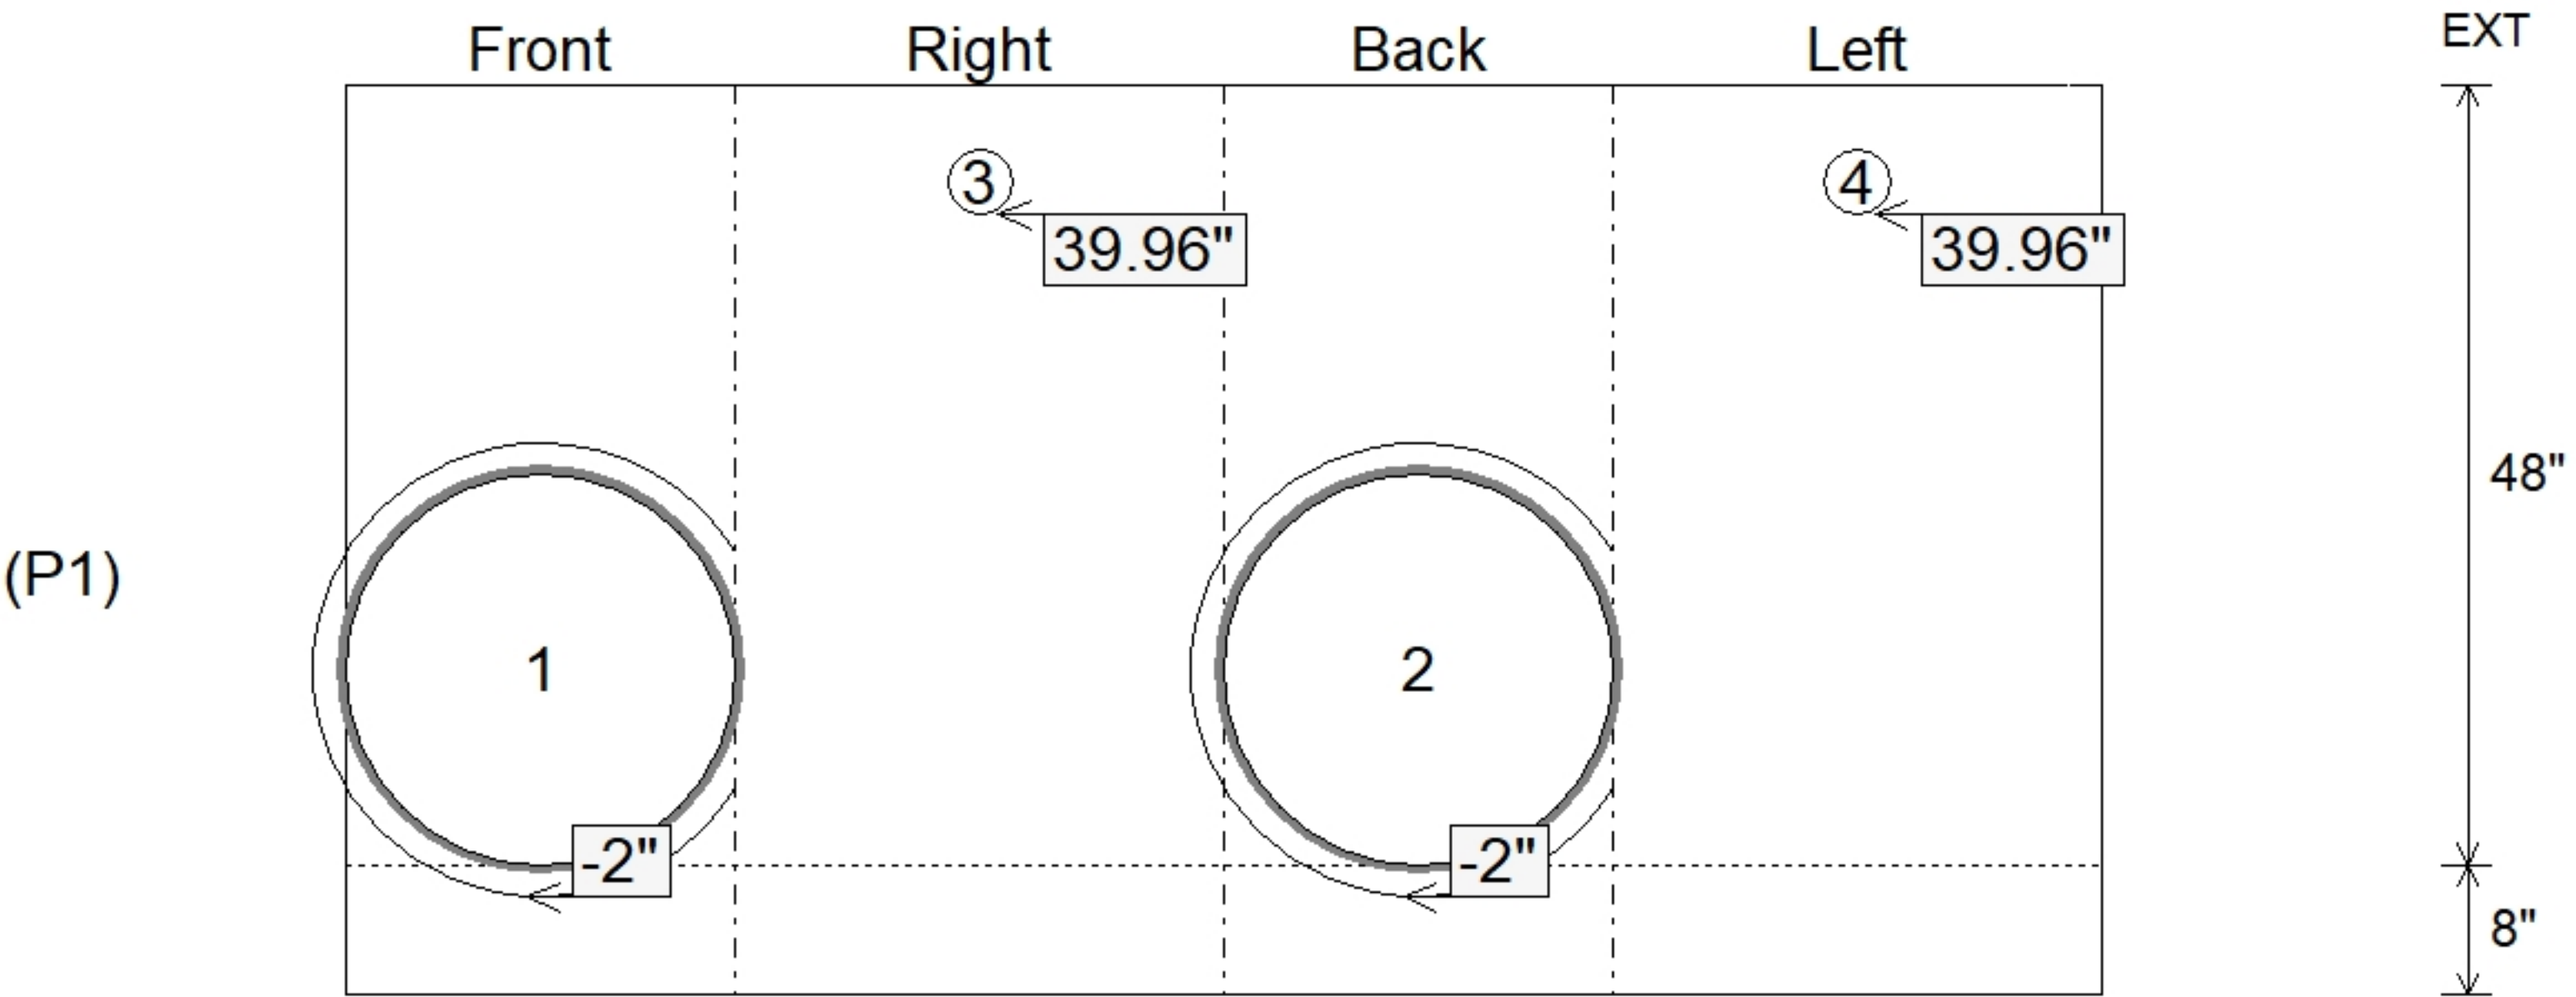

Submittal Drawing
8/17/2026 2:01:34 PM

SUBMITTAL
APPROVED BY:
