

Contractor: Cleary Construction, Inc.

TECH: Jared - F

Plant: 100



Size: 24" x 30"

Rim to Invert: 3.75'

Floor Height: 8"

Slack: 0.25"

****KYTC STATE PROJECT****

1. KYTC DBI TYPE 11 / ASTM C-913 SPEC'S.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. CASTING SUPPLIED BY OTHERS (HOE KY-460-11 F/G (DBI 11)).

REINFORCING PER ASTM A615 (GRADE 60).

- WALLS (As .31) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

STRUCTURE SUMMARY:


P2) 24" x 30" - CASTING HEIGHT - 3.75"

P1) 24" x 30" - BOX BASE 8inW, 8inF, Variable Ht - 41"

- 1) 24" x 30" - Conseal CS-102 1.00"
1) Hole - 20

0 lb
4878 lb
0 lb
0 lb



Structure Total: 4878 lb

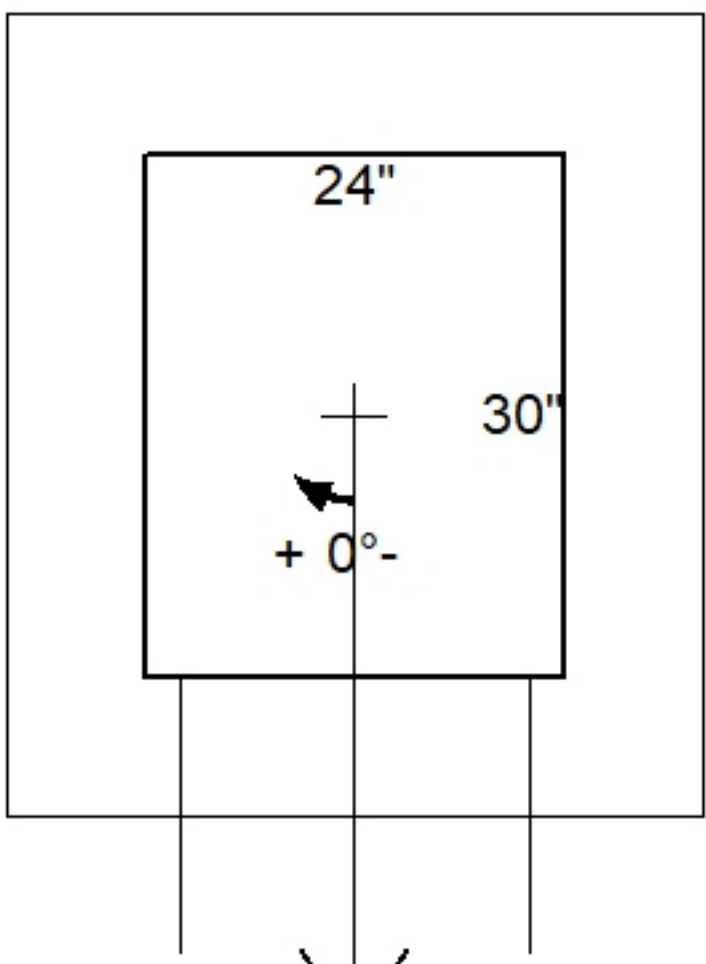

Invert: 1
Degree: 0°

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (⌵)	Ref
Rim	794.09'							
Reducer								
Invert 1	790.34'	0°	15" CMP	16"	20"	Hole 20	-2.5"	P1
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

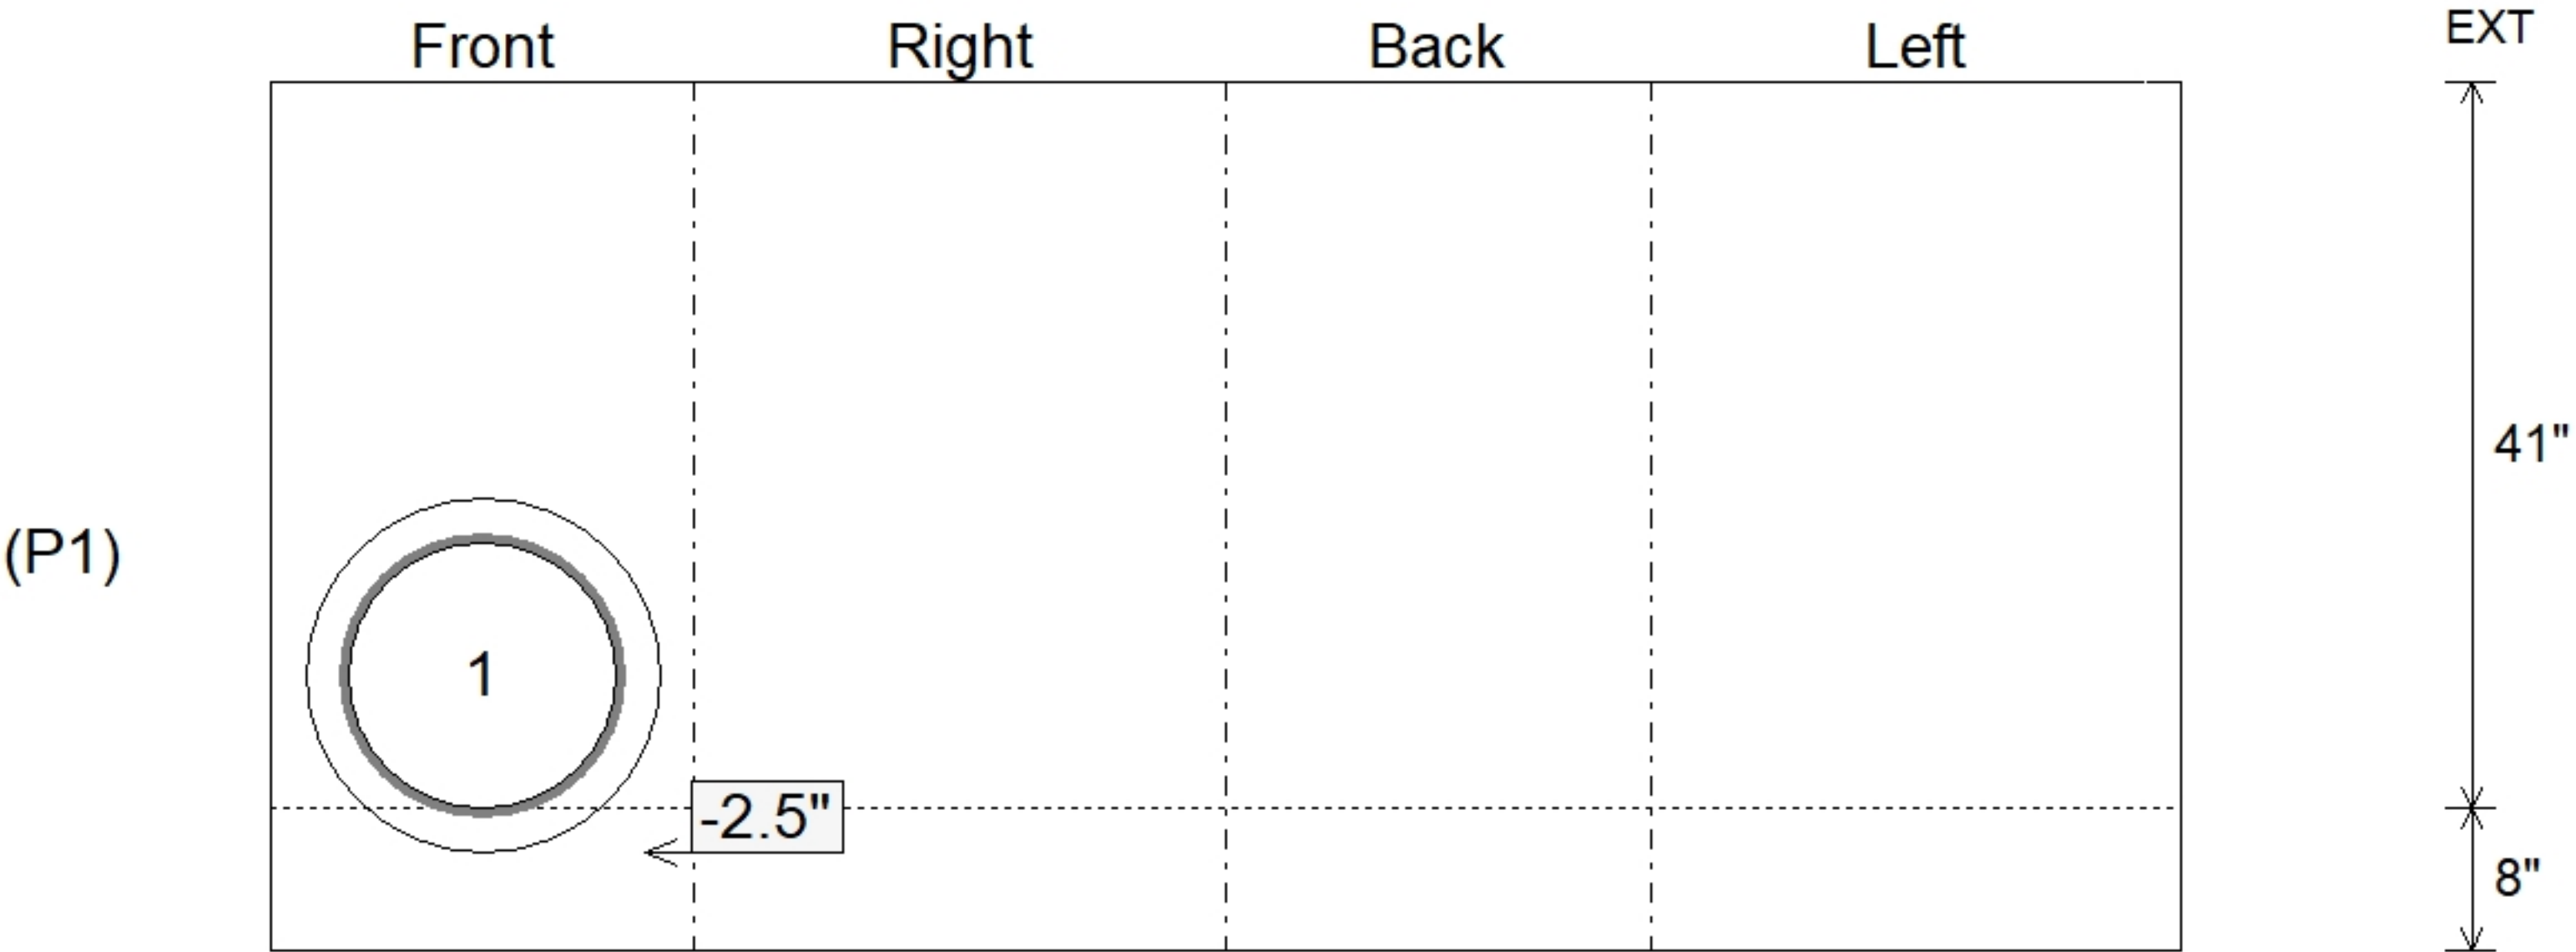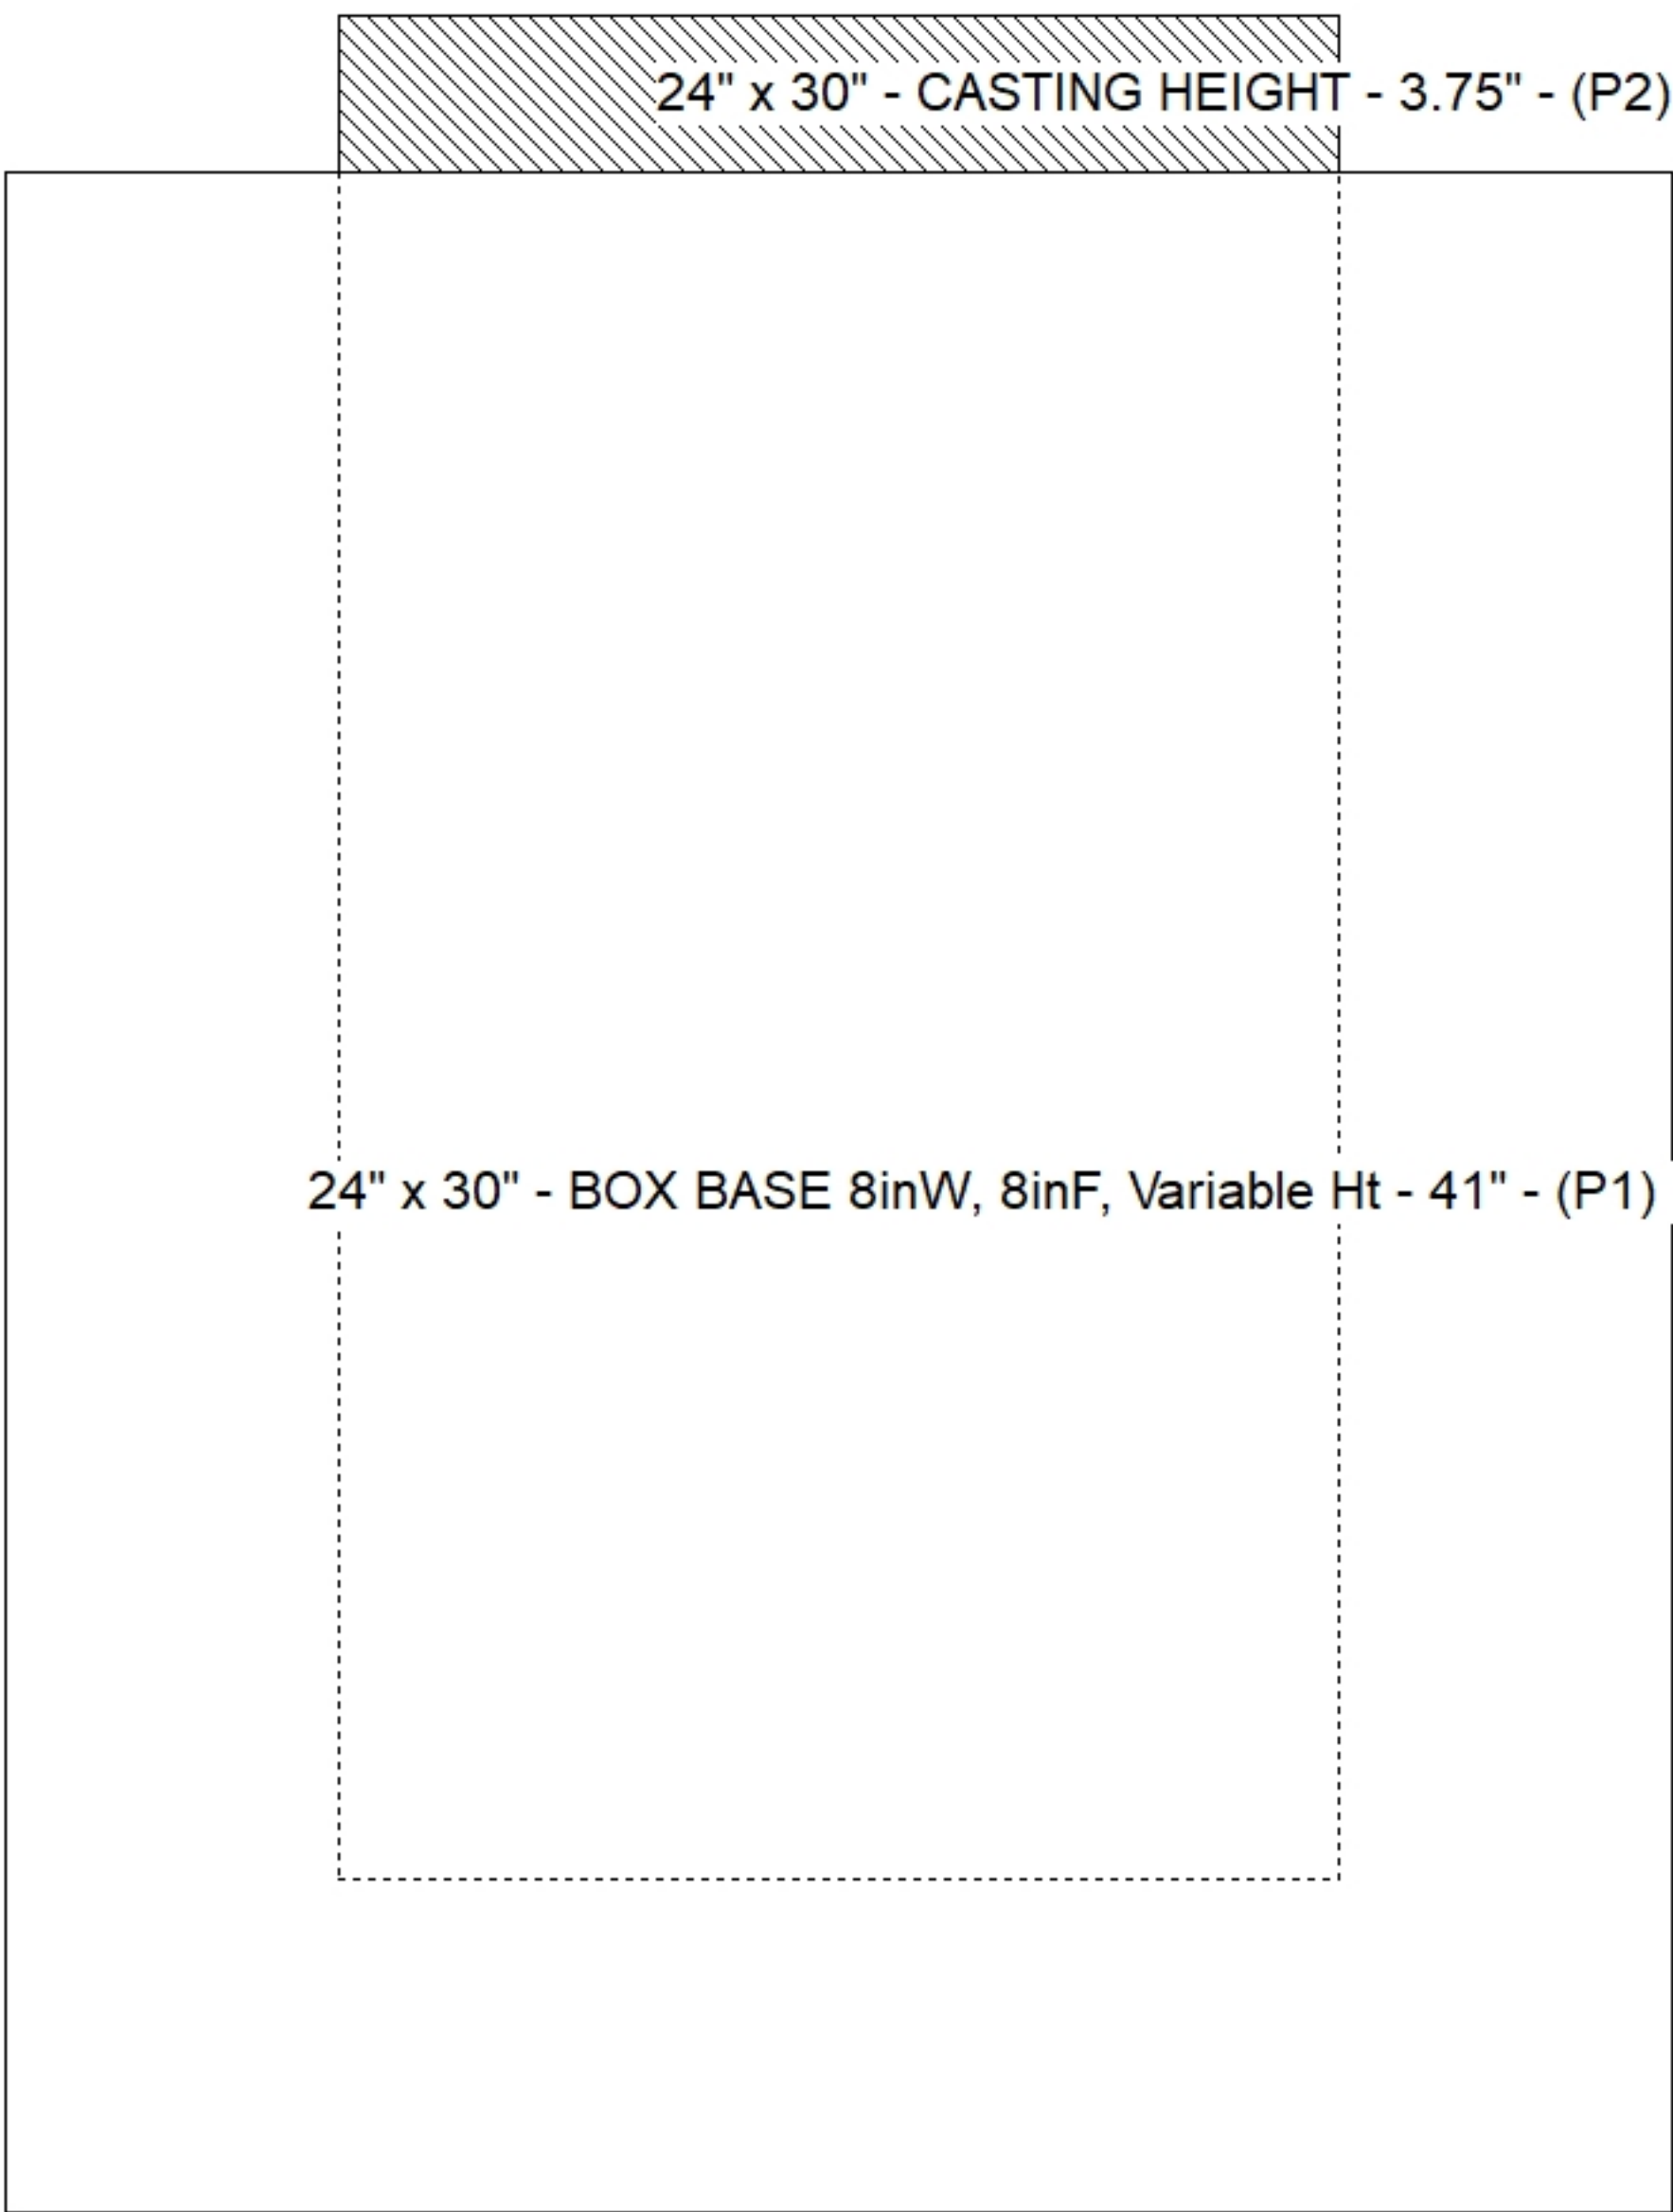

Submittal Drawing
8/17/2026 2:01:31 PM

SUBMITTAL
APPROVED BY:
