

Job Name: 26-1651B Buffalo Trace
Job Location: Campbellsville, KY
Contractor: Buzick Construction

Plant: Beaver Dam
6/26/2026 2:23:09 PM

Tech: S. Felletter
PC: E. Bradley



Structure ID: CB 816.09

P2 MH048LD12S


MH FLAT TOP w/34"x34" Hole F/G

- P3) 34" x 34" - CASTING HEIGHT - 3"
P2) 48" - MH FLAT TOP w/34"x34" Hole F/G - 12"
P1) 48" - MH BASE Custom Ht T/n - 27"
1) CASTING - HOE 595 F/G
1) 48" - Conseal CS-102 1.00"
1) Hole - 18
1) Hole - 12
2) MH Step ML-10-TDS-NCR - 10"

0 lb
1194 lb
3060 lb
376 lb
0 lb
0 lb
0 lb
0 lb
0 lb
Structure Total: 4630 lb


Structure Notes:
1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. CASTING BY ICAST (HOE 595 F/C).

REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

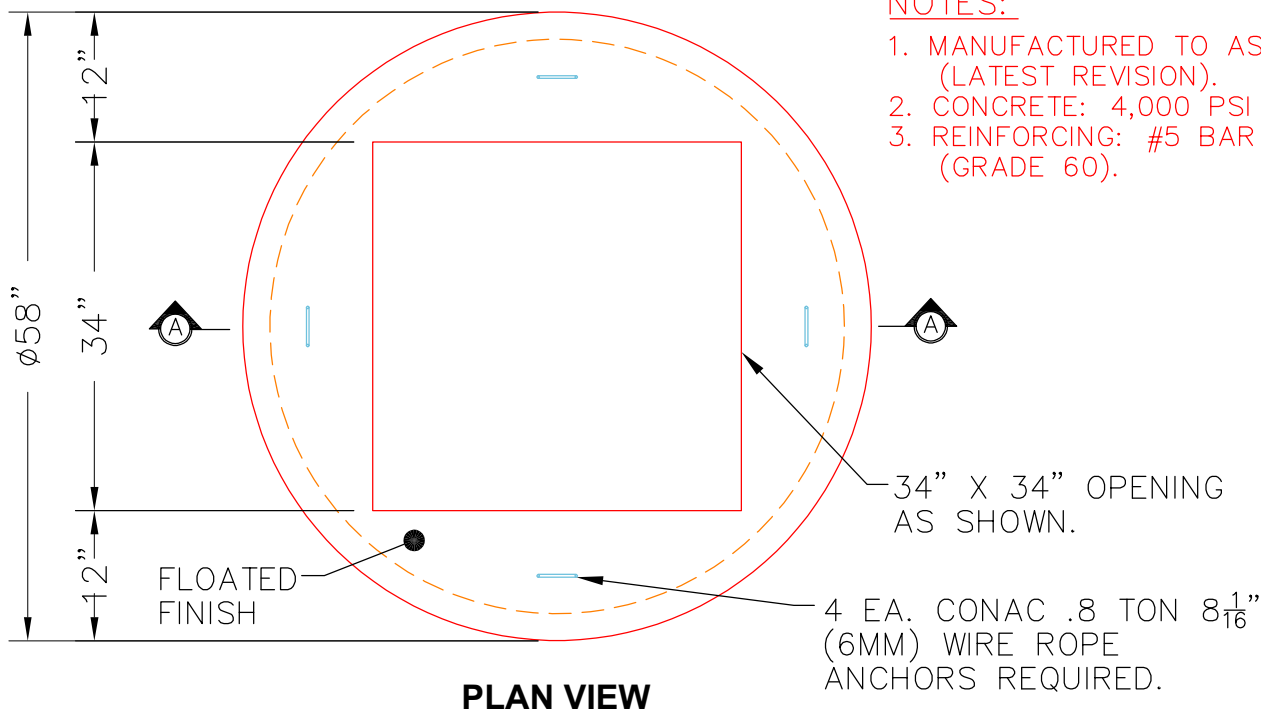

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: #5 BAR @ 6" C.C. E.W. (GRADE 60).

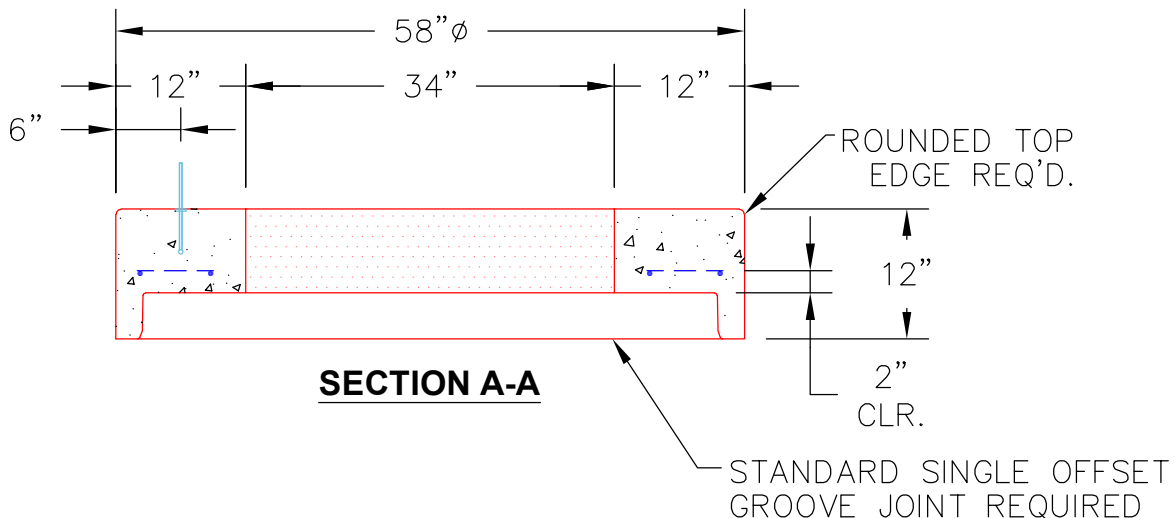

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 5"

Height (Ext): 12"

Weight (Net): 1194 lb
Volume (Net): 0.3cu.yd
