

Contractor: Weddle Enterprises, Inc

TECH: Jared - F

Plant: 100



Size: 48"

Rim to Invert: 3.6'

Floor Height: 6"

Slack: 0.2"

1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. NO INVERT CHANNEL.
4. CASTING SUPPLIED BY OTHERS.

REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .18)
- FLOOR (As .37) #5 BARS AT 10" C.C.E.W.

STRUCTURE SUMMARY:

0 lb

1700 lb

3146 lb

0 lb


0 lb

0 | b

0 | b



0 lb

Structure Total: 4846 lb

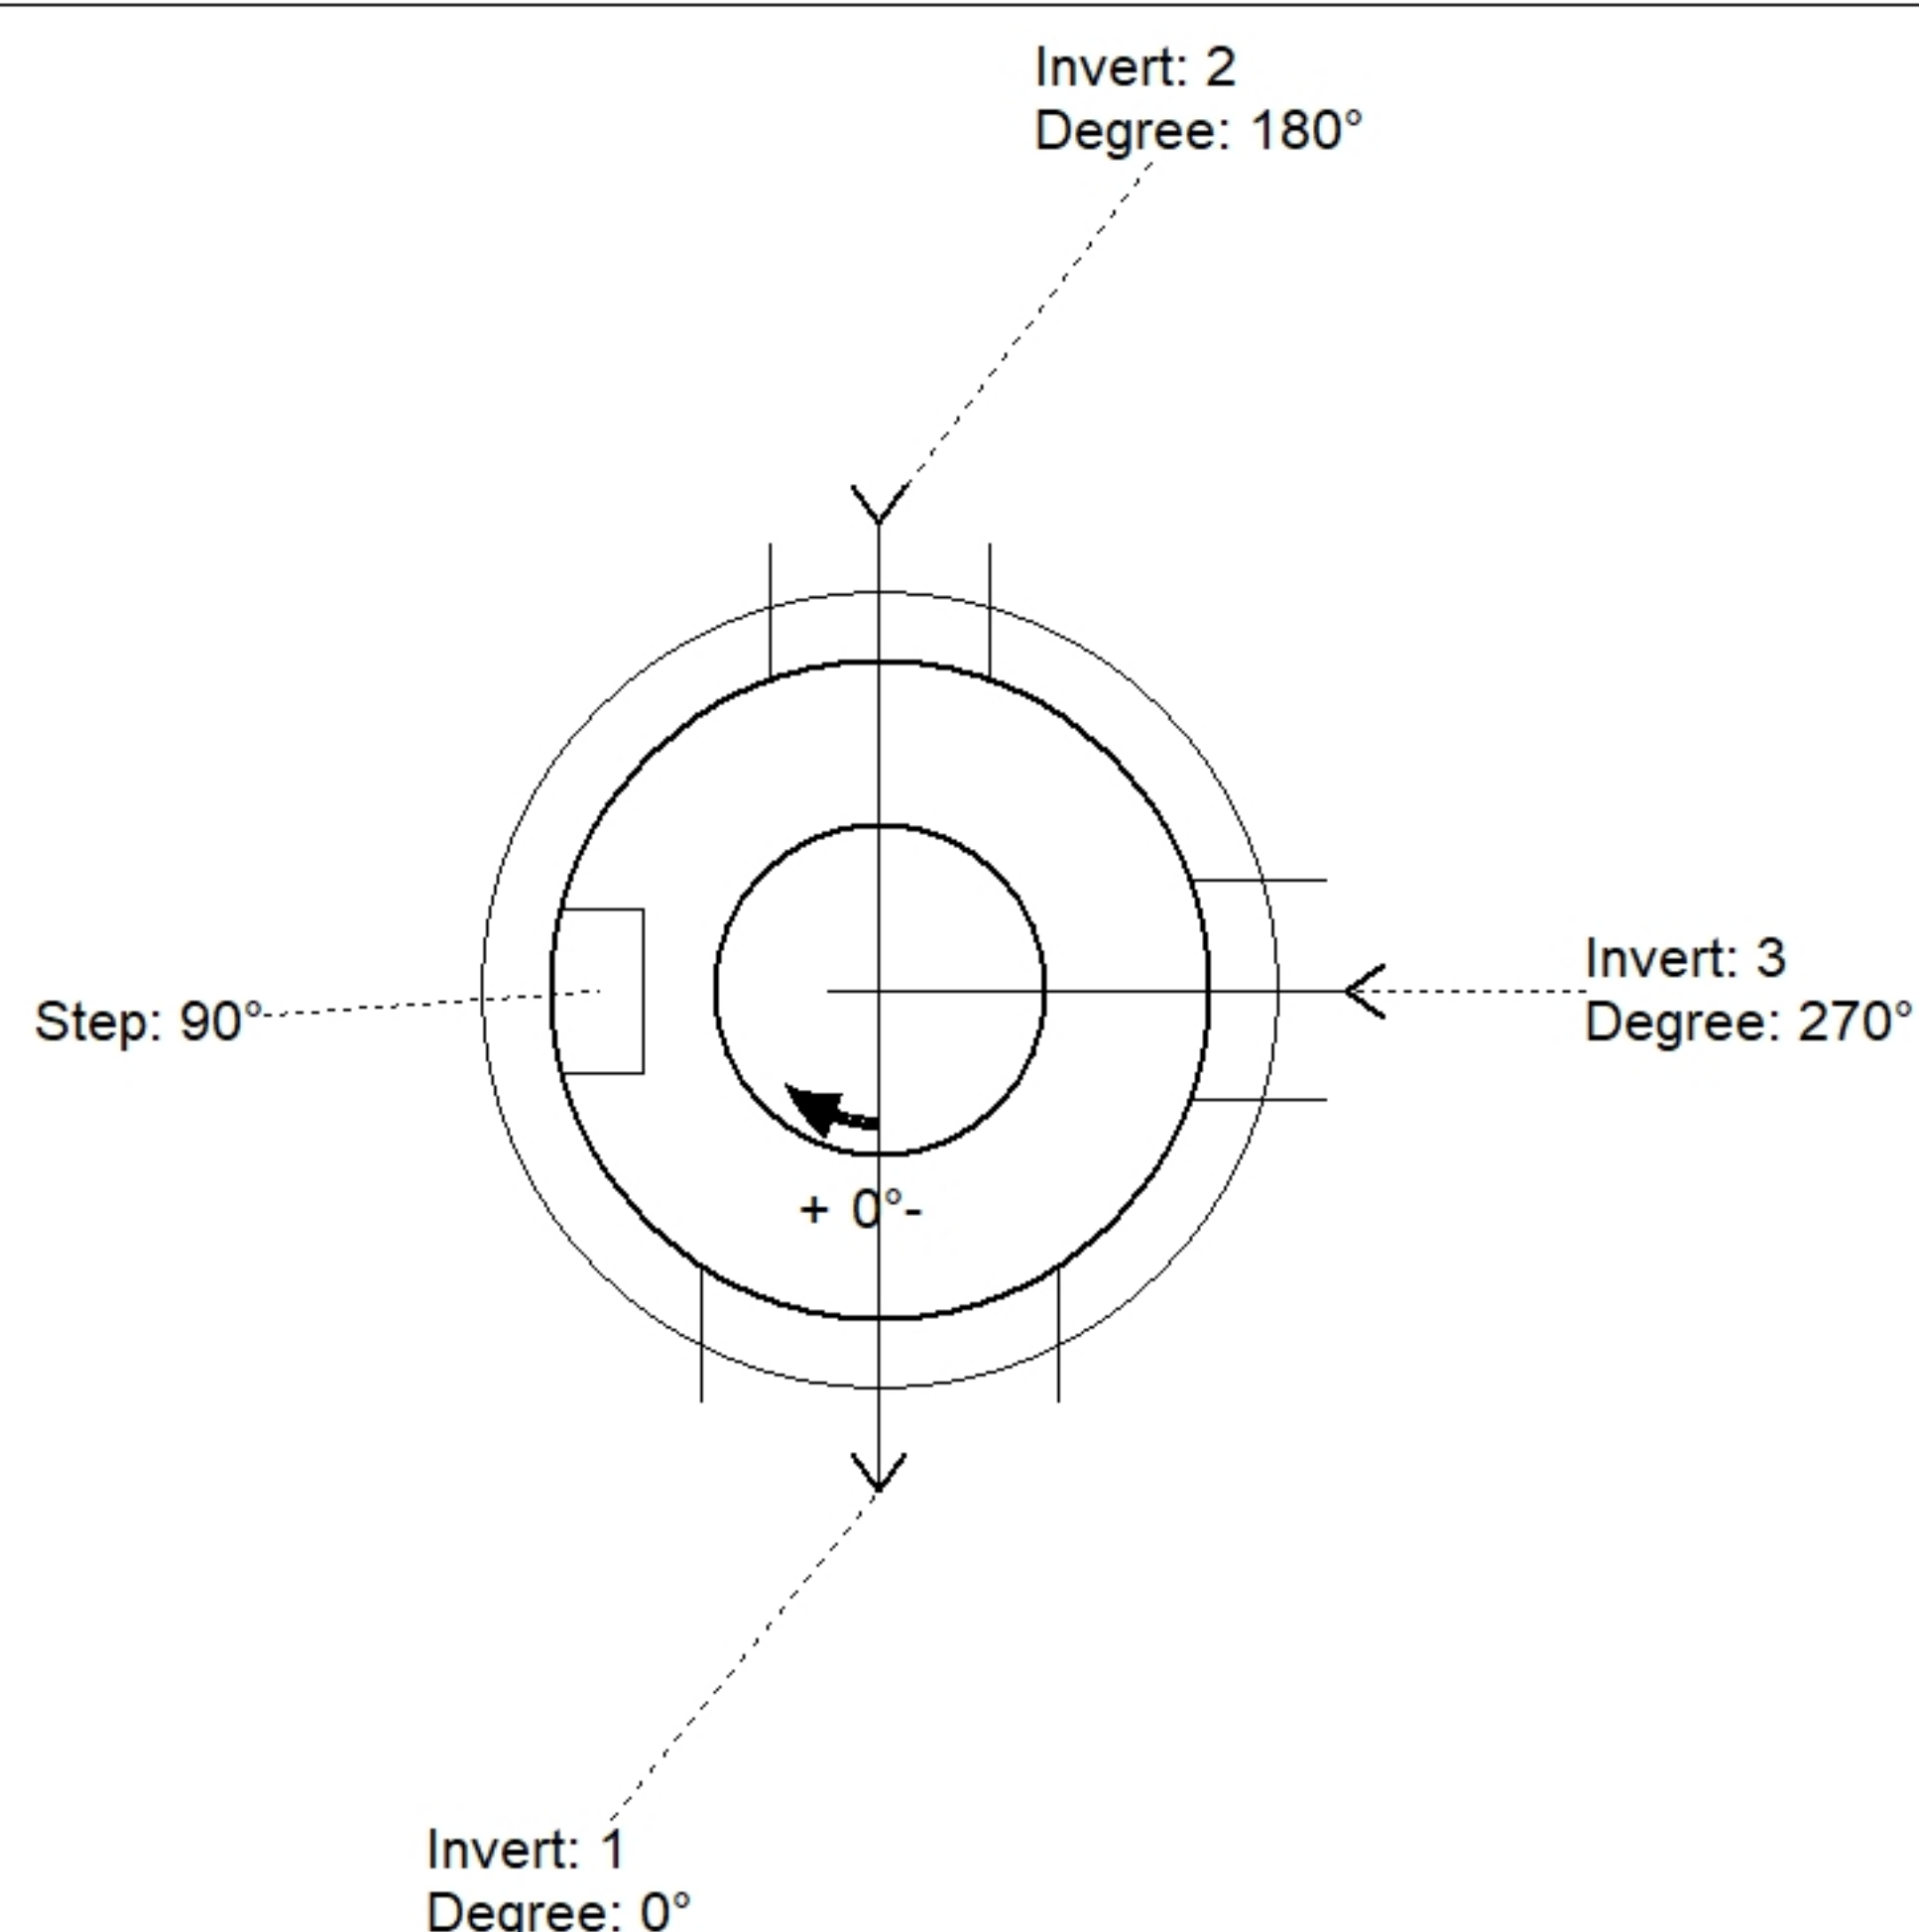

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	1076'							
Reducer								
Invert 1	1072.4'	0°	18" RCP B WALL	23"	26"	Hole 26	-2.5"	P1
Invert 2	1072.9'	180°	12" HDPE	14.5"	16"	Hole 16	4.75"	P1
Invert 3	1073.8'	270°	12" HDPE	14.5"	16" x 16"	DOGHOUSE INVRTD 16"x16"	15.55"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

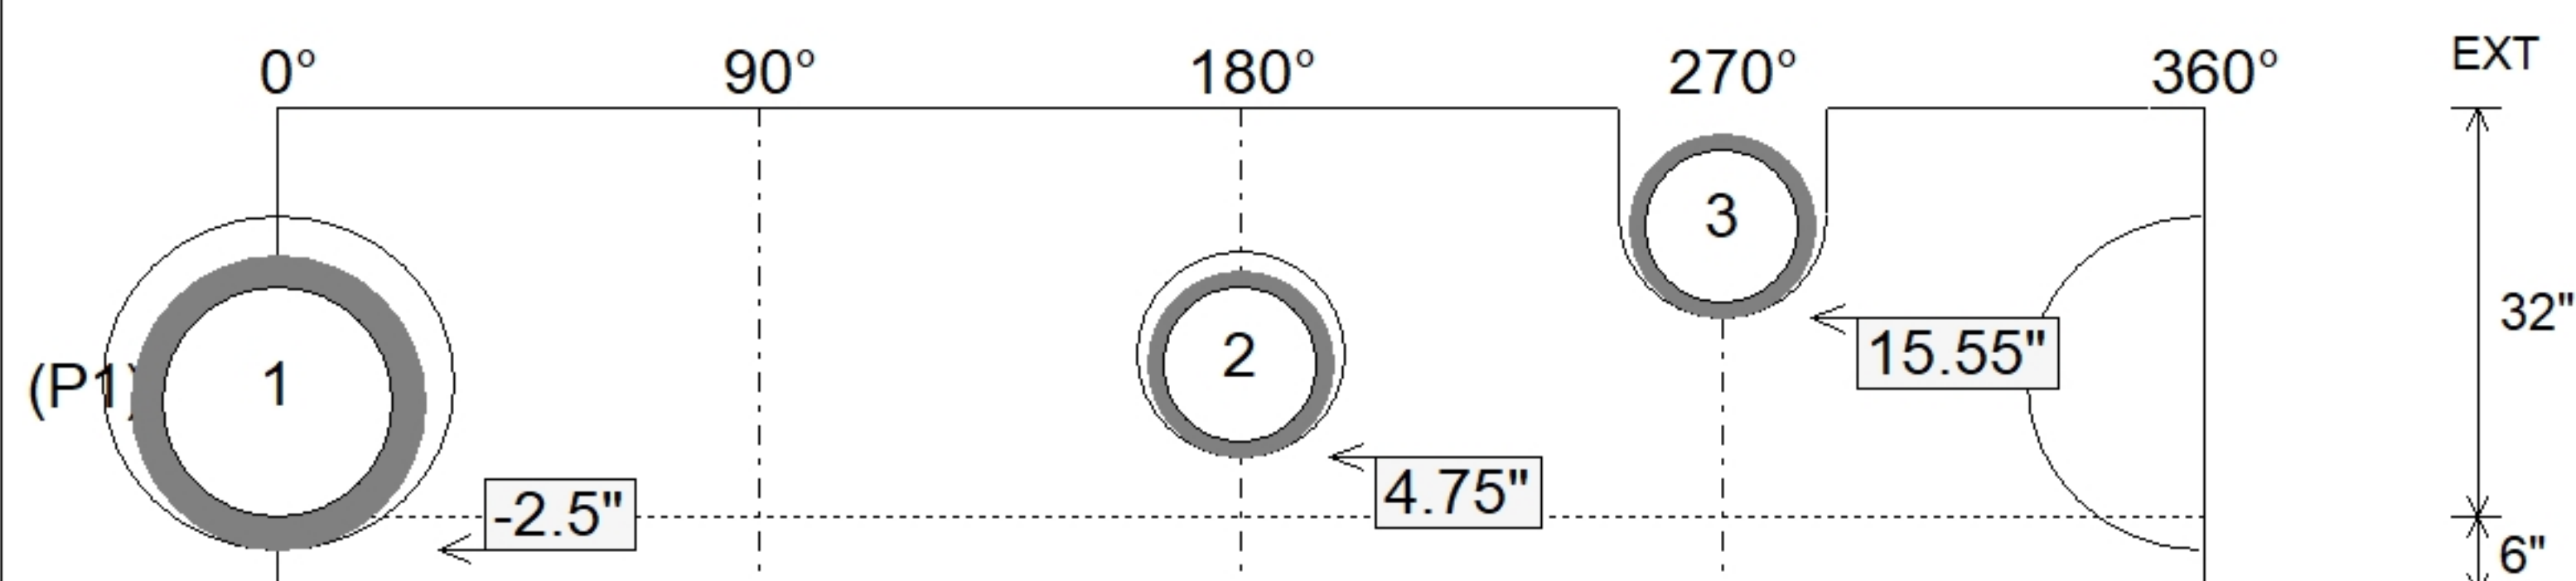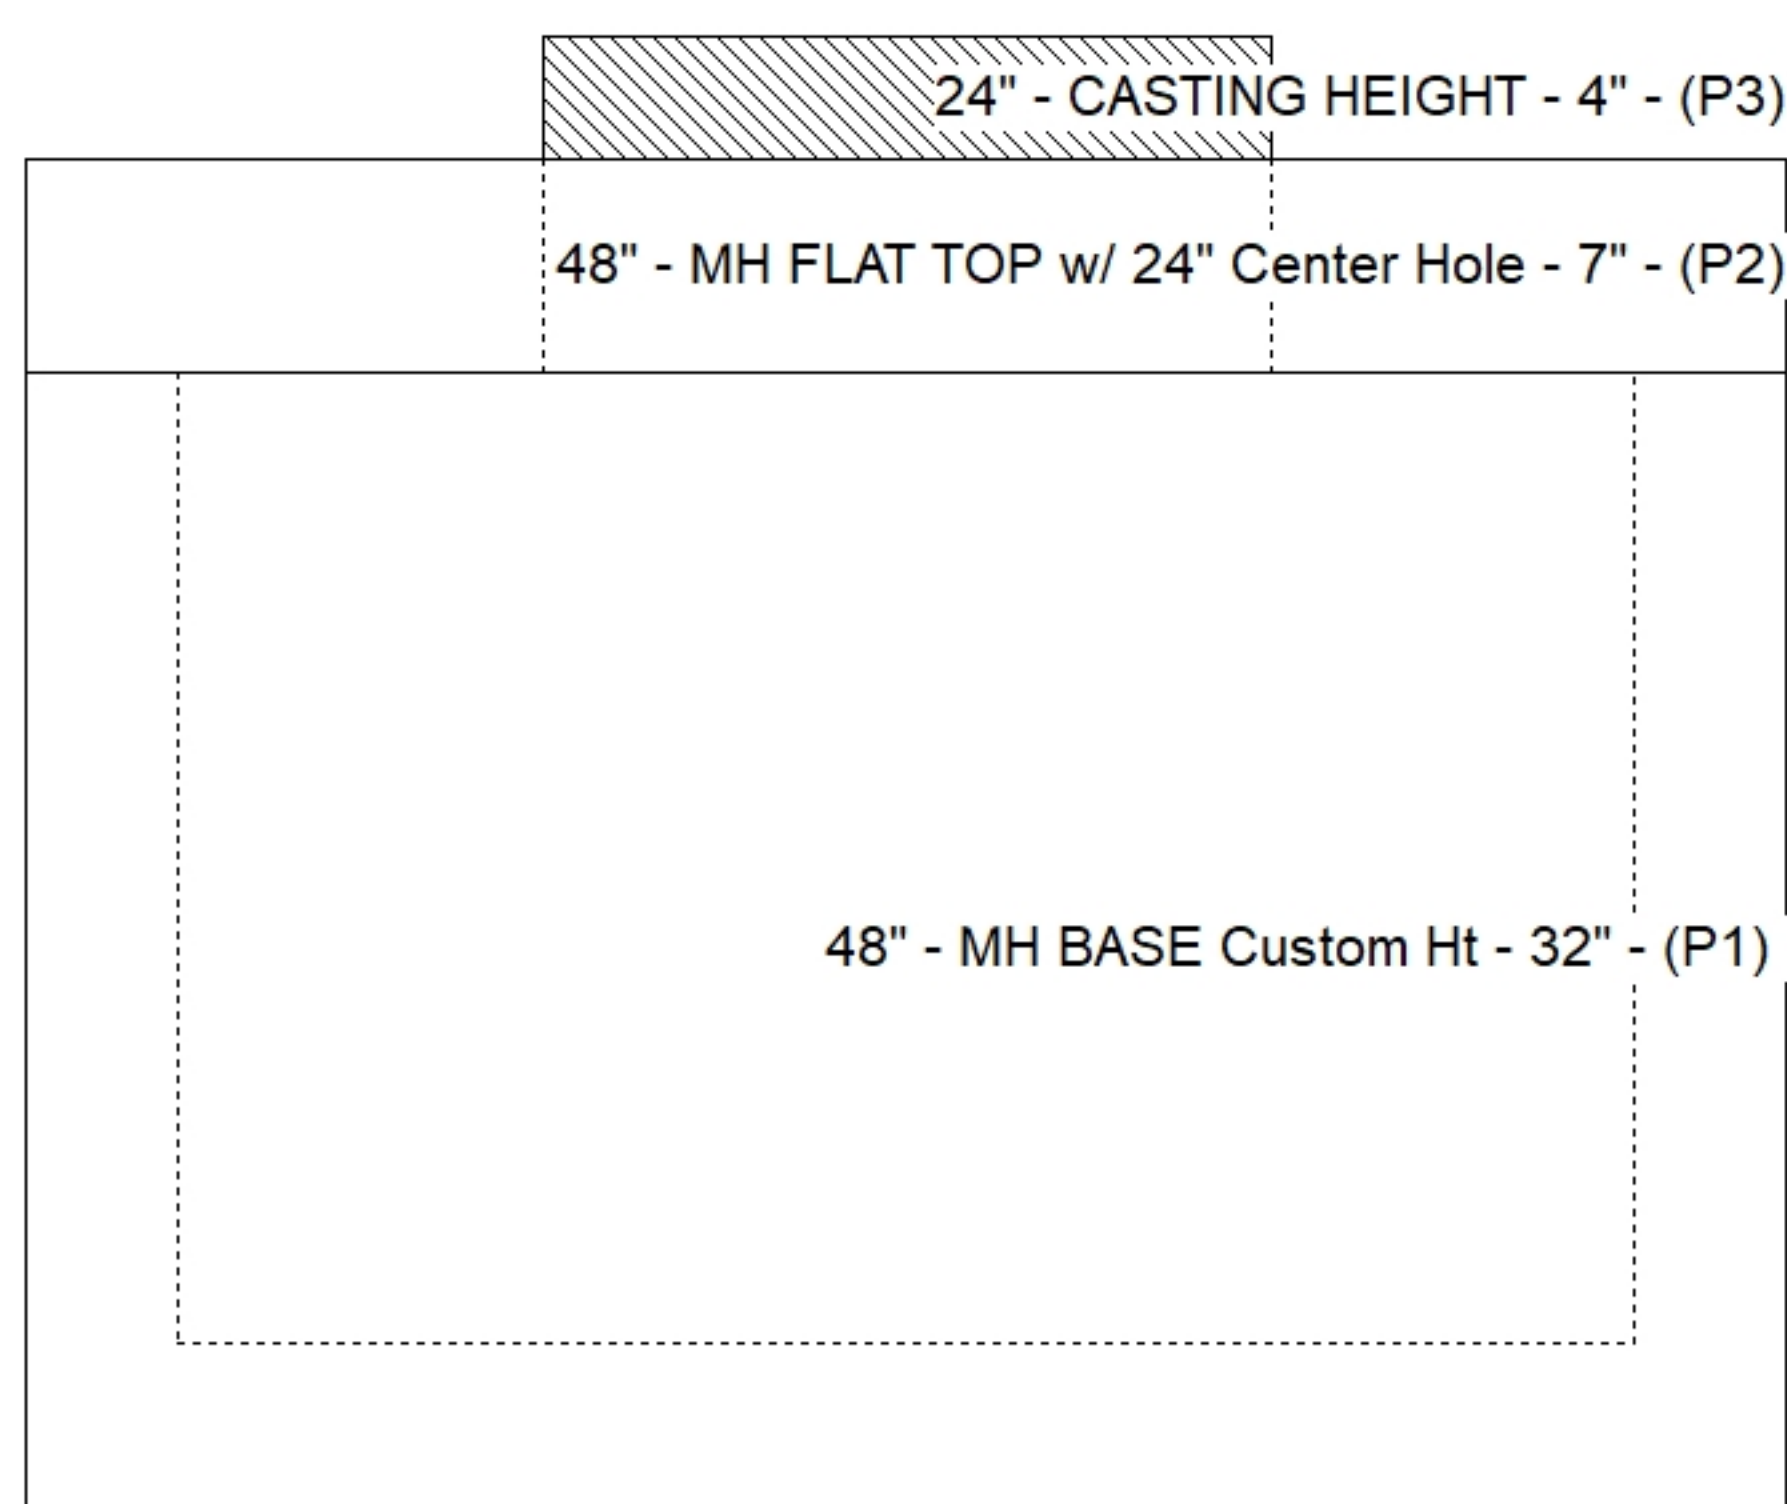

Submittal Drawing
7/21/2026 7:34:20 AM

SUBMITTAL
APPROVED BY:
