



Job Name: 26-1735 - City Of Clarksville Vaults Job Location: Clarksville, TN Contractor: Clarksville Gas and Water					Plant: 100 8/11/2026 6:30:52 PM		Tech: Jared - F PC: A. Chambers				
Structure ID: QL3											
P2 BX048096-08W-RSVF BOX RISER 8inW, Variable Ht F/F											
P4) 36" x 72" - HATCH (CAST FLUSH) - 3.5" P3) 48" x 96" - CB FLAT TOP 8"W w/36"x72" HATCH F/F - 8" P2) 48" x 96" - BOX RISER 8inW, Variable Ht F/F - 64" P1) 48" x 96" - P.I.P. BY OTHERS - BTM SLAB F/n - 0" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 2) 48" x 96" - Conseal CS-102 1.00" (Double) 1) 36" x 72" - Conseal CS-102 1.00" (Double) 2) DOGHOUSE - 16"x36"						100 lb 3072 lb 13058 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb		Structure Notes: 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. HATCH SUPPLIED BY OTHERS (HALLIDAY H1R 36"x72"). REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB(As.12) #5 BARS AT 6" C.C.E.W. - WALLS(As.12) #5 BARS AT 8" C.C.E.W.			
Structure Total: 16230 lb											
Rim: 6' Rim to Invert: 6' Slack: 0" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	0'	0°	32"	0" No Hole	0.01"	DOGHOUSE 16"x36"	16" x 36"	16"	0"	0"	
Invert 2	0'	180°	32"	0" No Hole	0.01"	DOGHOUSE 16"x36"	16" x 36"	16"	0"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

RIGHT-SIDE UP VIEW (int. dimensions)

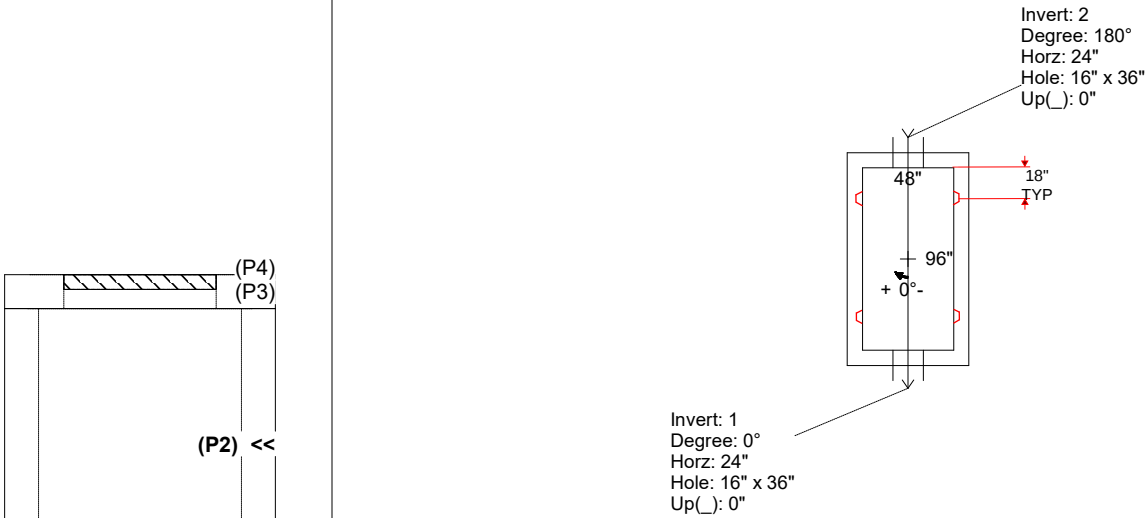

INSIDE WALL DIMENSIONS

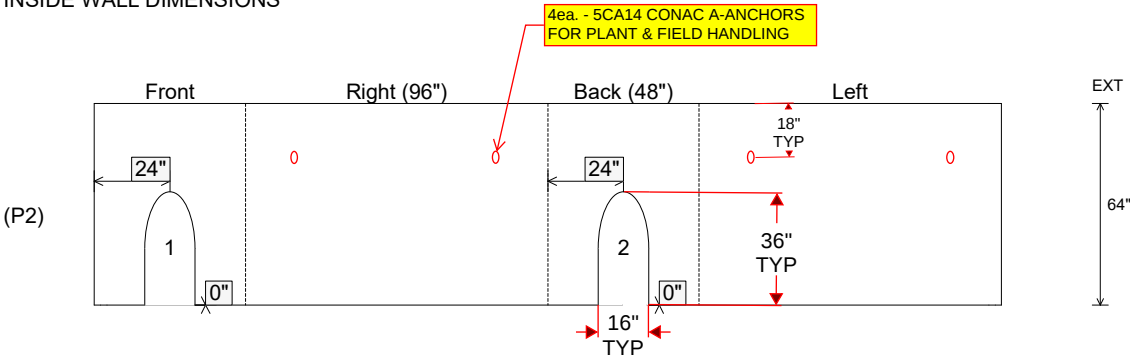

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Flat	Wall Thickness: 8" Floor Height: 0"	Height (Int): 64" Height (Ext): 64"	Weight (Net): 13058 lb Volume (Net): 3.34cu.yd
----------------------------------	--------------------------------	--	--	---
