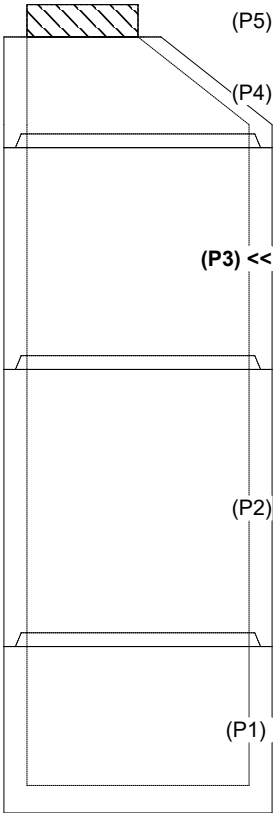

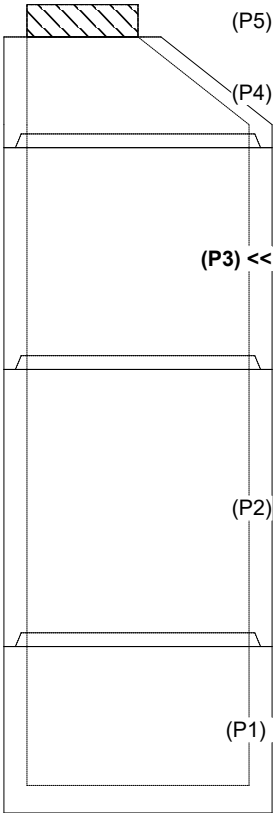
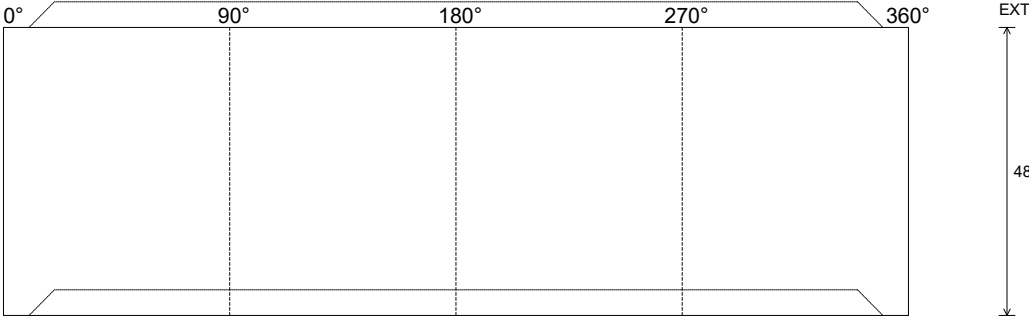


Job Name: 26-1822 - Project Versailles Job Location: Versailles, KY Contractor: KY Earthworks					Plant: 100 8/26/2026 3:49:26 PM		Tech: Jared - F PC: E. Bradley				
Structure ID: T1 SS-MH											
P3 MH048RS48S			MH RISER NO STEPS T/G								
P5) 24" - CASTING HEIGHT - 7" P4) 48" - ECC CONE w/ 24" HOLE NO STEP F/G - 24" P3) 48" - MH RISER NO STEPS T/G - 48" P2) 48" - MH RISER NO STEPS T/G - 60" P1) 48" - MH BASE NO STEP T/n - 30" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-375 F/C Sanitary 3) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) A-Lok - 0350						0 lb 1550 lb 3353 lb 4192 lb 3334 lb 0 lb 0 lb 1440 lb 271 lb 0 lb 0 lb 2 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS 4. CASTING BY ICAST (HOE MC-375 F/C SANITARY) . REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 935.33' Rim to Invert: 14.15' Slack: 2.8" Sump: 2" Step Position: 0°						Structure Total: 14142 lb					
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)											
											
INSIDE WALL DIMENSIONS											
											
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 5" Floor Height: 0"		Height (Int): 48" Height (Ext): 48"		Weight (Net): 3353 lb Volume (Net): 0.86cu.yd		
