



Job Name: 26-1822 - Project Versailles Job Location: Versailles, KY Contractor: KY Earthworks					Plant: 100 9/24/2026 11:31:42 AM		Tech: Jared - F PC: E. Bradley				
Structure ID: A6.3 ST-CI											
P1 MH048BAVF		MH BASE Custom Ht T/n									
P3) 24" x 36" - CASTING HEIGHT - 6" P2) 48" - MH FLAT TOP w/24"x36" Hole F/G - 12" P1) 48" - MH BASE Custom Ht T/n - 44" 1) CASTING - HOE 525 LV SET (F/G/H) 1) 48" - Conseal CS-102 1.00" 1) 24" x 36" - Conseal CS-102 1.00" 2) Hole - 30 1) Hole - 20 4) MH Step ML-10-TDS-NCR - 10"					0 lb 1300 lb 3637 lb 442 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 5379 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE 525 LV SET (F/G/H)) REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .18) - FLOOR (As .37) #5 BARS AT 10" C.C.E.W.				
Rim: 934.15' Rim to Invert: 5.1' Slack: 1.1' Sump: 1.9' Step Position: 90°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	929.05'	0°	0"	24" HDPE	27.8"	Hole 30	30"	32.406"	0"	0"	
Invert 2	930.55'	145°	73.375"	15" HDPE	17.6"	Hole 20	20"	20.629"	18.625"	0"	
Invert 3	929.05'	235°	119"	24" HDPE	27.8"	Hole 30	30"	32.406"	0"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											


RIGHT-SIDE UP VIEW (int. dimensions)

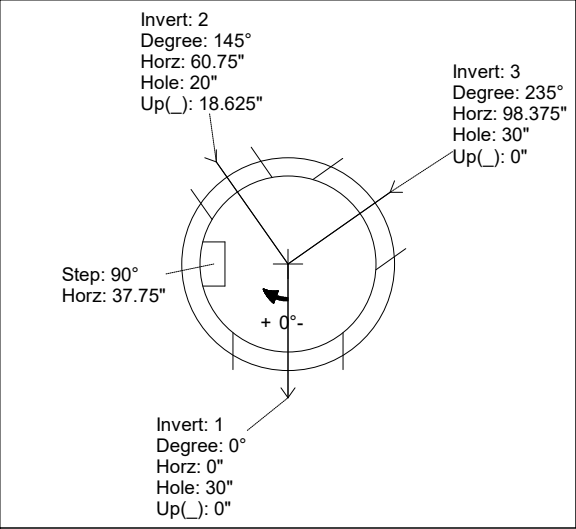

UPSIDE-DOWN VIEW (int. dimensions)

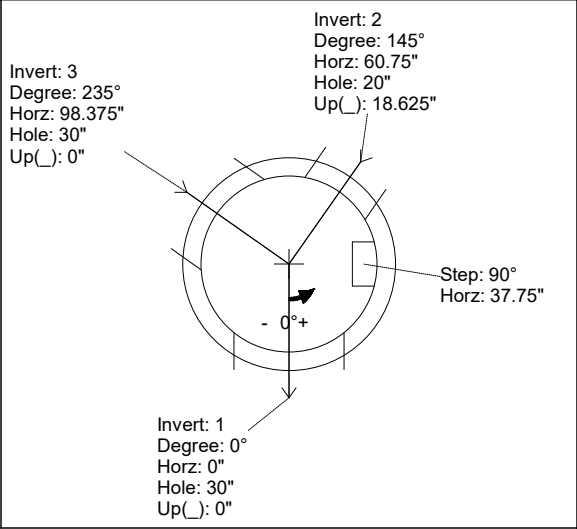

INSIDE WALL DIMENSIONS

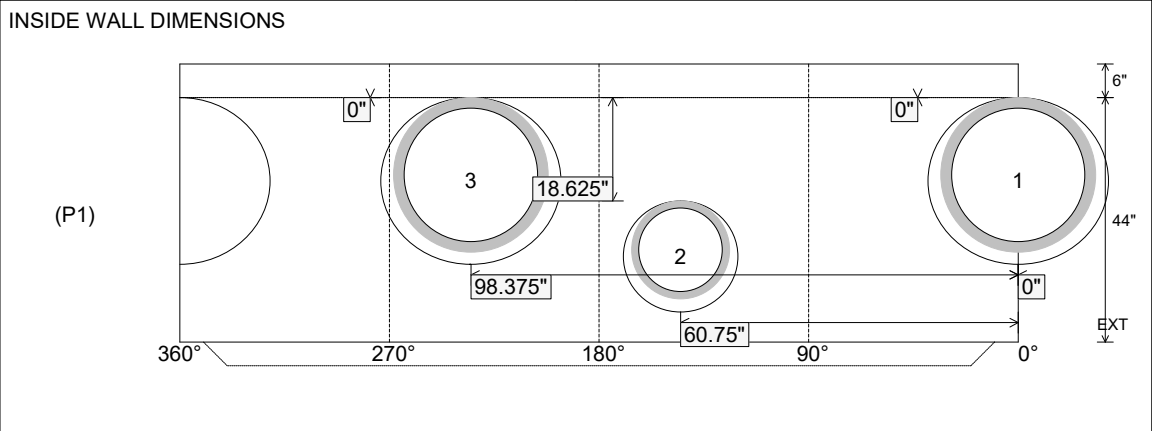

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 44" Height (Ext): 50"	Weight (Net): 3637 lb Volume (Net): 0.93cu.yd
----------------------------------	---------------------------------	--	--	--
