




Job Name: 26-1822 - Project Versailles Job Location: Versailles, KY Contractor: KY Earthworks					Plant: 100 9/24/2026 11:31:23 AM		Tech: Jared - F PC: E. Bradley			
Structure ID: D10 ST-CI										
P1 MH048BAVF		MH BASE Custom Ht F/n								
P3) 24" x 36" - CASTING HEIGHT - 6" P2) 48" - MH FLAT TOP w/24"x36" Hole F/F - 7" P1) 48" - MH BASE Custom Ht F/n - 28" 1) CASTING - HOE 525 LV SET (F/G/H) 1) 48" - Conseal CS-102 1.00" 1) 24" x 36" - Conseal CS-102 1.00" 1) DOGHOUSE INVRTD - 30"x28" 1) Hole - 24 2) MH Step ML-10-TDS-NCR - 10"					0 lb 1044 lb 2752 lb 442 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 4238 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE 525 LV SET (F/G/H)). REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 933.49' Rim to Invert: 3.28' Slack: 0.26" Sump: 1.9" Step Position: 90°										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	930.21'	0°	0"	24" HDPE	27.8"	DOGHOUSE INVRTD 30"x28"	30" x 28"	32.406"	0"	0"
Invert 2	930.21'	292°	144.75"	18" HDPE	21.2"	Hole 24	24"	25.429"	0.25"	-3"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										




RIGHT-SIDE UP VIEW (int. dimensions)

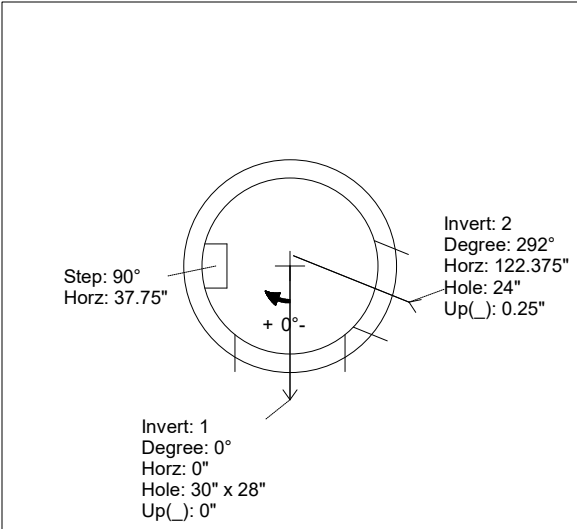

UPSIDE-DOWN VIEW (int. dimensions)

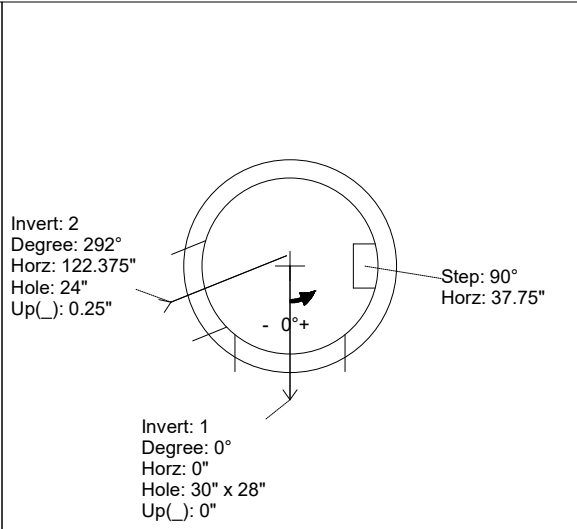

INSIDE WALL DIMENSIONS

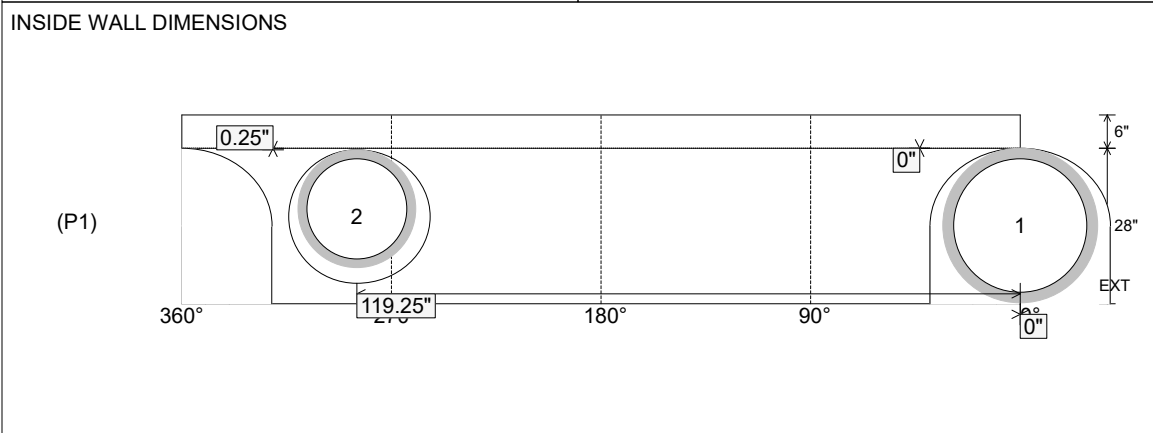

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 28" Height (Ext): 34"	Weight (Net): 2752 lb Volume (Net): 0.7cu.yd
----------------------------------	-------------------------------	--	--	---
