

Contractor: KY Earthworks

TECH: Jared - F

Plant: 100



Size: 60"

Rim to Invert: 8.1'

Floor Height: 8"

Slack: 1.05"


1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. NO INVERT CHANNEL.
4. CASTING BY ICAST (HOE 280T F/G)

- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. (DOUBLE MAT)
- RISER/WALLS (As .18)
- FLOOR (As .37) #5 BARS AT 10" C.C.E.W.


P4) 24" x 24" - CASTING HEIGHT - 4"
P3) 60" - MH FLAT TOP w/24"x24" Hole - 13"
P2) 60" - MH RISER - 24"
P1) 60" - MH BASE Custom Ht - 58"
1) CASTING - HOE 280T F/G
2) 60" - Conseal CS-102 1.00"
1) 24" x 24" - Conseal CS-102 1.00"
2) Hole - 44
7) MH Step ML-10-TDS-NCR - 10"

0 lb
2619 lb
2505 lb
7105 lb
182 lb
0 lb
0 lb
0 lb
0 lb


Structure Total: 12411 lb

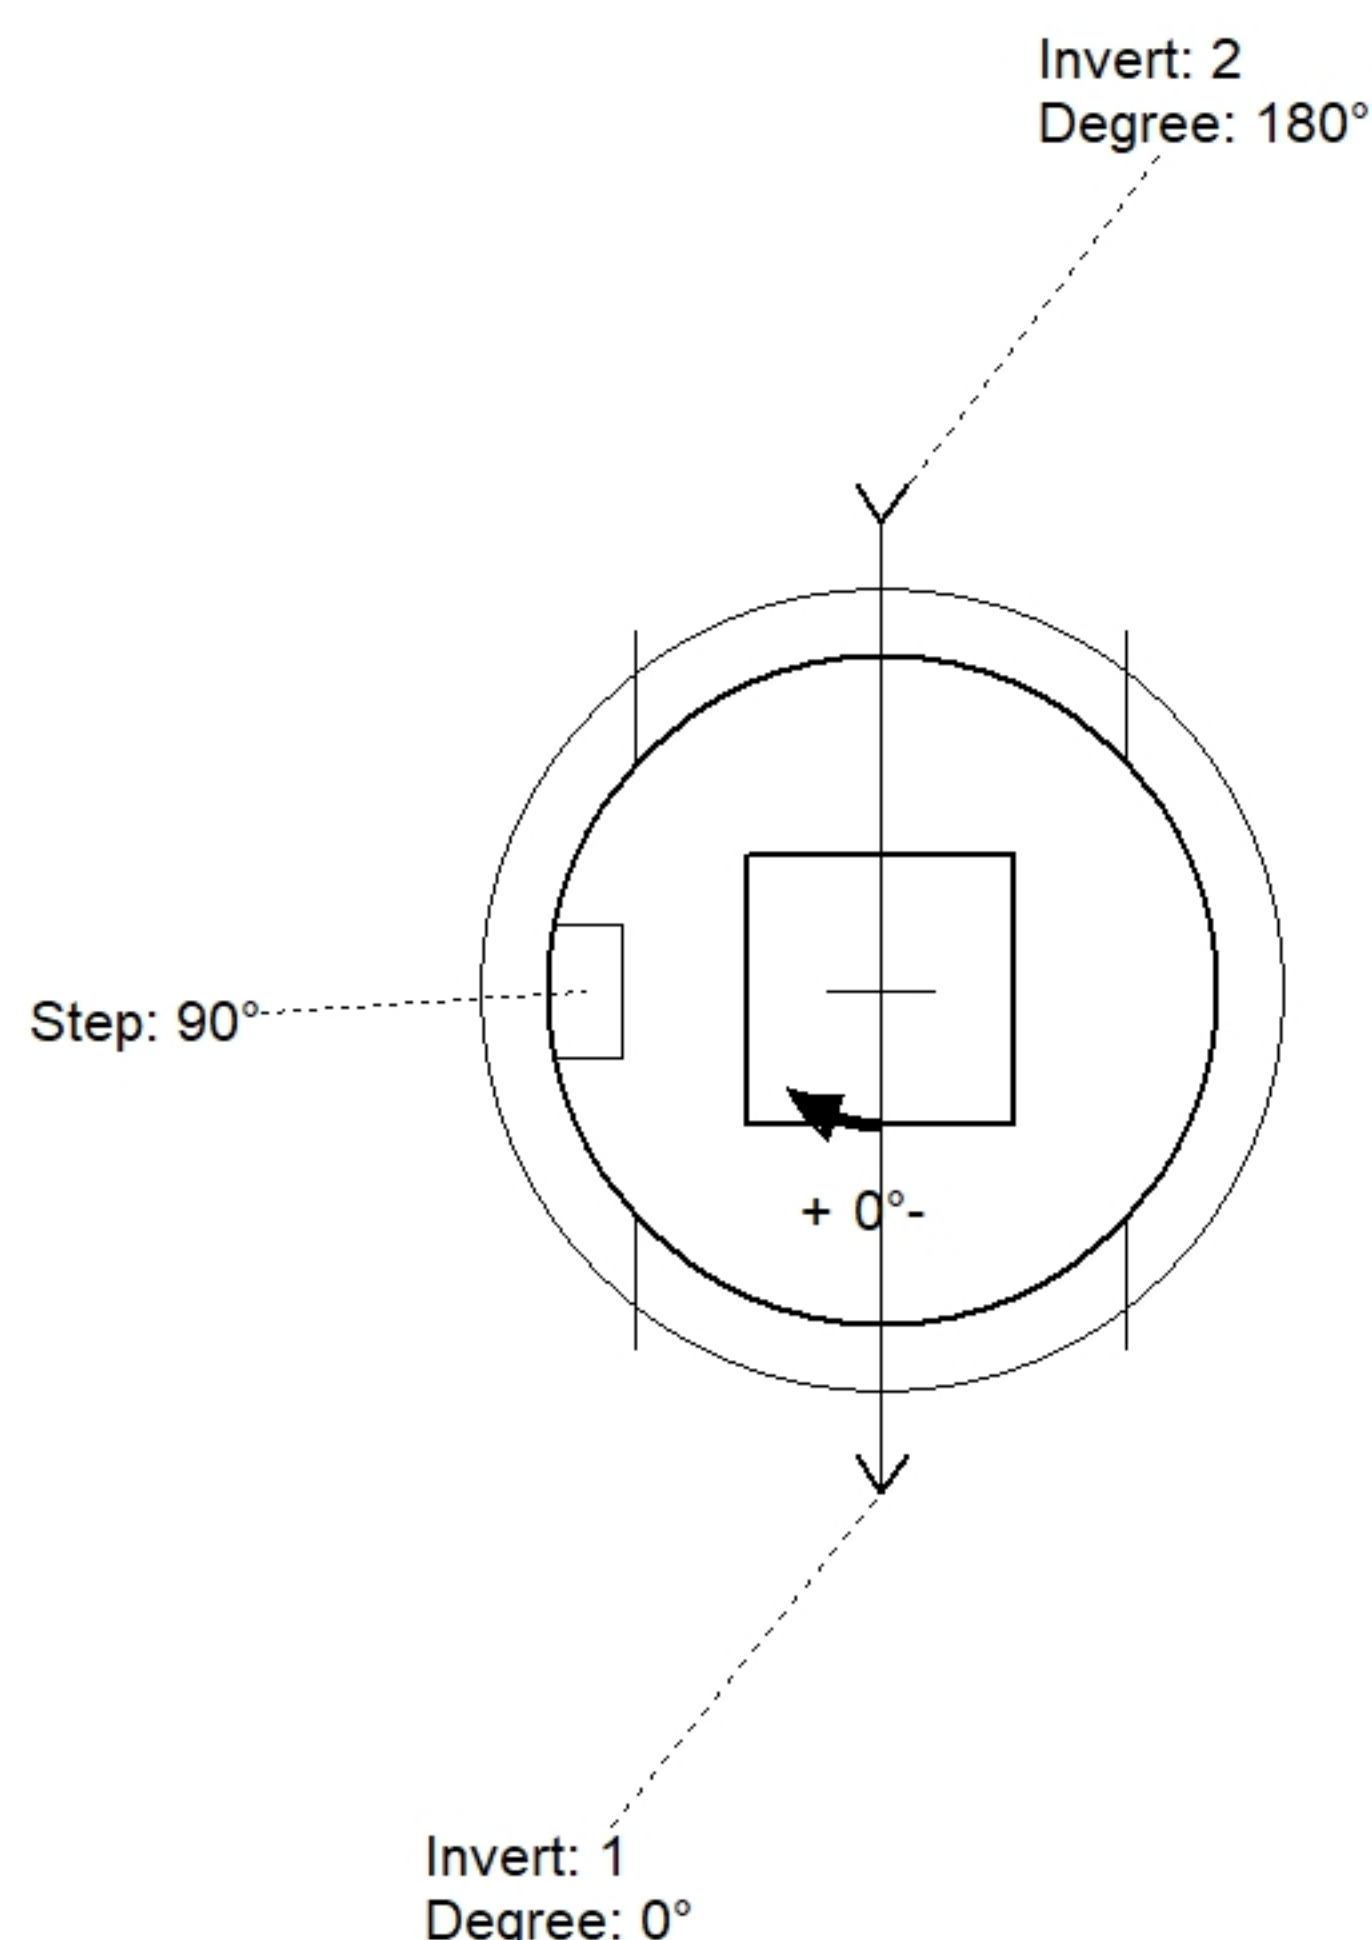

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	934.18'							
Reducer								
Invert 1	926.08'	0°	36" HDPE	41.7"	44"	Hole 44	0"	P1
Invert 2	926.08'	180°	36" HDPE	41.7"	44"	Hole 44	0"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

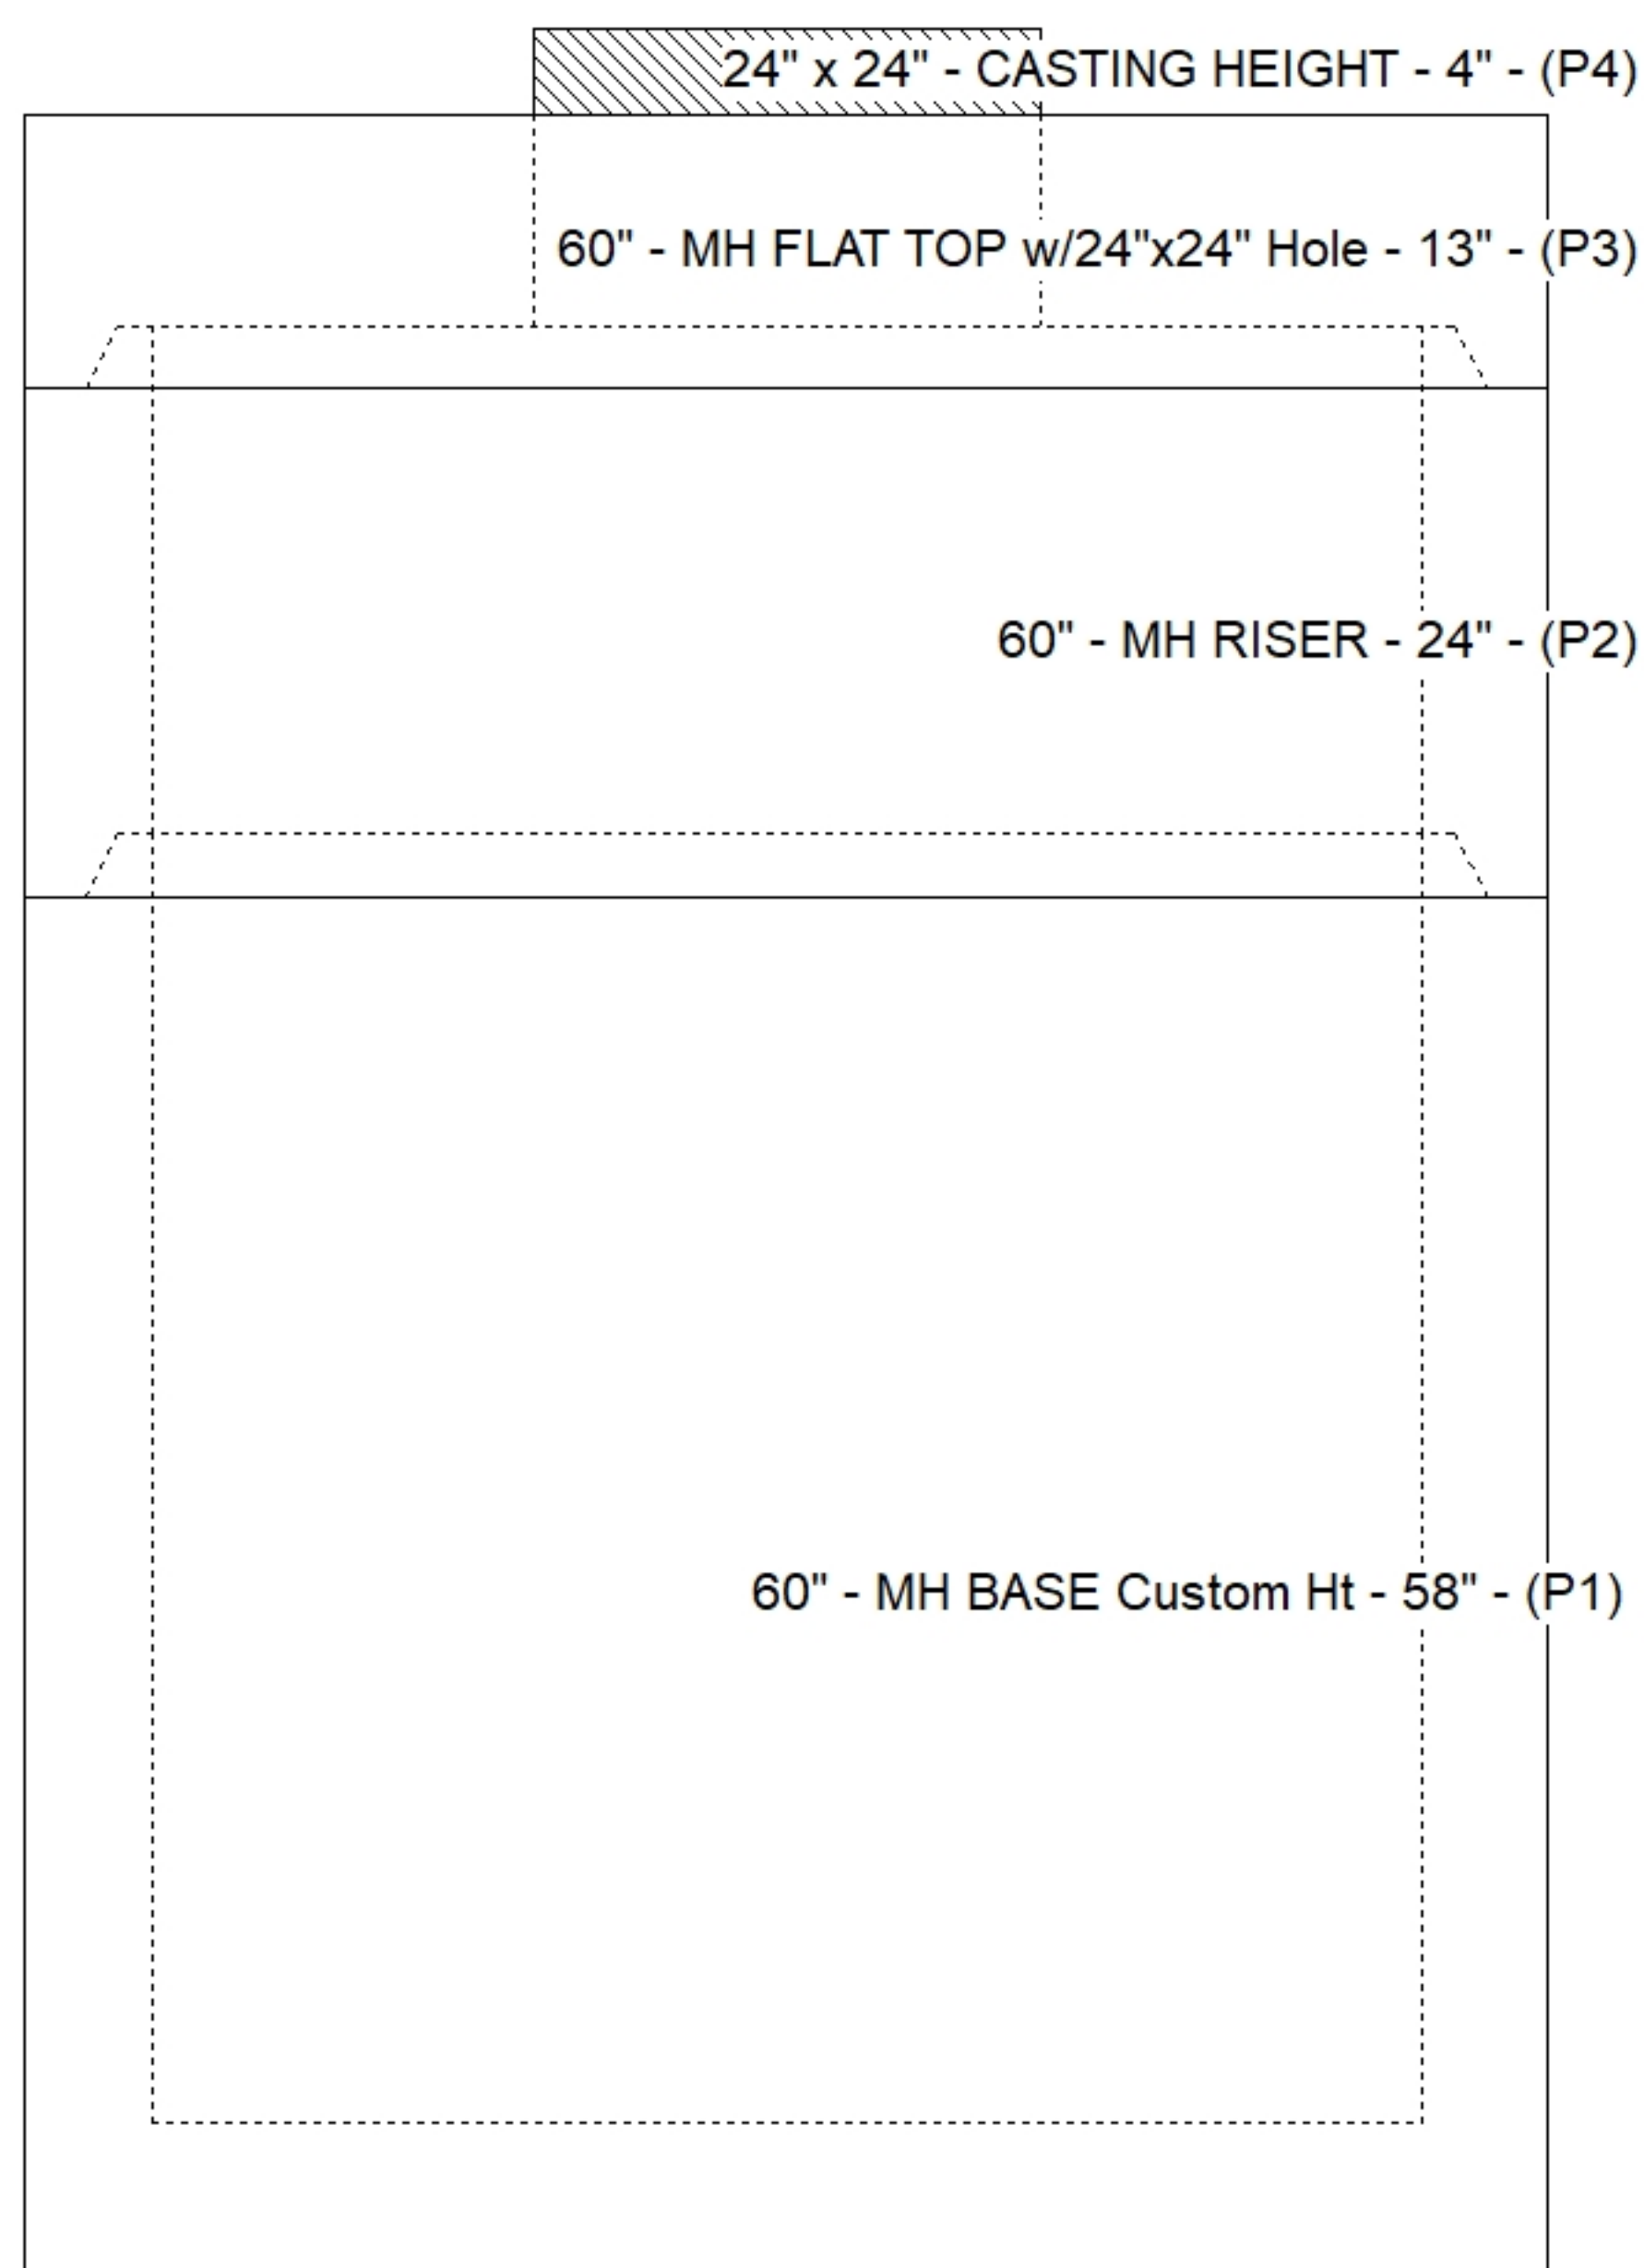

Default - Interior Dimensions

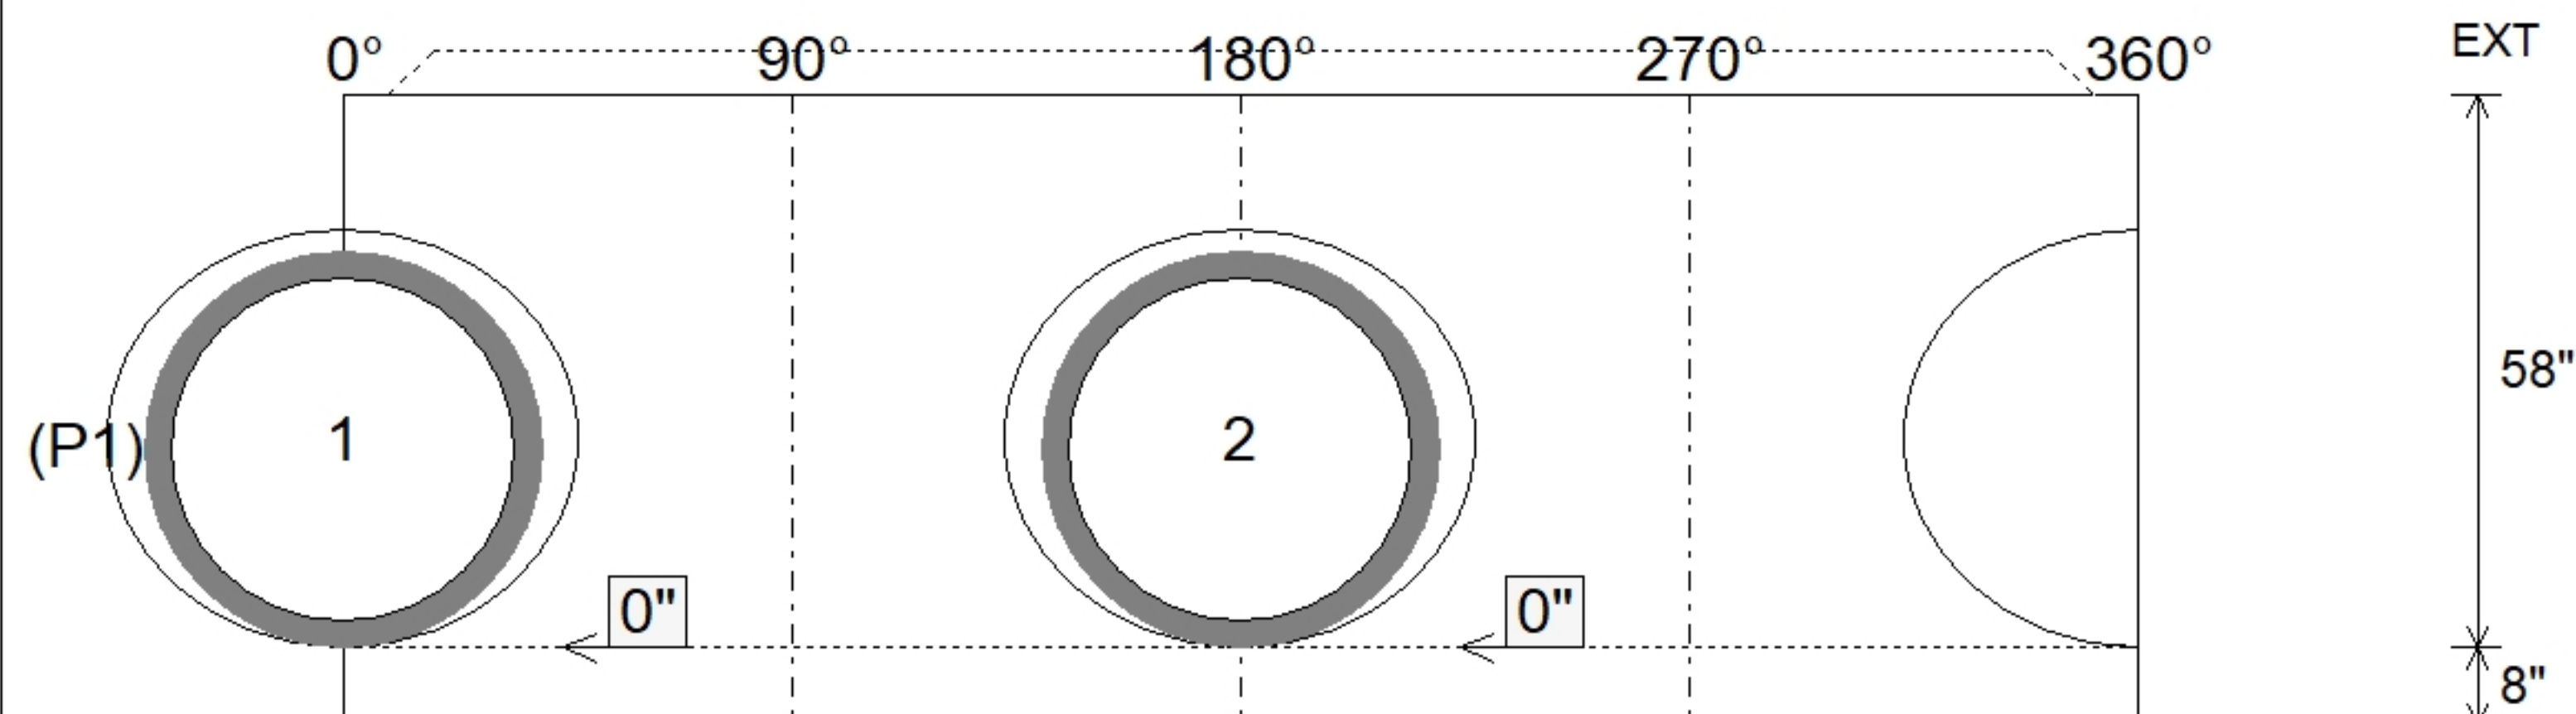

Submittal Drawing
9/29/2026 8:26:01 AM

SUBMITTAL
APPROVED BY:
