




Job Name: 26-1822 - Project Versailles Job Location: Versailles, KY Contractor: KY Earthworks					Plant: 100 9/24/2026 11:31:25 AM		Tech: Jared - F PC: E. Bradley			
Structure ID: D7 ST-CI										
P1 MH060BAVF		MH BASE Custom Ht T/n								
P4) 24" x 36" - CASTING HEIGHT - 6" P3) 60" - MH FLAT TOP w/24"x36" Hole F/G - 13" P2) 60" - MH RISER T/G - 24" P1) 60" - MH BASE Custom Ht T/n - 52" 1) CASTING - HOE 525 LV SET (F/G/H) 2) 60" - Conseal CS-102 1.00" 1) 24" x 36" - Conseal CS-102 1.00" 2) Hole - 38 6) MH Step ML-10-TDS-NCR - 10"					0 lb 3499 lb 2505 lb 6942 lb 442 lb 0 lb 0 lb 0 lb 0 lb ----- 13388 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE 525 LV SET (F/G/H)). REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 936.2' Rim to Invert: 7.87' Slack: 1.99' Sump: 2.55' Step Position: 90°										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	928.33'	0°	0"	30" HDPE	35.1"	Hole 38	38"	41.151"	0"	0"
Invert 2	928.33'	180°	113.125"	30" HDPE	35.1"	Hole 38	38"	41.151"	0"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

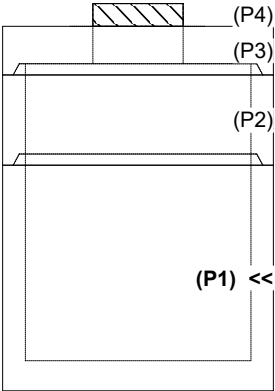


RIGHT-SIDE UP VIEW (int. dimensions)

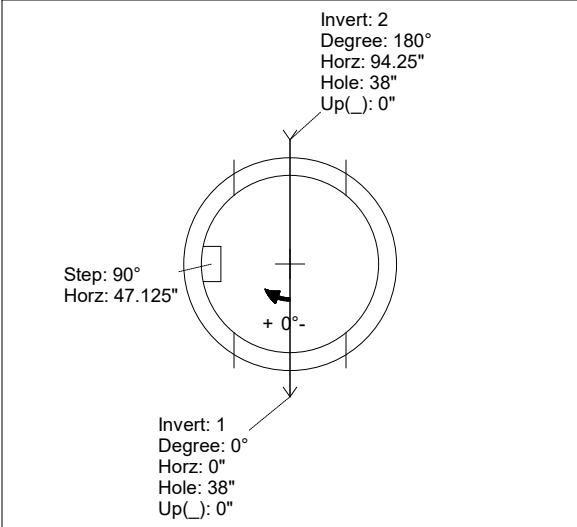

UPSIDE-DOWN VIEW (int. dimensions)

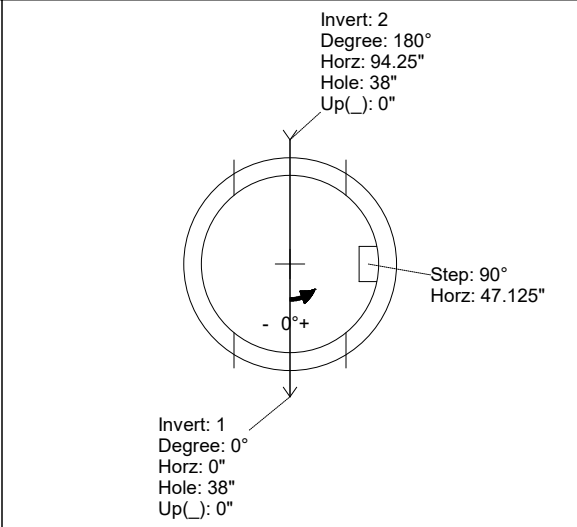

INSIDE WALL DIMENSIONS

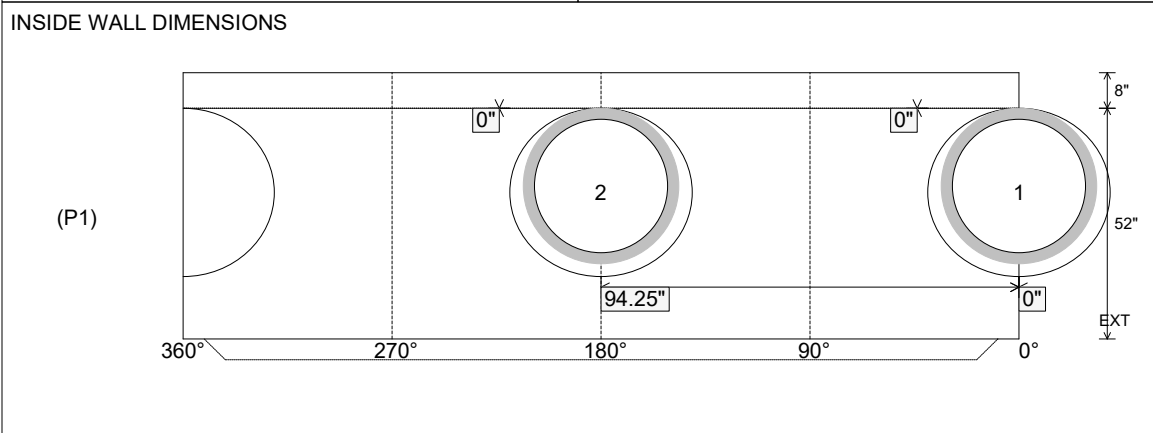

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 6" Floor Height: 8"	Height (Int): 52" Height (Ext): 60"	Weight (Net): 6942 lb Volume (Net): 1.77cu.yd
----------------------------------	---------------------------------	--	--	--
