



Job Name: 26-1987P6 - Project Nova Job Location: Sullivan, IN 47882 Contractor: McCreary Concrete Products, Inc.					Plant: Beaver Dam 9/3/2026 3:12:37 PM		Tech: J. Coppage PC: M. Sullivan				
Structure ID: 1305											
P1		MH108BA96		MH BASE							
P5) 24" - CASTING HEIGHT - 0" P4) 24" - GRADE RING - 4" P3) 108" - MH FLAT TOP w/24" ECC Hole - 17" P2) 108" - MH RISER - 96" P1) 108" - MH BASE - 96" 2) 108" - Conseal CS-102 1.00" 2) 24" - Conseal CS-102 1.00" 1) Hole - 76 1) Hole - 68 1) Hole - 34 4) Hole - 6 16) MH Step ML-10-TDS-NCR - 10"					0 lb 270 lb 10472 lb 29768 lb 34643 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb		Structure Notes: 1. (CASTING PROVIDED BY OTHERS) 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .36) - FLOOR (As .47) #5 BARS AT 8" C.C.E.W.				
Structure Total:					75153 lb						
Rim: 508.94' Rim to Invert: 17.38' Slack: 1.56" Sump: 6" Step Position: 240											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	491.56'	0°	0"	60" RCP B WALL	72"	Hole 76	76"	84.304"	0"	0"	
Invert 2	492.06'	180°	201.062"	54" RCP B WALL	65"	Hole 68	68"	73.556"	6.5"	0"	
Invert 3	494.56'	90°	100.531"	24" RCP B WALL	30"	Hole 34	34"	34.588"	39"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											


RIGHT-SIDE UP VIEW (int. dimensions)

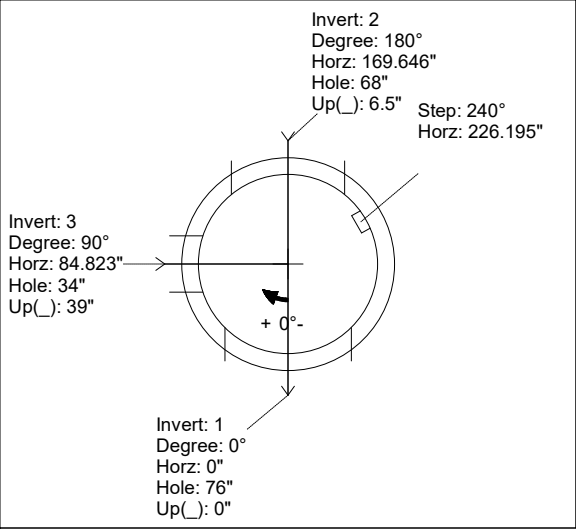

UPSIDE-DOWN VIEW (int. dimensions)

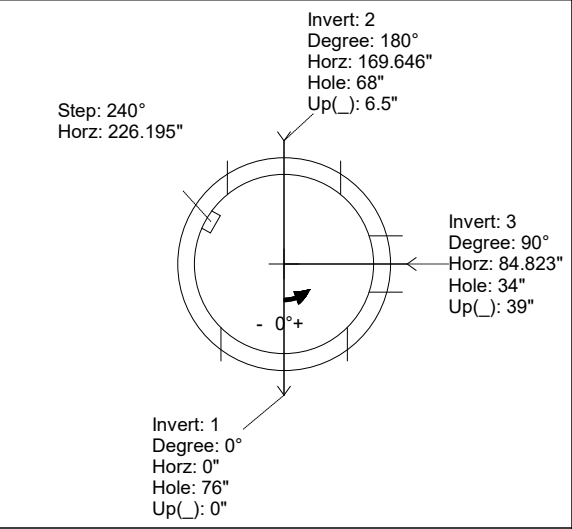

INSIDE WALL DIMENSIONS

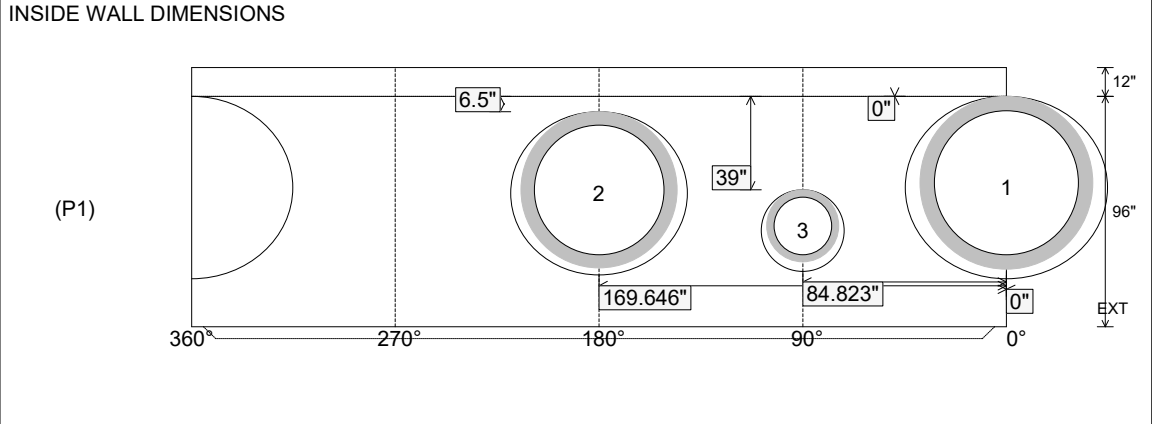

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 10" Floor Height: 12"	Height (Int): 96" Height (Ext): 108"	Weight (Net): 34643 lb Volume (Net): 8.85cu.yd
----------------------------------	---------------------------------	--	---	---
