



Job Name: 26-1987P6 - Project Nova Job Location: Sullivan, IN 47882 Contractor: McCreary Concrete Products, Inc.					Plant: Beaver Dam 9/3/2026 3:12:40 PM		Tech: J. Coppage PC: M. Sullivan						
Structure ID: 1415													
P1		MH120BVF										MH BASE	
P5) 24" - CASTING HEIGHT - 0" P4) 120" - MH FLAT TOP w/ 24" ECC Hole - 18" P3) 120" - MH RISER - 84" P2) 120" - MH RISER - 96" P1) 120" - MH BASE - 96" 3) 120" - Conseal CS-102 1.00" 1) 24" - Conseal CS-102 1.00" 2) Hole - 90 1) Hole - 60 4) Hole - 6 22) MH Step ML-10-TDS-NCR - 10"					0 lb 16678 lb 31805 lb 36468 lb 36701 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb Structure Total: 121651 lb		Structure Notes: 1. (CASTING PROVIDED BY OTHERS) 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .36) - FLOOR (As .47) #5 BARS AT 8" C.C.E.W. 4 EA - 8CA18 A-Anchors In The Floor For Handling						
Rim: 510.79' Rim to Invert: 23.96' Slack: 0.52' Sump: 7" Step Position: 90													
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset			
Invert 1	486.83'	0°	0"	72" RCP B WALL	86"	Hole 90	90"	101.767"	0"	0"			
Invert 2	486.93'	180°	223.053"	72" RCP B WALL	86"	Hole 90	90"	101.767"	1.2"	0"			
Invert 3	488.05'	270°	334.58"	48" RCP B WALL	58"	Hole 60	60"	62.832"	16.64"	0"			
Invert 4													
Invert 5													
Invert 6													
Invert 7													
Invert 8													


RIGHT-SIDE UP VIEW (int. dimensions)

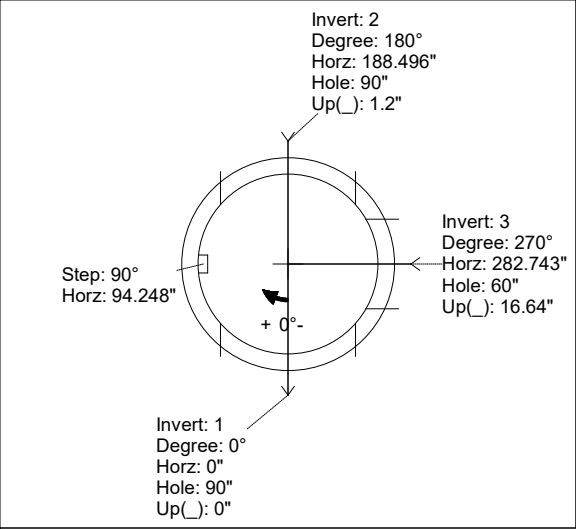

UPSIDE-DOWN VIEW (int. dimensions)

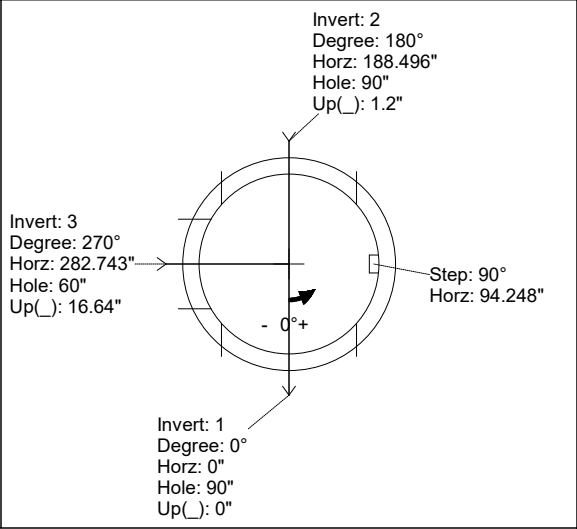

INSIDE WALL DIMENSIONS

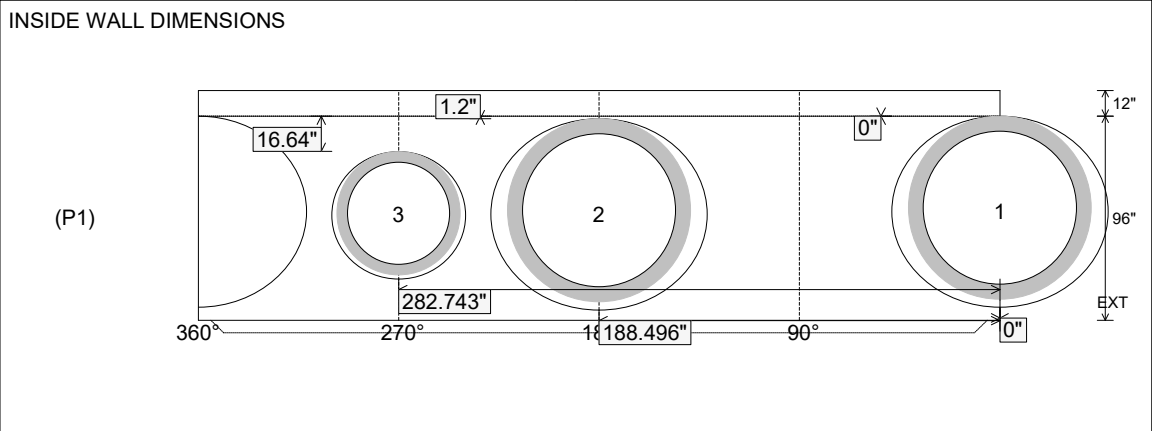

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 11" Floor Height: 12"	Height (Int): 96" Height (Ext): 108"	Weight (Net): 36701 lb Volume (Net): 9.37cu.yd
----------------------------------	---------------------------------	--	---	---
