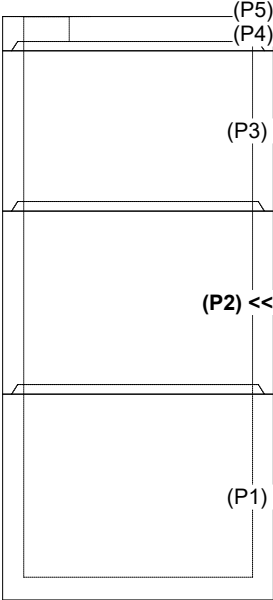




Job Name: 26-1987P6 - Project Nova Job Location: Sullivan, IN 47882 Contractor: McCreary Concrete Products, Inc.					Plant: Beaver Dam 9/3/2026 3:15:46 PM		Tech: J. Coppage PC: M. Sullivan				
Structure ID: 1415											
P2		MH120RS96		MH RISER							
P5) 24" - CASTING HEIGHT - 0" P4) 120" - MH FLAT TOP w/ 24" ECC Hole - 18" P3) 120" - MH RISER - 84" P2) 120" - MH RISER - 96" P1) 120" - MH BASE - 96" 3) 120" - Conseal CS-102 1.00" 1) 24" - Conseal CS-102 1.00" 2) Hole - 90 1) Hole - 60 4) Hole - 6 22) MH Step ML-10-TDS-NCR - 10"					0 lb 16678 lb 31805 lb 36468 lb 36701 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb		Structure Notes: . 1. (CASTING PROVIDED BY OTHERS) 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .36) - FLOOR (As .47) #5 BARS AT 8" C.C.E.W.				
Rim: 510.79' Rim to Invert: 23.96' Slack: 0.52" Sump: 7" Step Position: 90					Structure Total: 121651 lb						
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)											
											
INSIDE WALL DIMENSIONS											
											
Coating (Int): Coating (Ext):		Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 11" Floor Height: 0"		Height (Int): 96" Height (Ext): 96"		Weight (Net): 36468 lb Volume (Net): 9.32cu.yd			
