





Job Name: 26-2025 - KYTC Warren Co (261510) Job Location: Bowling Green, KY Contractor: Mick-Murf Construction Inc.					Plant: 100 8/25/2026 12:58:52 PM		Tech: Jared - F PC: T. Lewis				
Structure ID: CB18 CBIA											
P1 BX2436-08BVF BOX BASE 8inW, 8inF, Variable Ht T/n											
P3) 24" x 120" - CB INLET KY A 10' TOP LEFT F/G - 10" P2) 24" x 120" - CB INLET KY A 10' BOTTOM LEFT T/G - 18" P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht T/n - 37" 1) CASTING - HOE KY-206 F/C (KY CBI A) 1) 24" x 36" - Conseal CS-102 1.00" 3) Hole - 22"						3400 lb 5270 lb 4406 lb 206 lb 0 lb 0 lb ----- Structure Total: 13282 lb		Structure Notes: ** KYTC STATE PROJECT ** 1. PER KYTC CBI TYPE A / ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE KY-206 F/C (KY CBI A)) REINFORCING PER ASTM A615 (GRADE 60). - TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W. - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 556.61' Rim to Invert: 5.67' Slack: 3.04" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1	550.94'	0°	20"	18" CMP	19"	Hole 22	22"	22"	-2"	0"	
Invert 2	551.02'	180°	20"	18" CMP	19"	Hole 22	22"	22"	-1"	0"	
Invert 3	551.02'	270°	26"	18" CMP	19"	Hole 22	22"	22"	-1"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

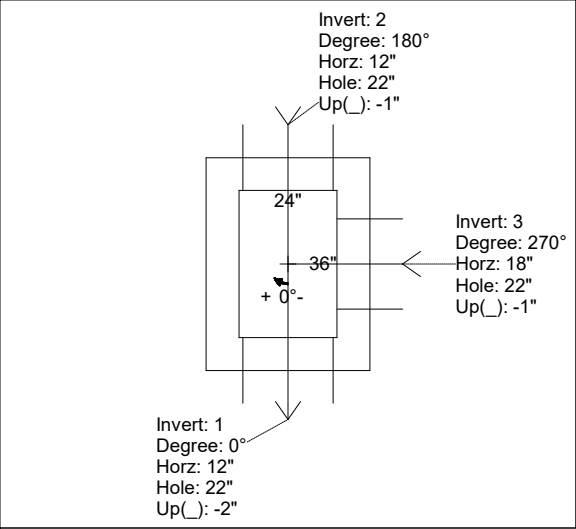

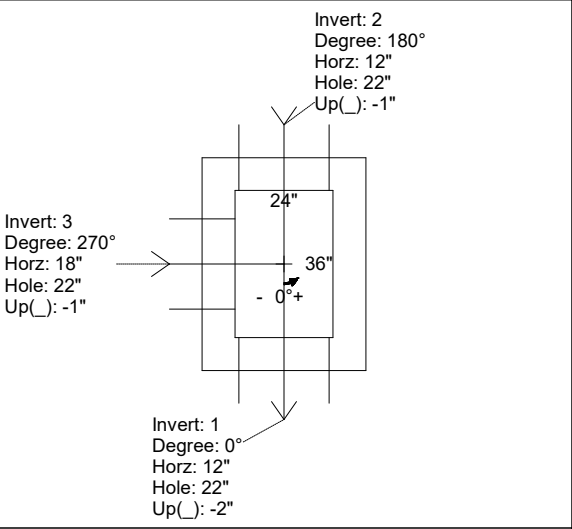

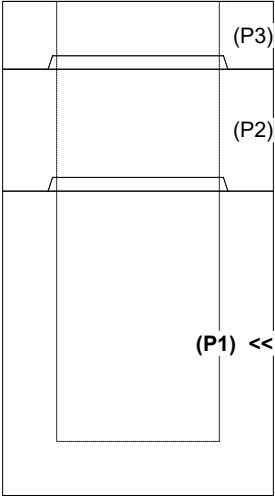

INSIDE WALL DIMENSIONS

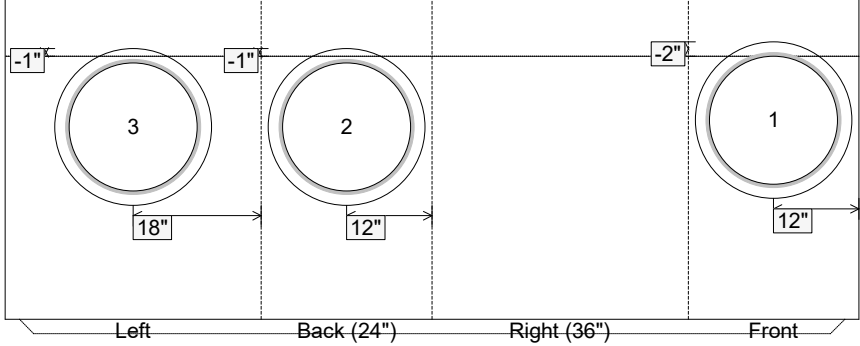

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 37" Height (Ext): 45"	Weight (Net): 4406 lb Volume (Net): 1.12cu.yd
----------------------------------	---------------------------------	--	--	--
