

Contractor: Jim Smith Contracting Co, LLC

TECH: J. Horsley

Plant: 100



Size: 24" x 24"

Rim to Invert: 5.44'


Floor Height: 8"

Slack: 0.28"


REINFORCING PER ASTM A615 (GRADE 60).

- TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W.
- WALLS (As .31) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


Structure Total: 8255 lb

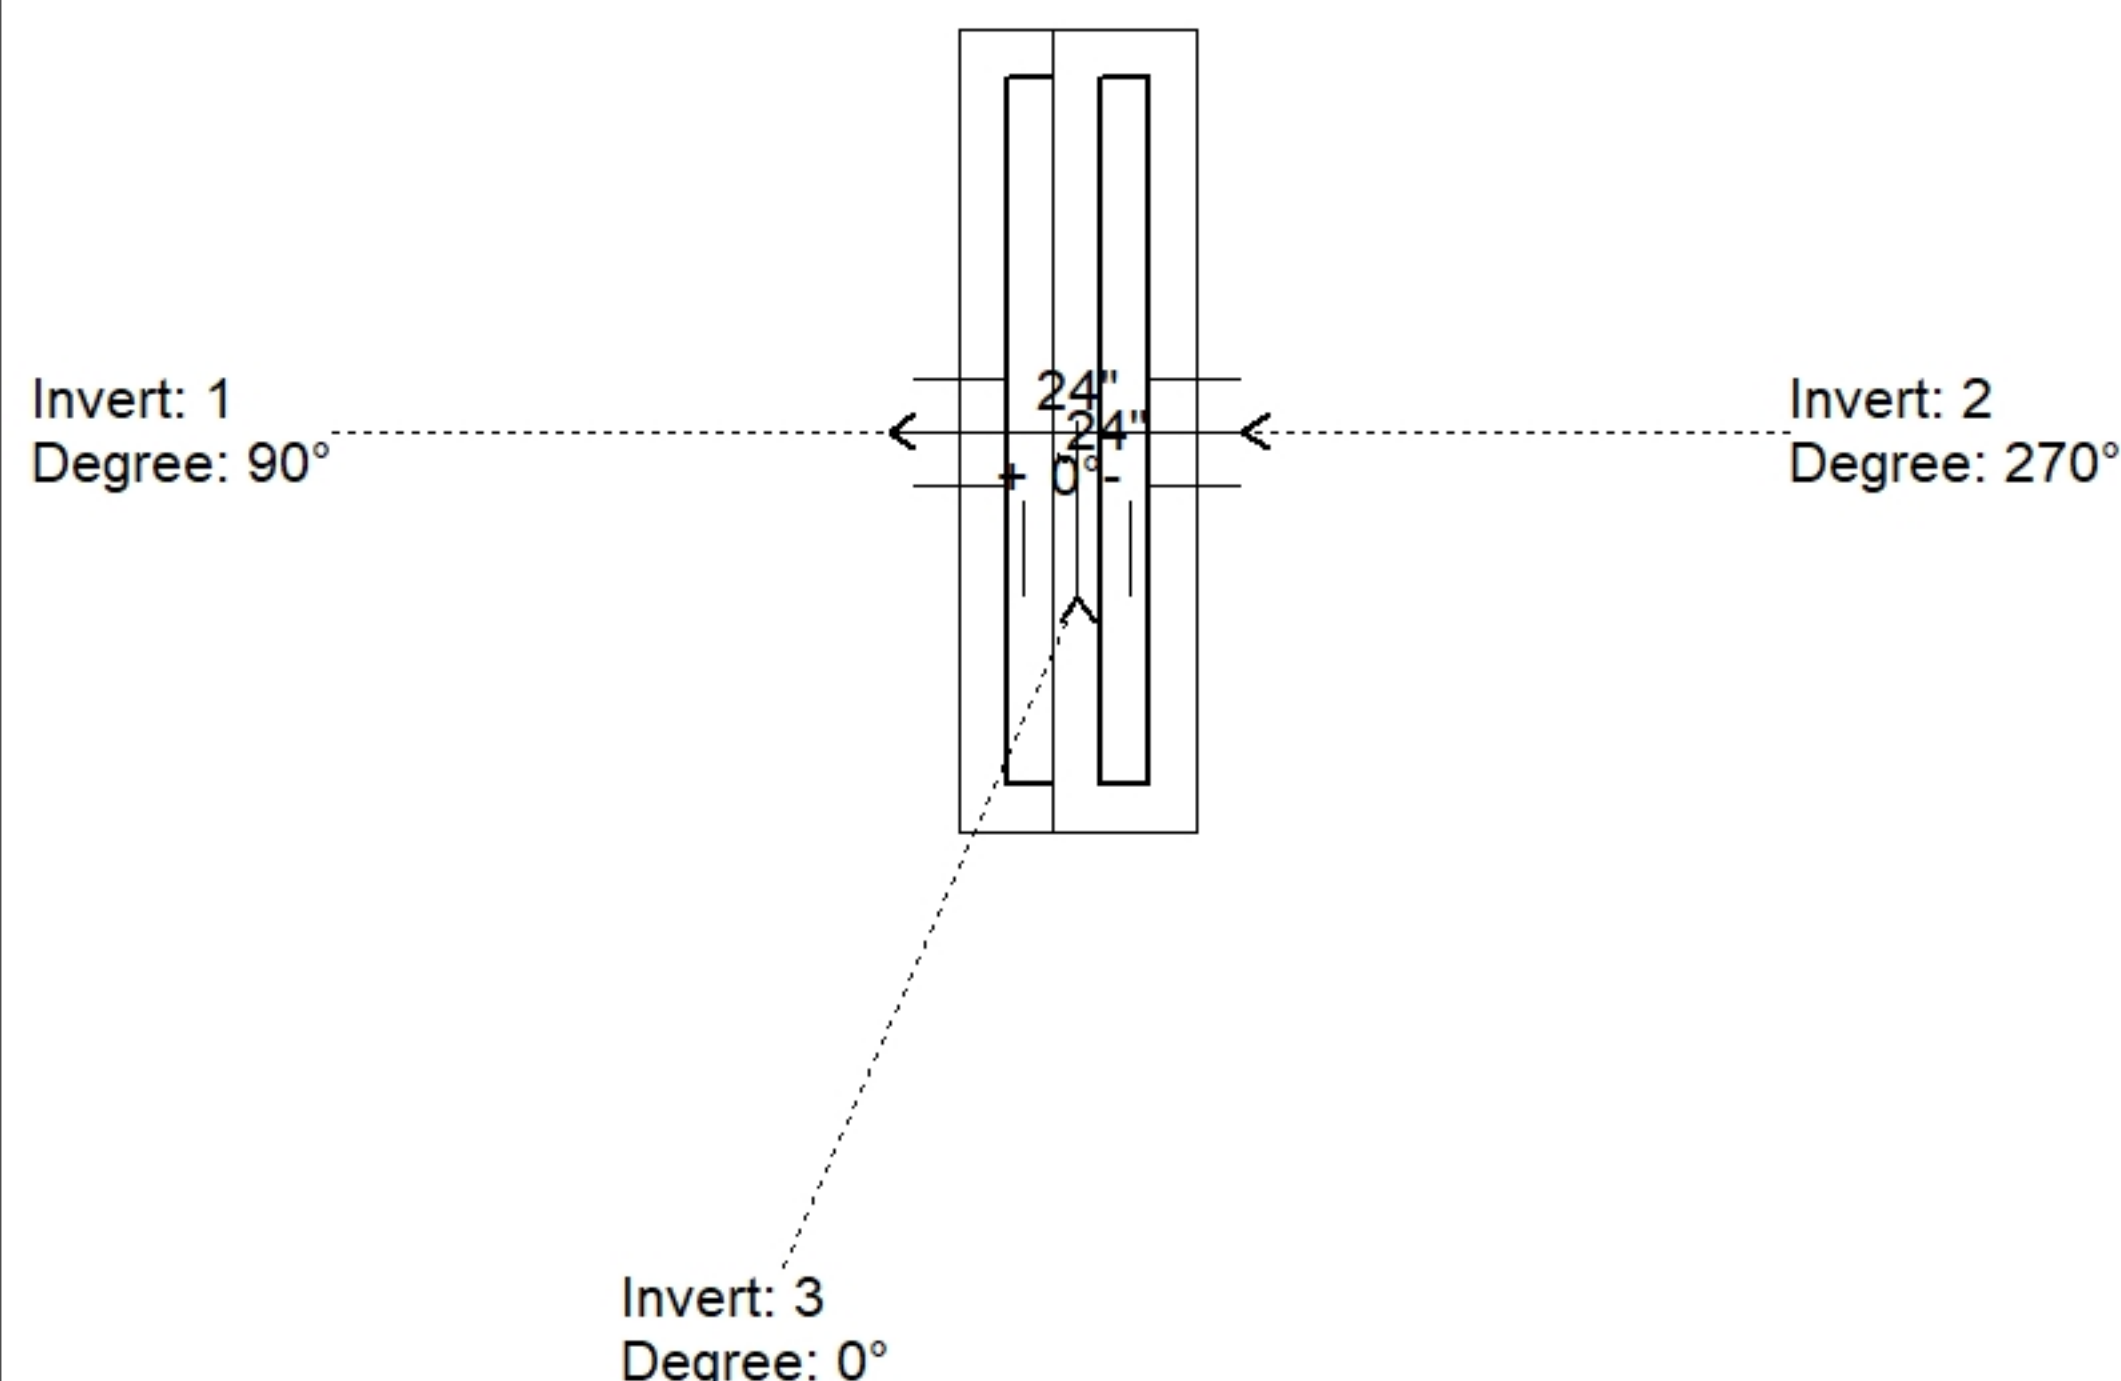

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	372.94'							
Reducer								
Invert 1	367.5'	90°	15" CMP	16"	18"	Hole 18	-1.5"	P1
Invert 2	367.5'	270°	15" CMP	16"	18"	Hole 18	-1.5"	P1
Invert 3	367.5'	0°	15" CMP	16"	18"	Hole 18	-1.5"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

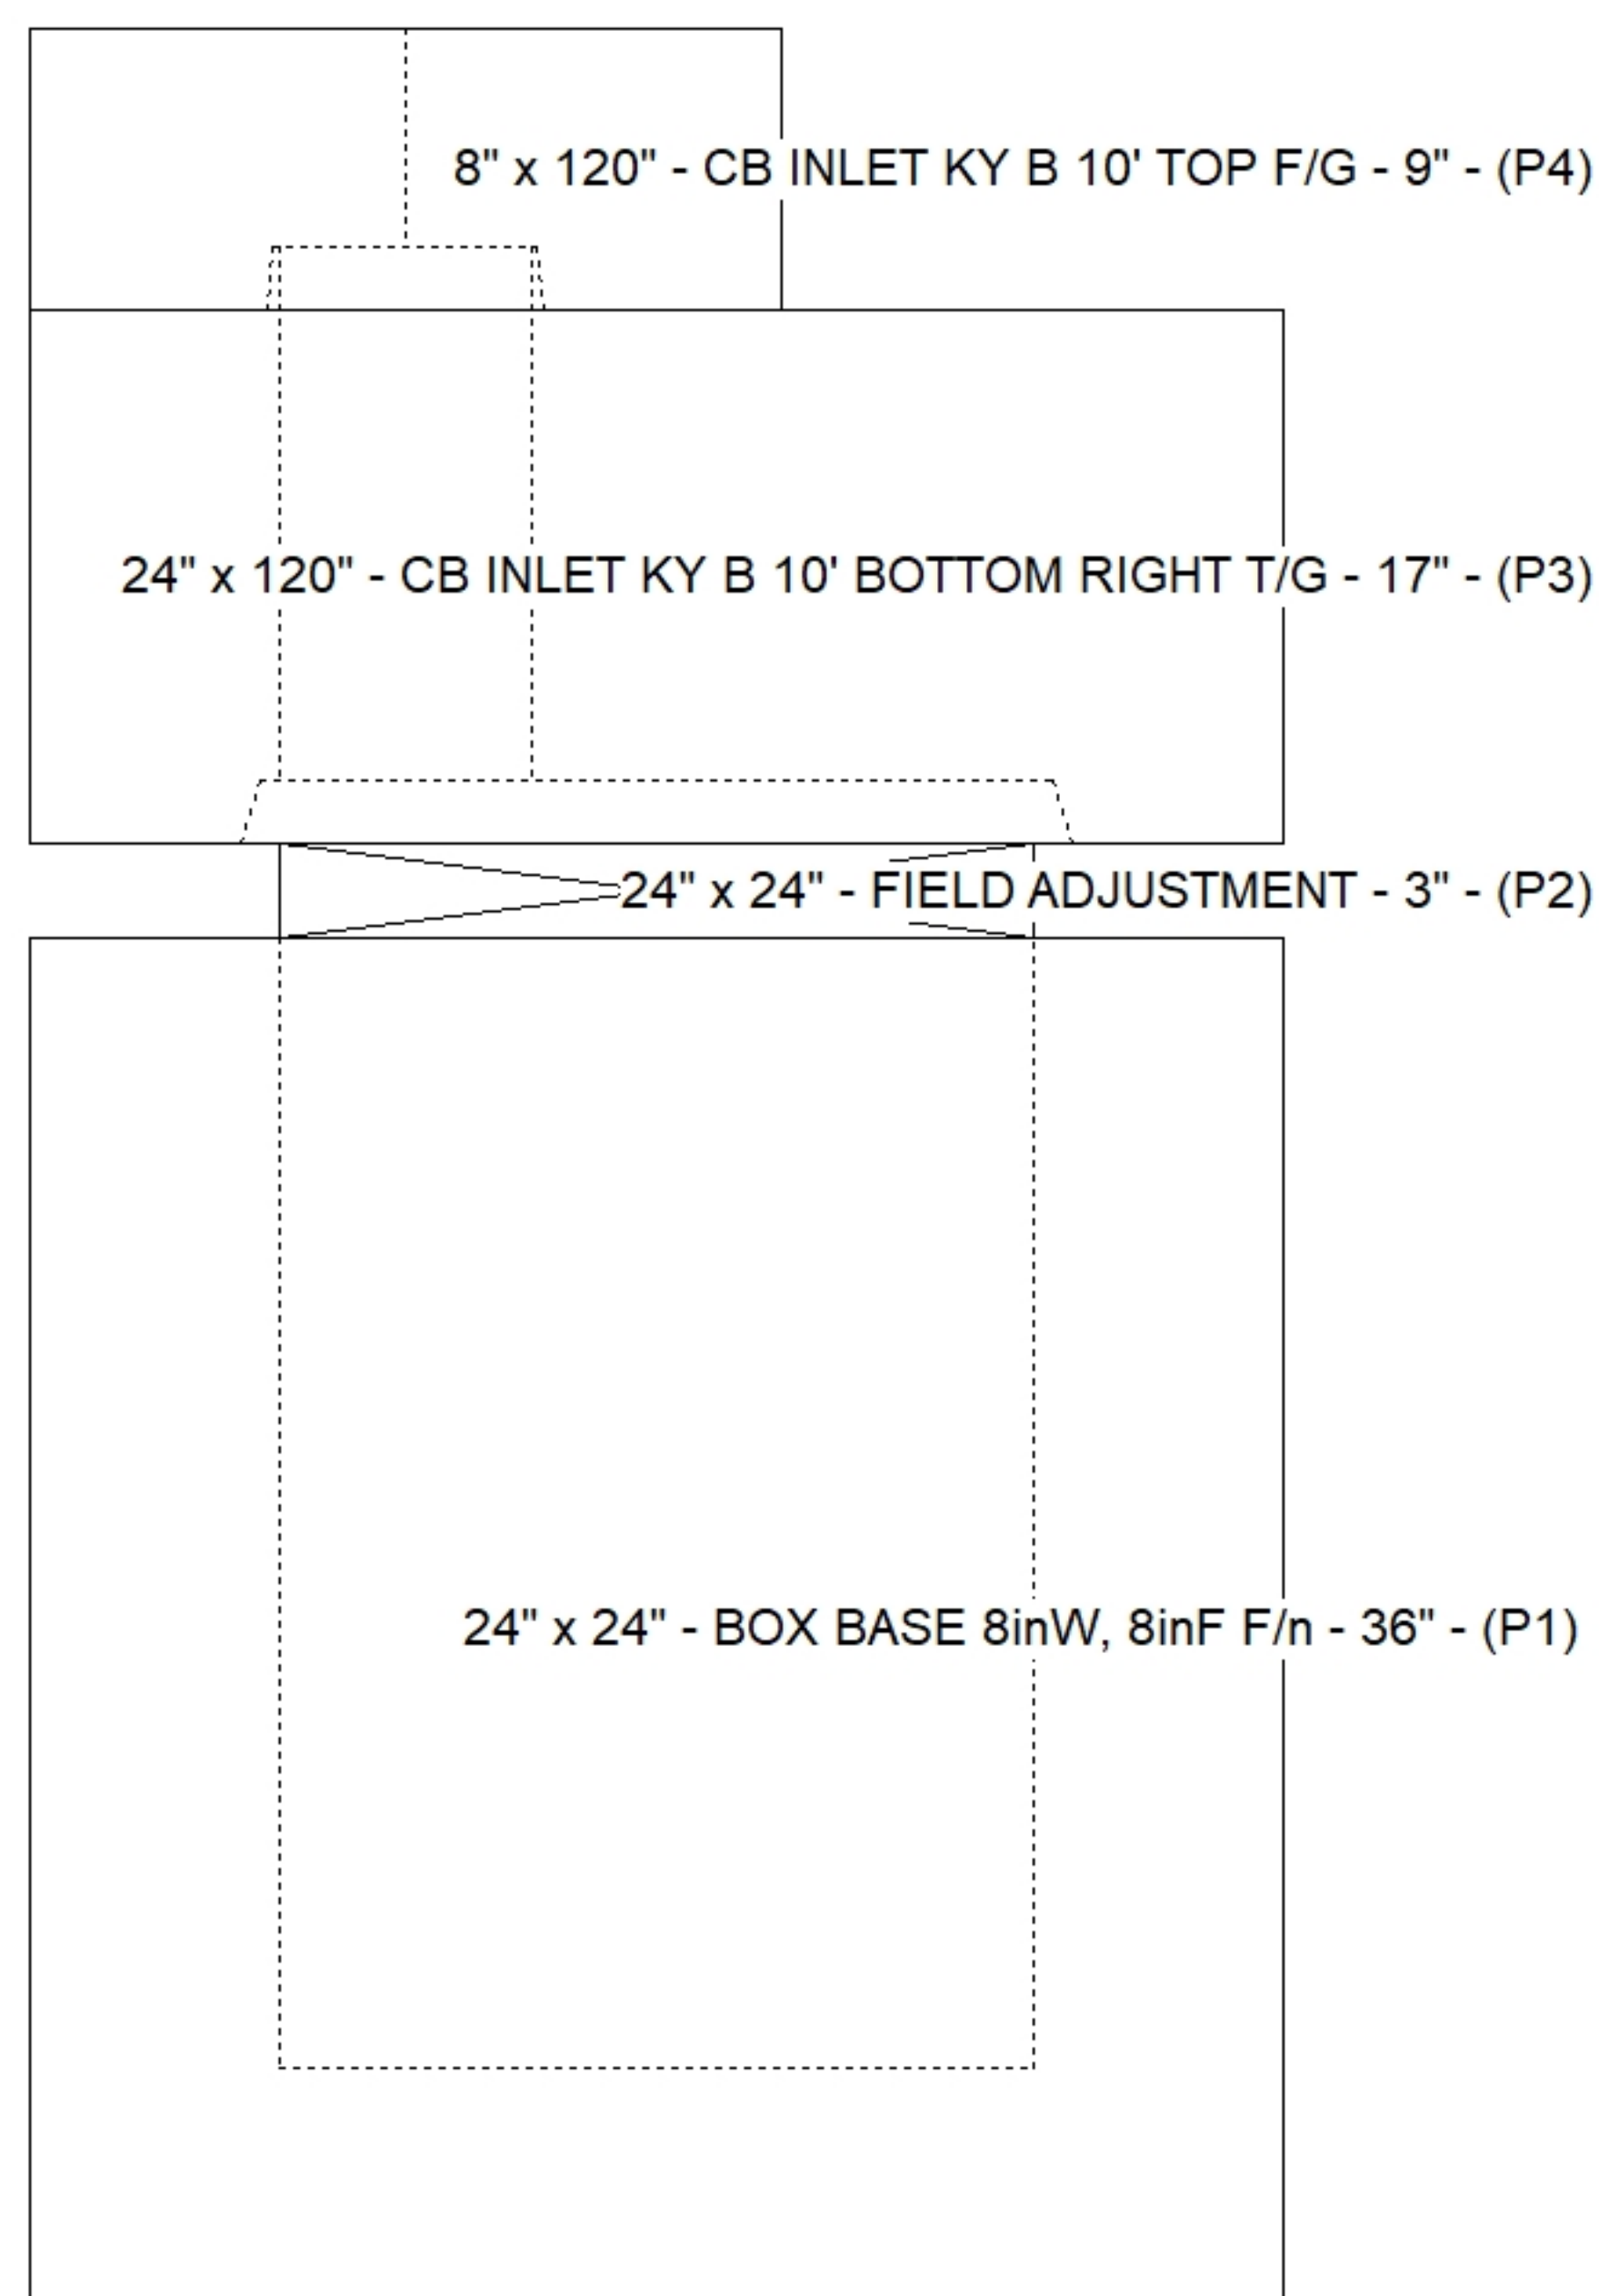

Cast (Int. Dim.) - Interior Dimensions

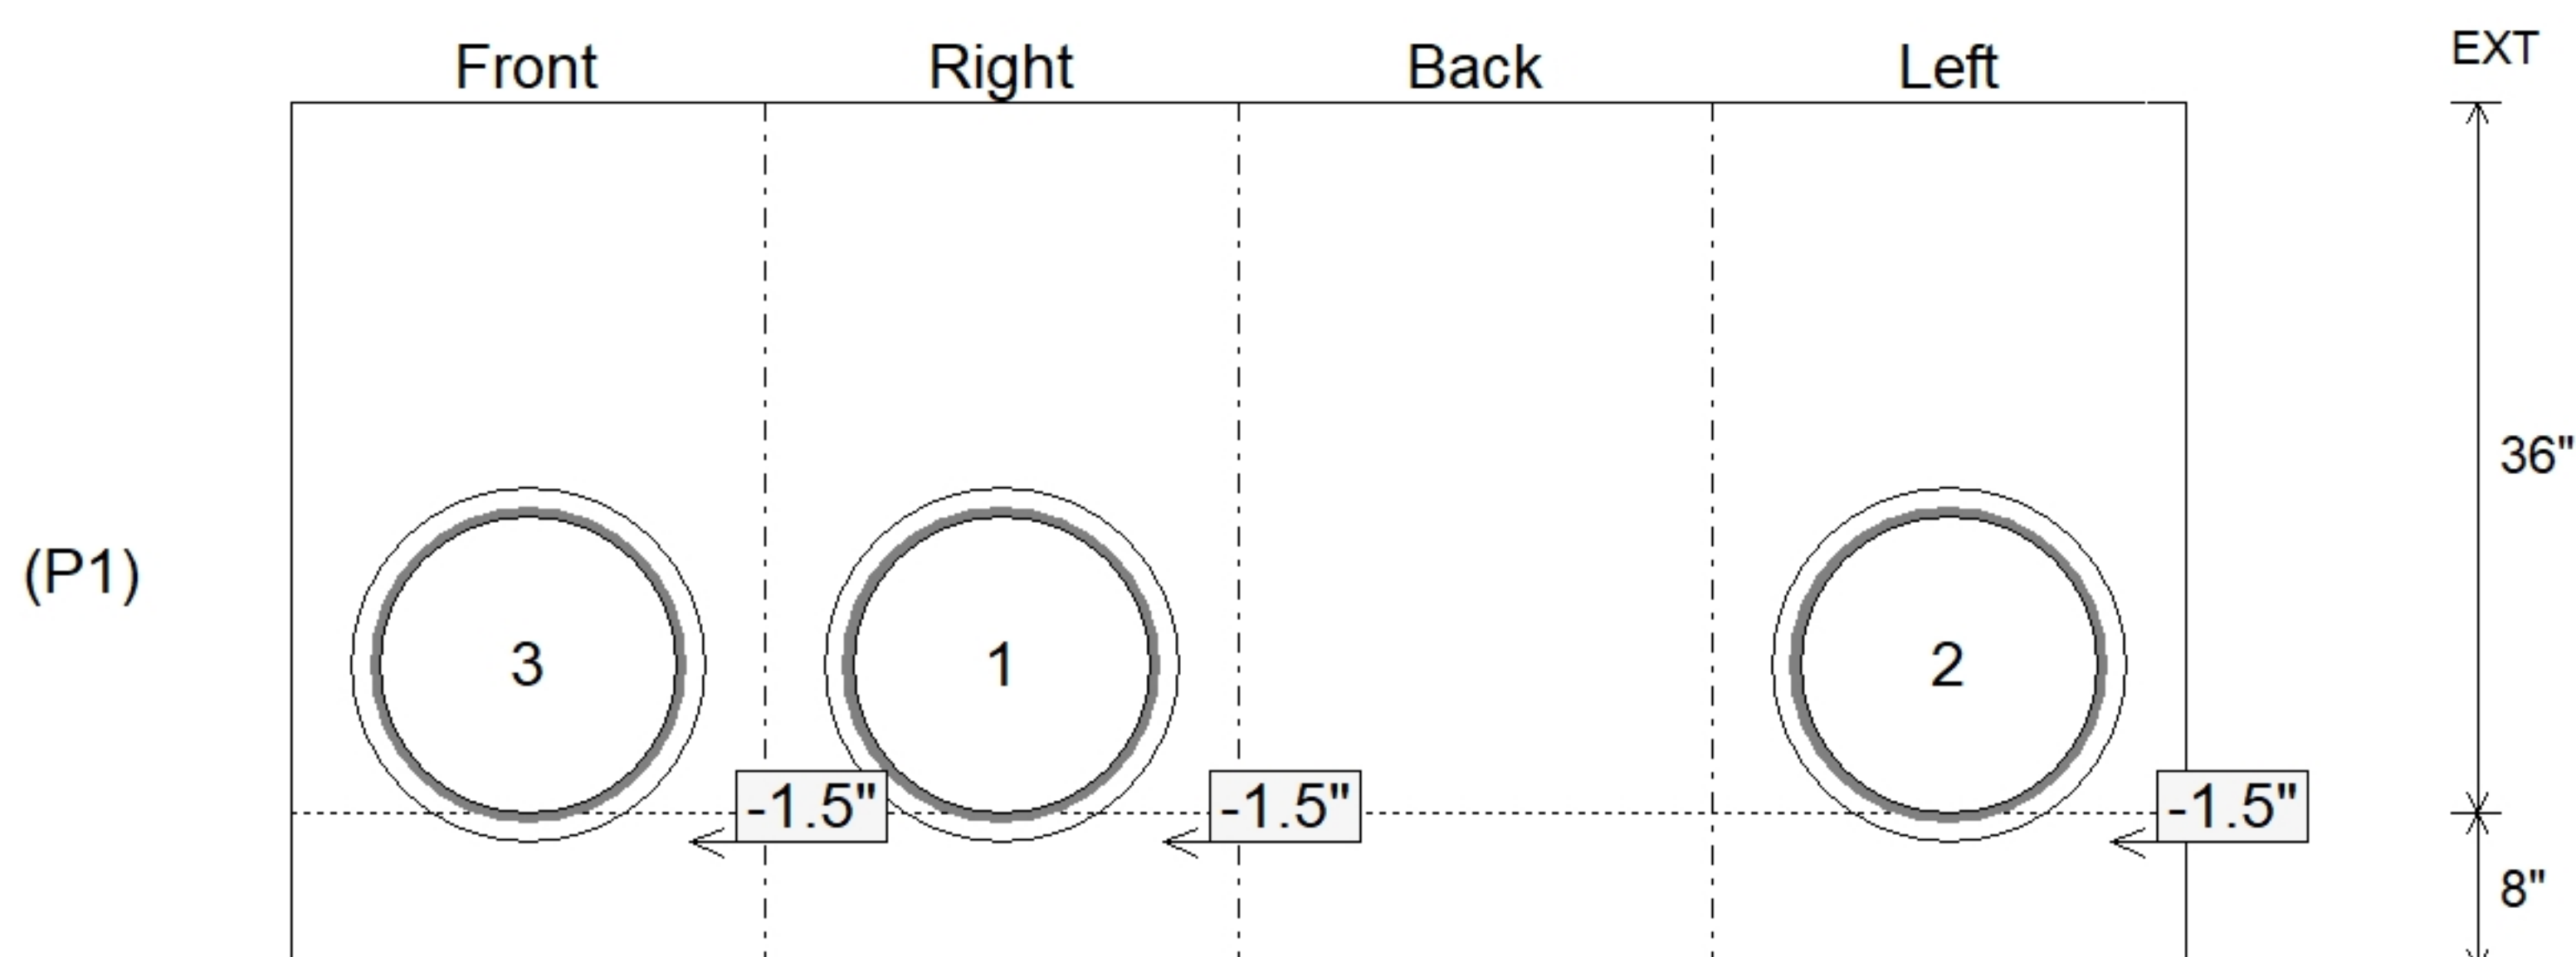

Submittal Drawing
6/12/2026 7:48:33 AM

SUBMITTAL
APPROVED BY:
