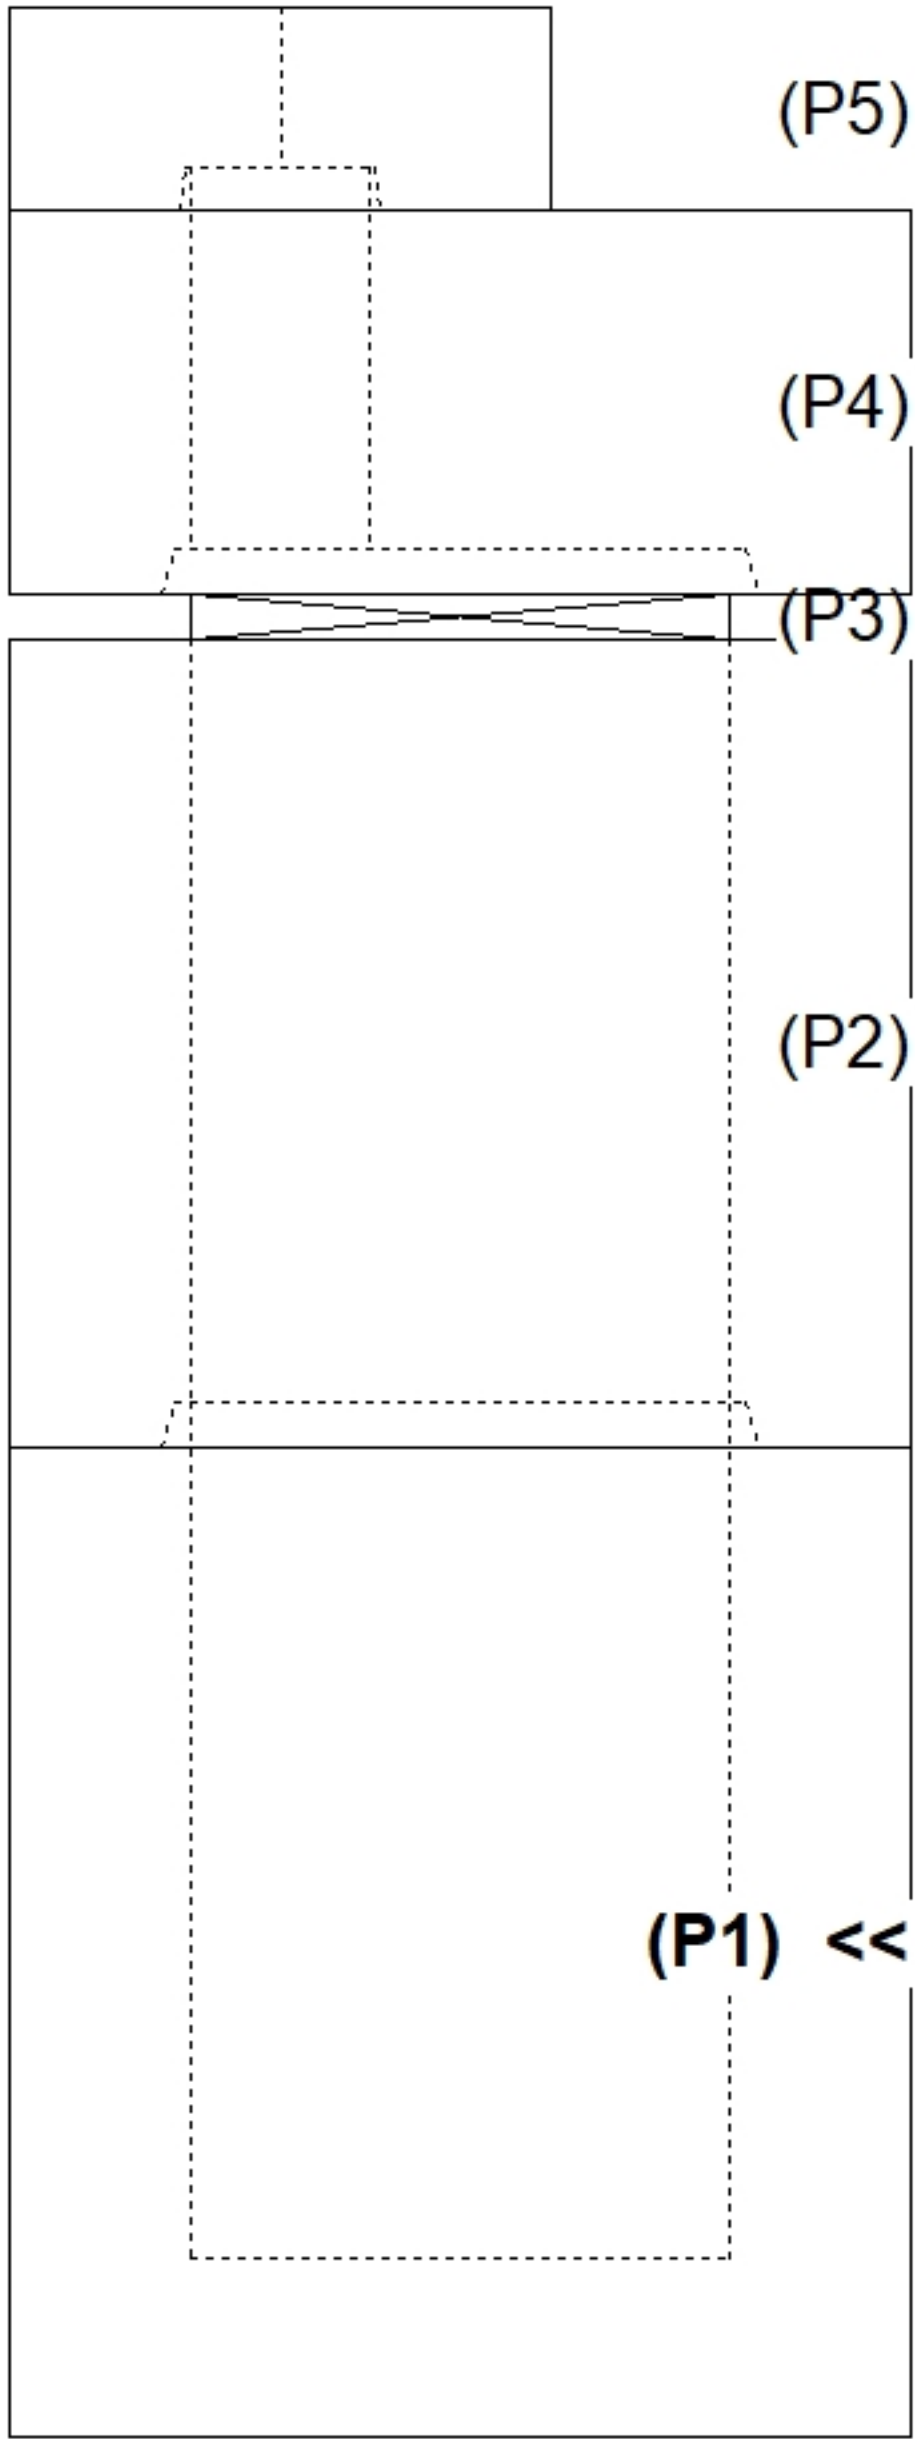
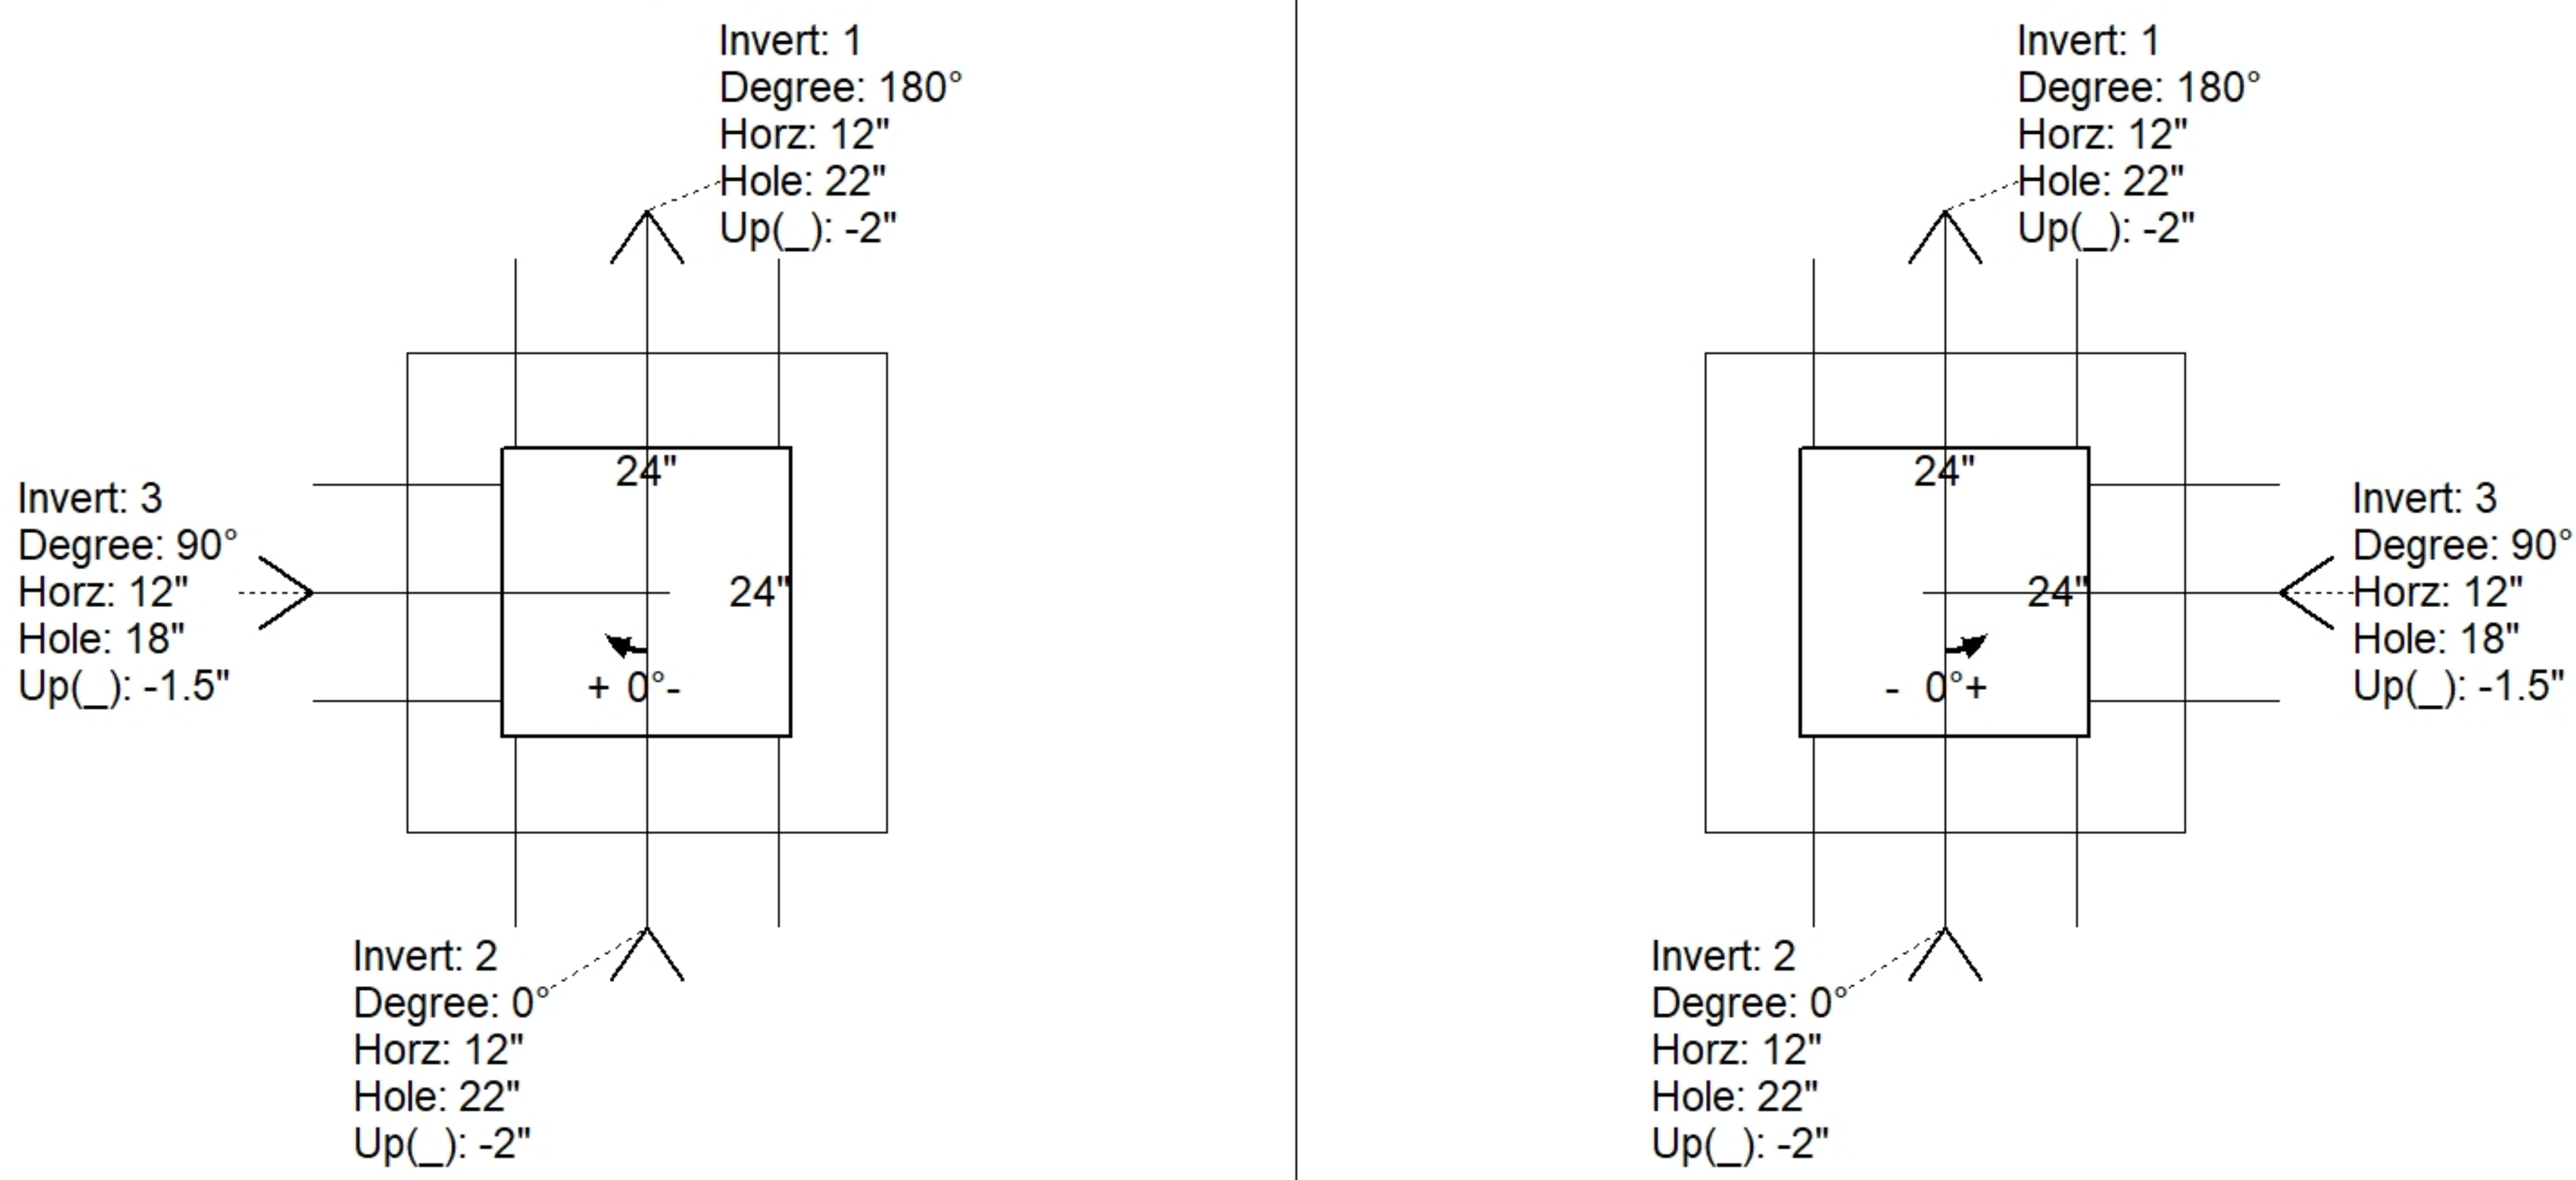
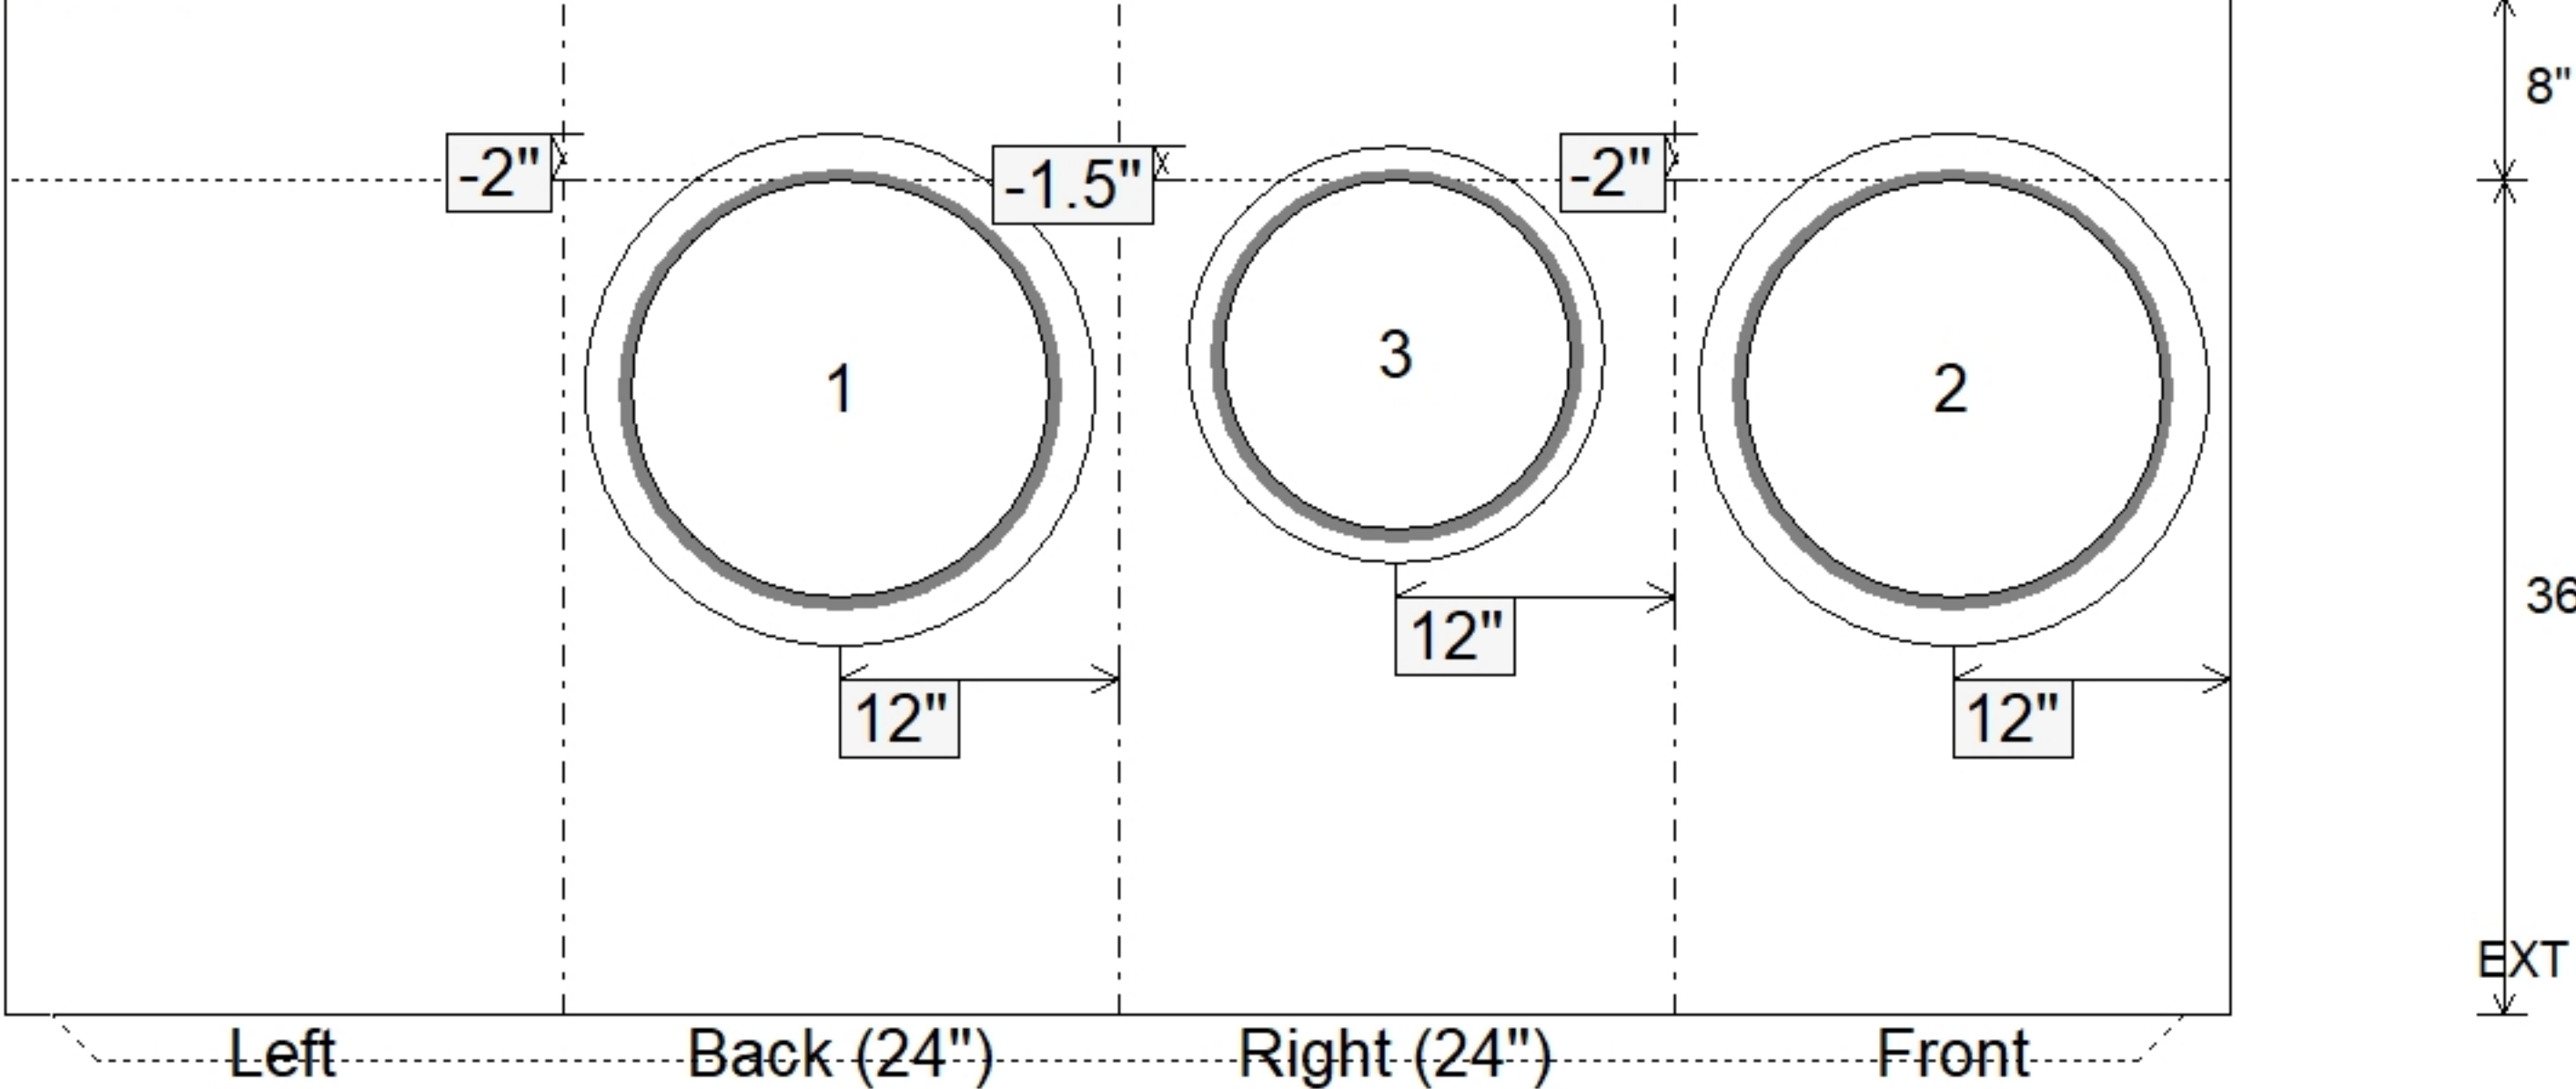


Job Name: 26-2030 - KYTC McCracken Co. Call 111 (ID 264505) Job Location: Paducah, KY Contractor: Jim Smith Contracting Co, LLC					Plant: 100 6/12/2026 7:49:41 AM		Tech: J. Horsley PC: J. Jarvis				
Structure ID: 151+22 RT S-3 CBIB											
P1		BX2424-08BA36			BOX BASE 8inW, 8inF T/n						
P5) 8" x 120" - CB INLET KY B 10' TOP F/G - 9" P4) 24" x 120" - CB INLET KY B 10' BOTTOM LEFT T/G - 17" P3) 24" x 24" - FIELD ADJUSTMENT - 2" P2) 24" x 24" - BOX RISER 8inW F/G - 36" P1) 24" x 24" - BOX BASE 8inW, 8inF T/n - 36" 1) CASTING - HOE KY-345 SET (CBI B) 2) 24" x 24" - Conseal CS-102 1.00" 2) Hole - 22 1) Hole - 18					1660 lb 2650 lb 0 lb 3093 lb 3486 lb 290 lb 0 lb 0 lb 0 lb ----- Structure Total: 11180 lb		Structure Notes: . ** KYTC STATE PROJECT ** 1. PER KYTC CBI TYPE B / ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PI AT 28 DAYS. 3. CASTING BT ICAST (HOE KY-345 F/G(CBI-B) . REINFORCING PER ASTM A615 (GRADE 60). - TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W. - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 375.16' Rim to Invert: 8.38' Slack: 0.56" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	366.78'	180°	20"	18" CMP	19"	Hole 22	22"	22"	-2"	0"	
Invert 2	366.78'	0°	20"	18" CMP	19"	Hole 22	22"	22"	-2"	0"	
Invert 3	366.78'	90°	20"	15" CMP	16"	Hole 18	18"	18"	-1.5"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions) UPSIDE-DOWN VIEW (int. dimenions) INSIDE WALL DIMENSIONS											
											
											
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 36" Height (Ext): 44"		Weight (Net): 3486 lb Volume (Net): 0.89cu.yd		
