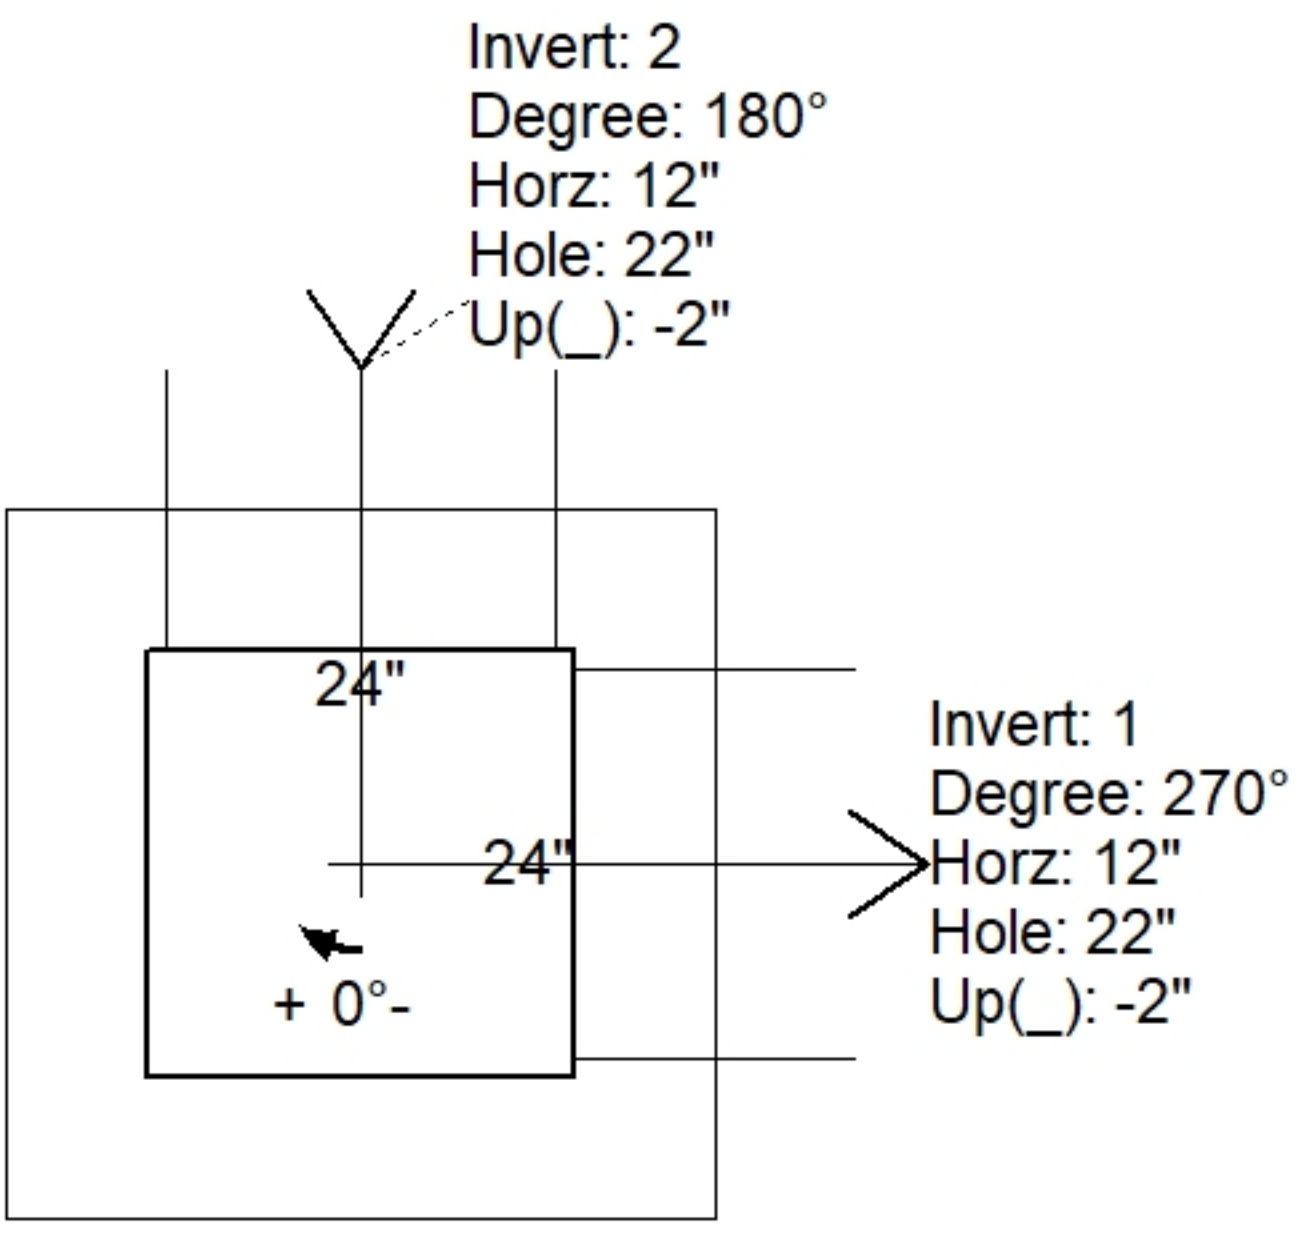
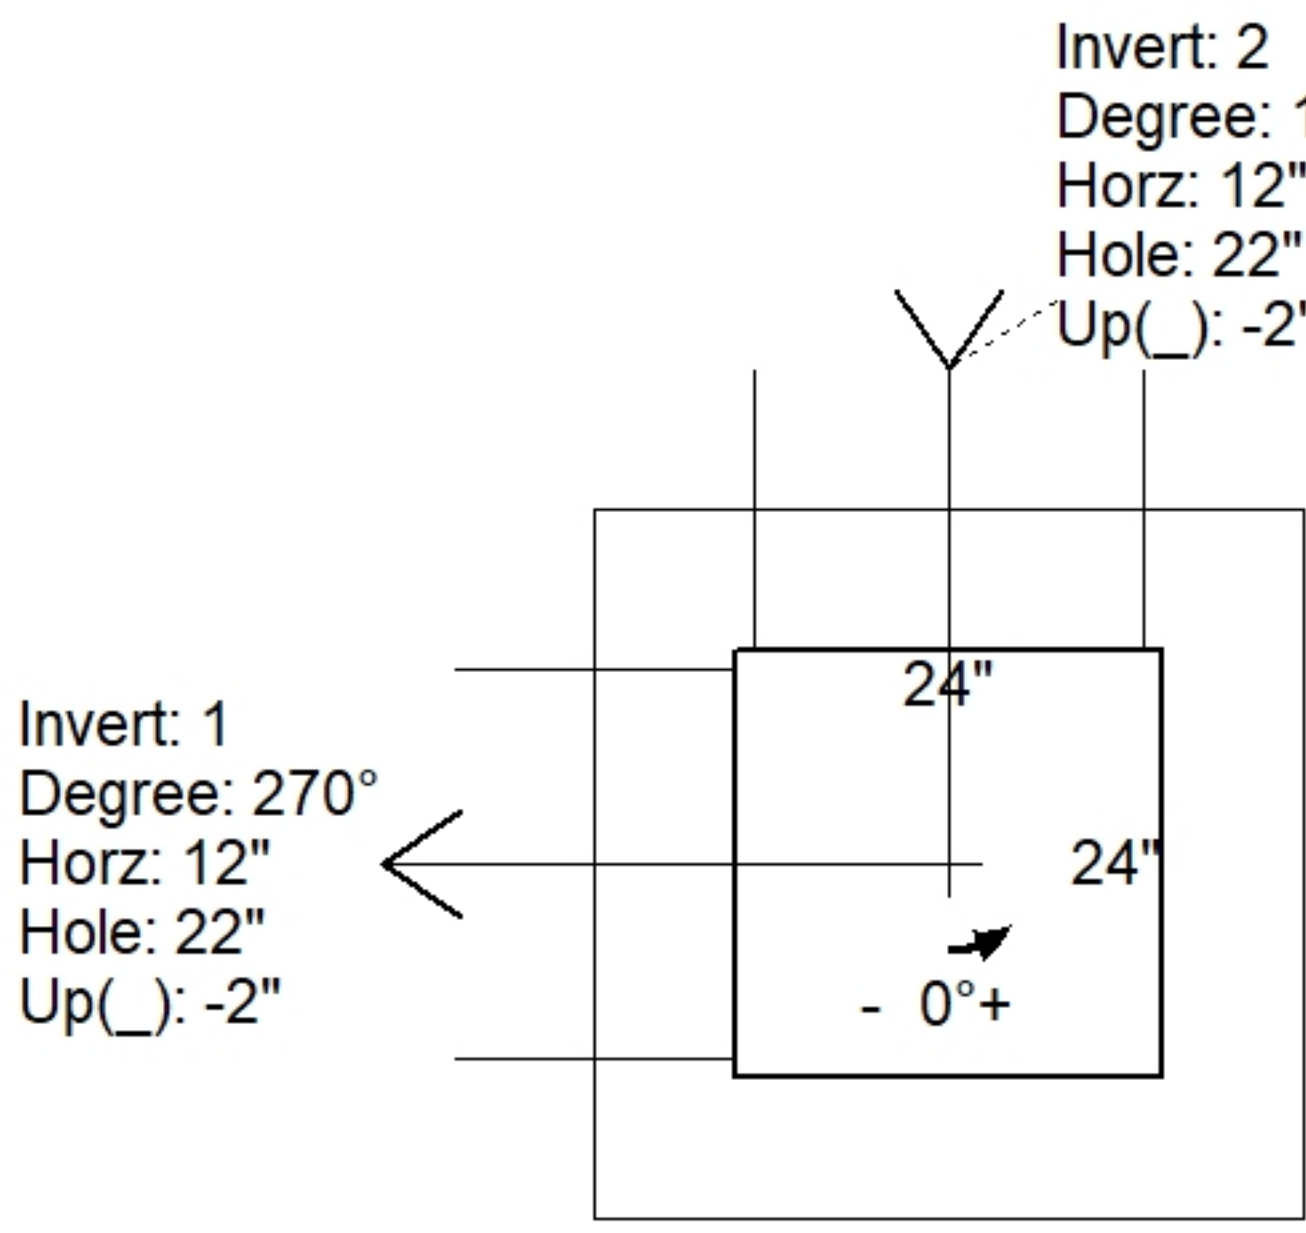
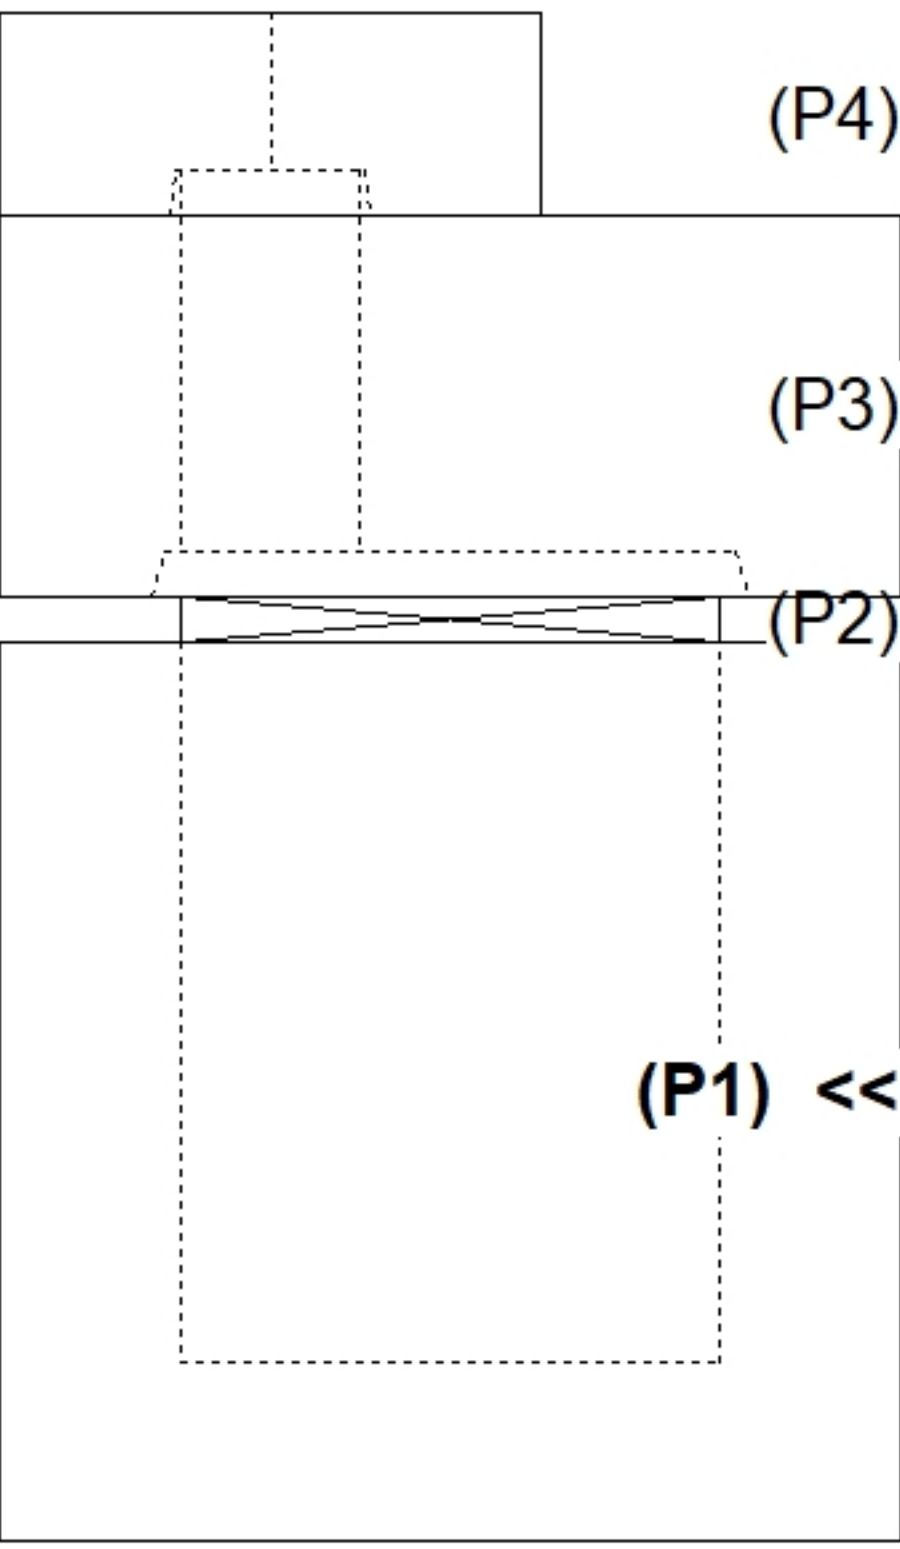
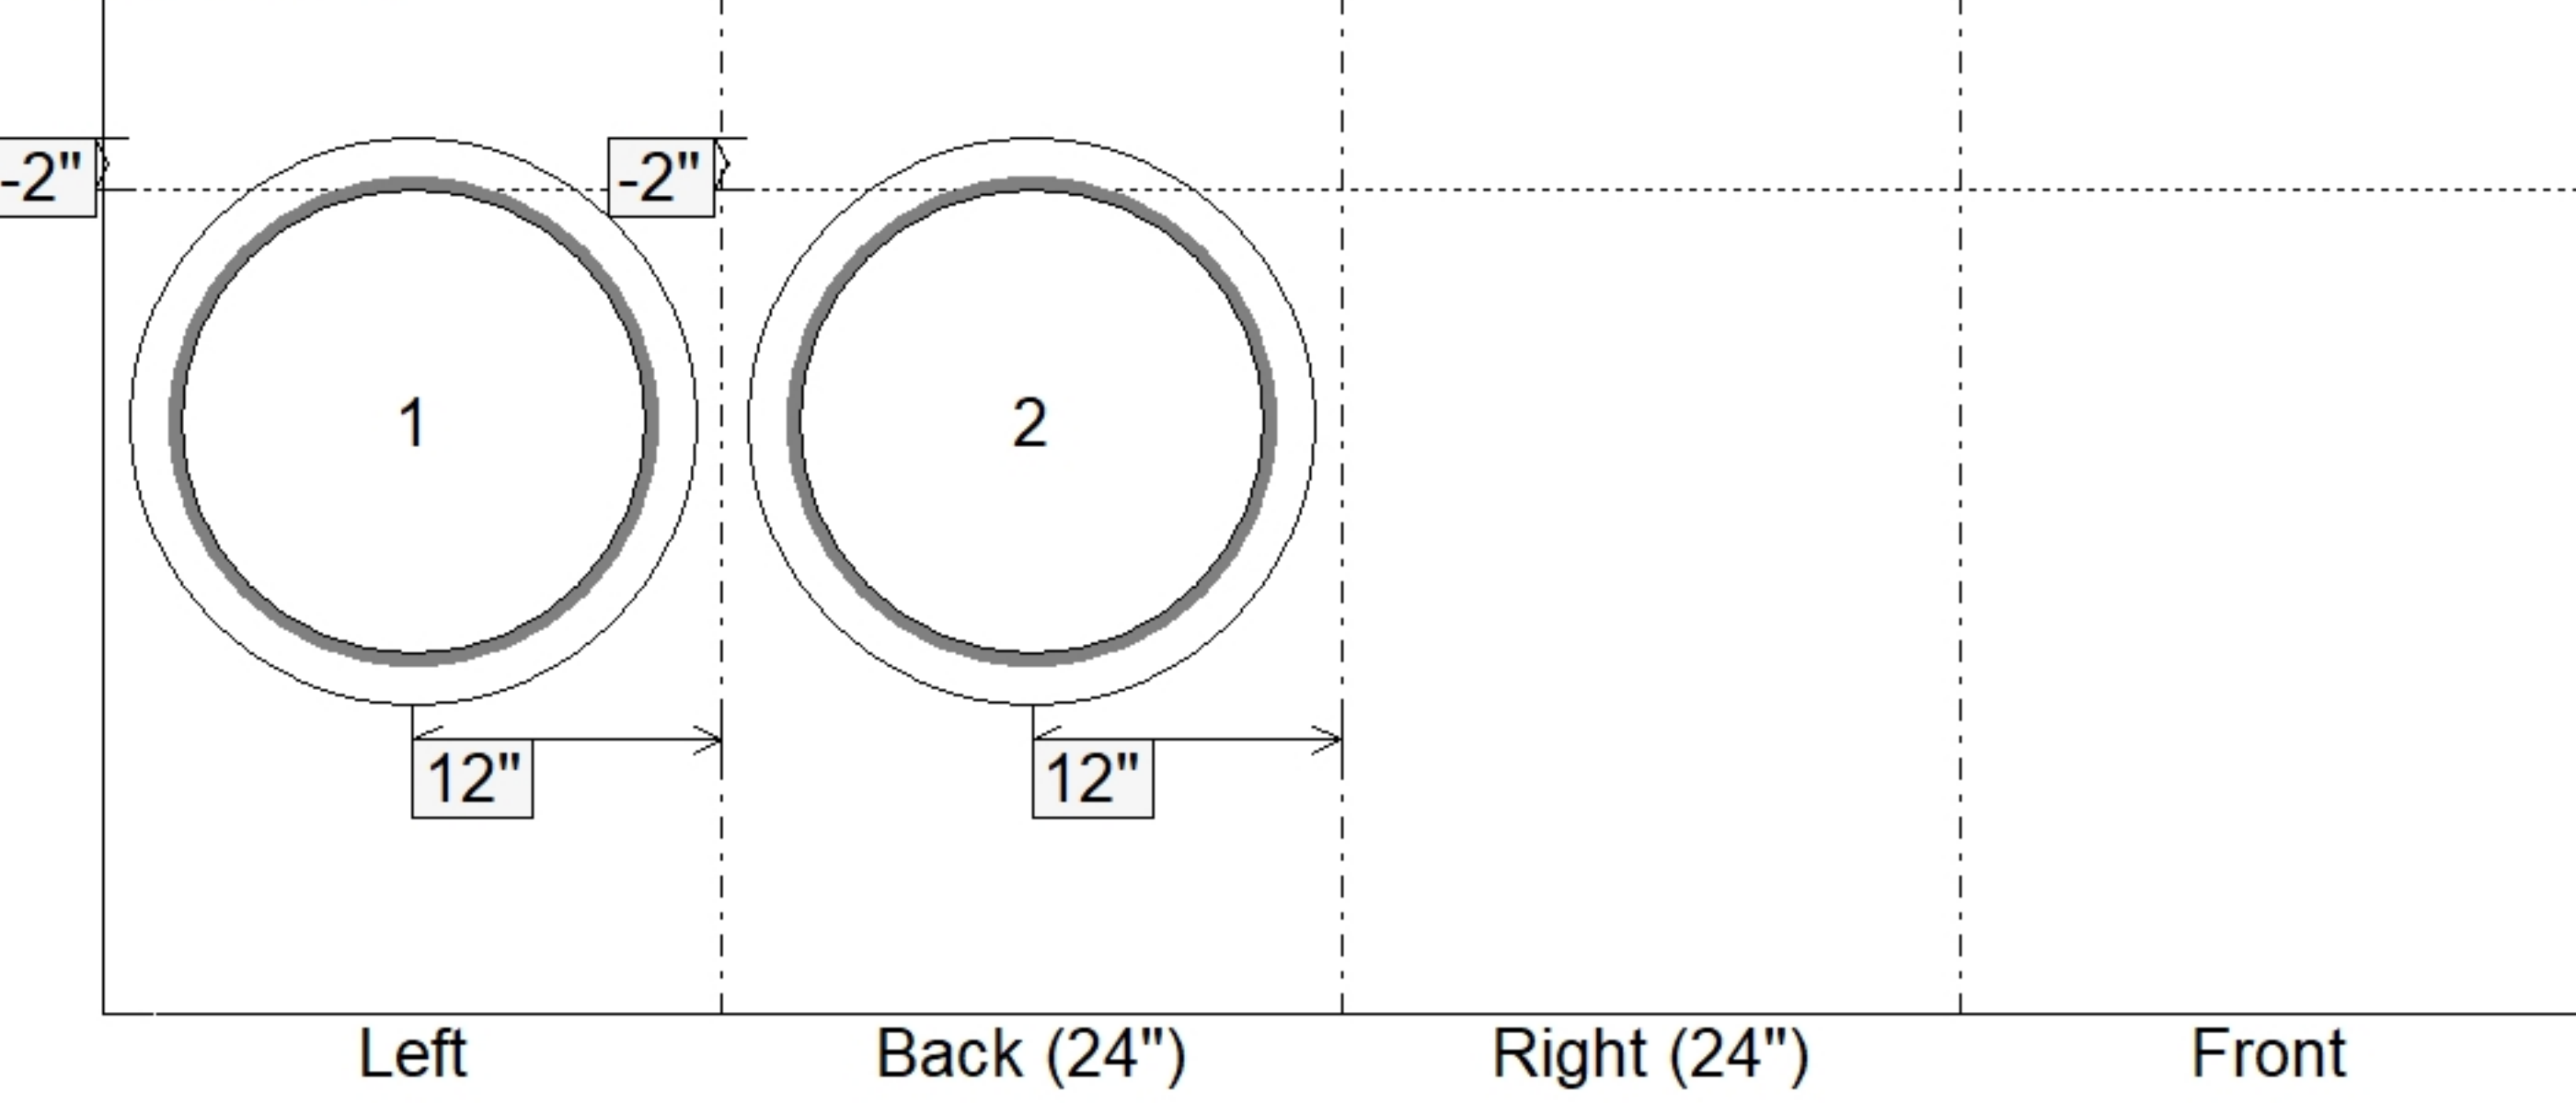


Job Name: 26-2030 - KYTC McCracken Co. Call 111 (ID 264505) Job Location: Paducah, KY Contractor: Jim Smith Contracting Co, LLC				Plant: 100 6/12/2026 7:49:43 AM		Tech: J. Horsley PC: J. Jarvis				
Structure ID: 152+51 LT S-1 CBIB										
P1		BX2424-08BAVF			BOX BASE 8inW, 8inF, Variable Ht F/n					
P4) 8" x 120" - CB INLET KY B 10' TOP F/G - 9" P3) 24" x 120" - CB INLET KY B 10' BOTTOM RIGHT T/G - 17" P2) 24" x 24" - FIELD ADJUSTMENT - 2" P1) 24" x 24" - BOX BASE 8inW, 8inF, Variable Ht F/n - 32" 1) CASTING - HOE KY-345 SET (CBI B) 1) 24" x 24" - Conseal CS-102 1.00" 2) Hole - 22					1660 lb 2650 lb 0 lb 3313 lb 290 lb 0 lb 0 lb ----- Structure Total: 7913 lb		Structure Notes: . ** KYTC STATE PROJECT ** 1. PER KYTC CBI TYPE B / ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PI AT 28 DAYS. 3. CASTING BT ICAST (HOE KY-345 F/G(CBI-B) . REINFORCING PER ASTM A615 (GRADE 60). - TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W. - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 375.64' Rim to Invert: 5.03' Slack: 0.36" Sump: 0" Step Position:										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	370.61'	270°	20"	18" CMP	19"	Hole 22	22"	22"	-2"	0"
Invert 2	370.61'	180°	20"	18" CMP	19"	Hole 22	22"	22"	-2"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										
RIGHT-SIDE UP VIEW (int. dimensions)  UPSIDE-DOWN VIEW (int. dimenions) 										
 INSIDE WALL DIMENSIONS 										
Coating (Int): Coating (Ext):			Seam Up: Flat Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 32" Height (Ext): 40"		Weight (Net): 3313 lb Volume (Net): 0.85cu.yd	
