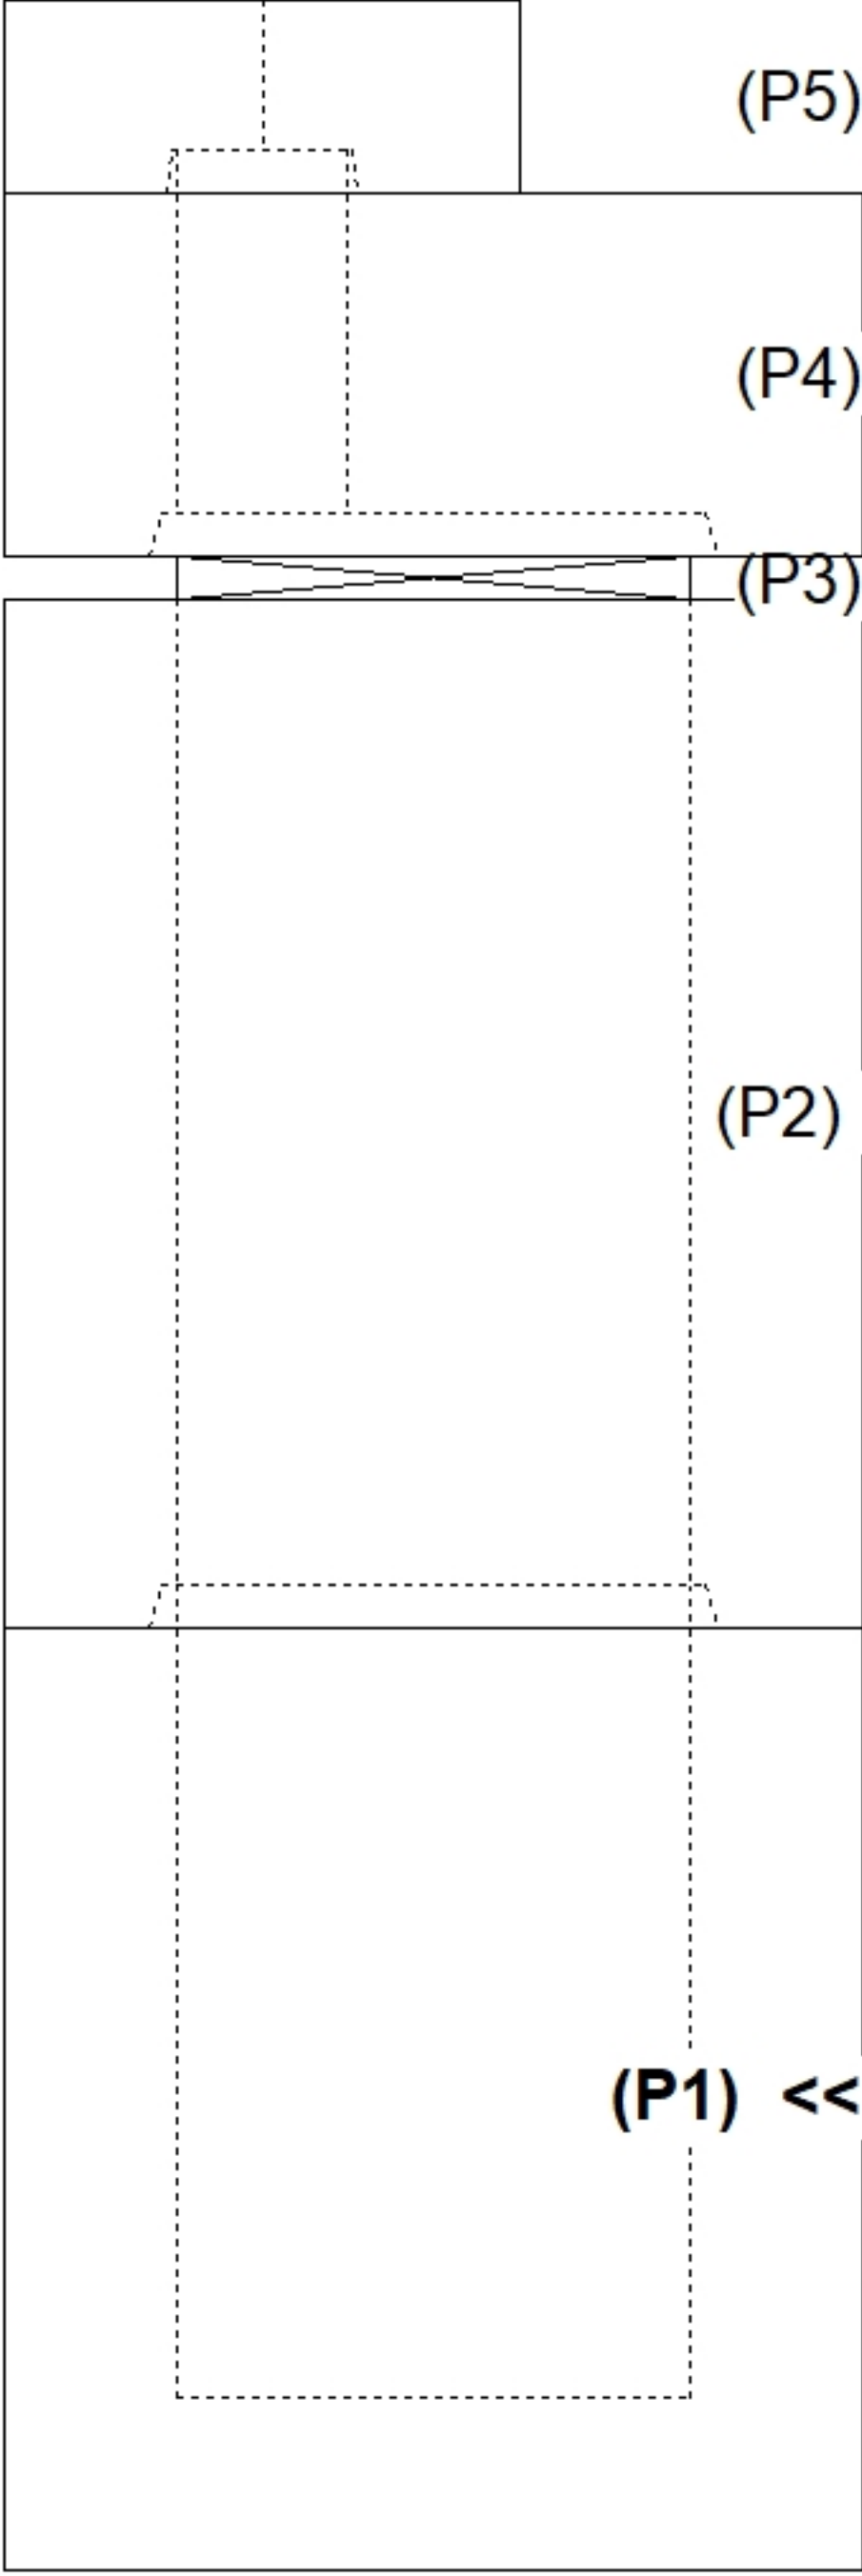
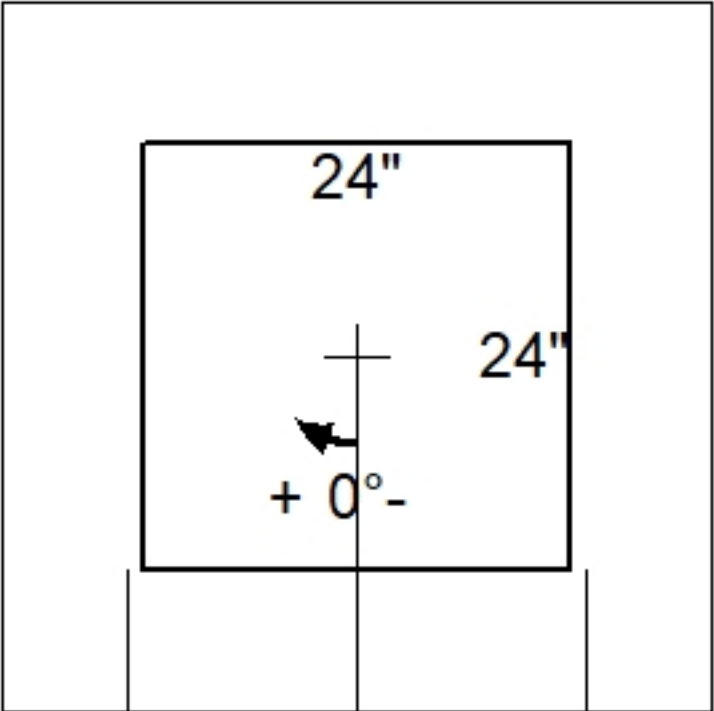
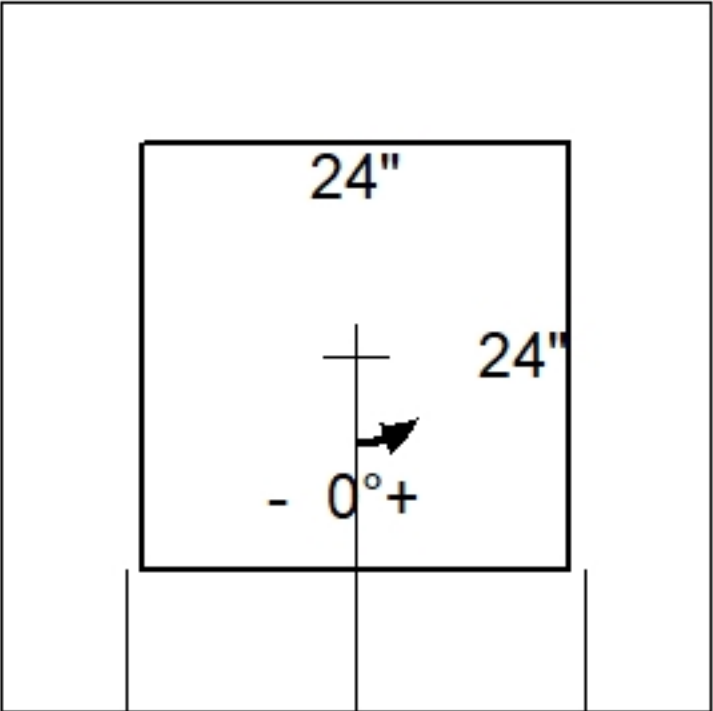
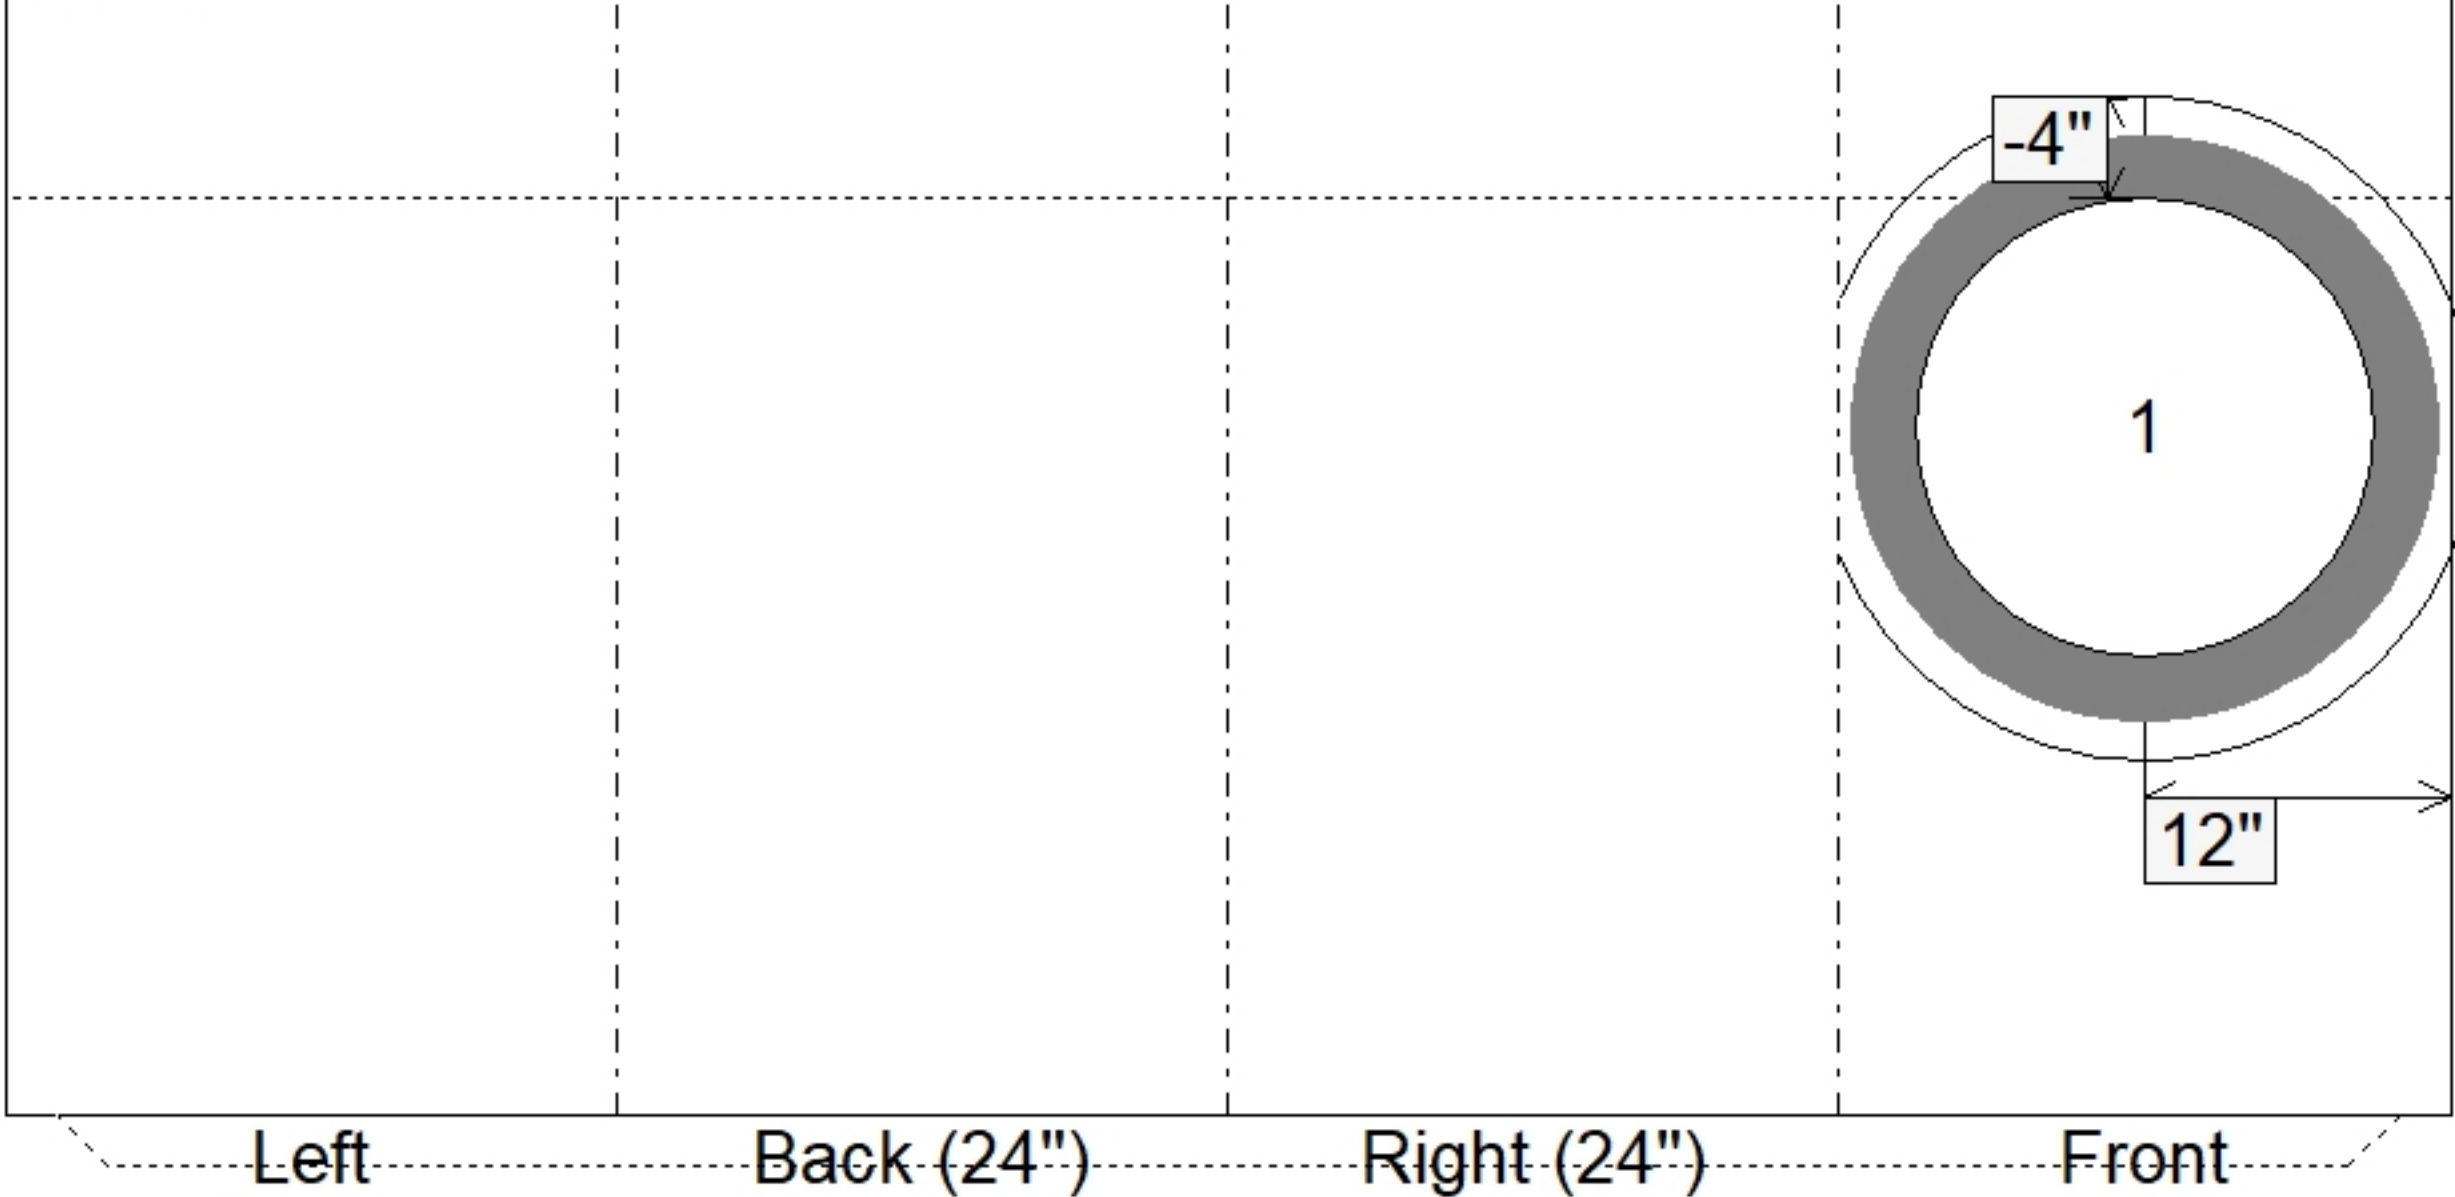


Job Name: 26-2030 - KYTC McCracken Co. Call 111 (ID 264505) Job Location: Paducah, KY Contractor: Jim Smith Contracting Co, LLC				Plant: 100 6/12/2026 7:49:42 AM		Tech: J. Horsley PC: J. Jarvis						
Structure ID: 152+51 RT S- CBIB												
P1 BX2424-08BA36				BOX BASE 8inW, 8inF T/n								
P5) 8" x 120" - CB INLET KY B 10' TOP F/G - 9" P4) 24" x 120" - CB INLET KY B 10' BOTTOM LEFT T/G - 17" P3) 24" x 24" - FIELD ADJUSTMENT - 2" P2) 24" x 24" - BOX RISER 8inW F/G - 48" P1) 24" x 24" - BOX BASE 8inW, 8inF T/n - 36" 1) CASTING - HOE KY-345 SET (CBI B) 2) 24" x 24" - Conseal CS-102 1.00" 1) Hole - 26 1) Hole - 22						1660 lb 2650 lb 0 lb 3869 lb 3900 lb 290 lb 0 lb 0 lb 0 lb ----- Structure Total: 12370 lb		Structure Notes: . ** KYTC STATE PROJECT ** 1. PER KYTC CBI TYPE B / ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PI AT 28 DAYS. 3. CASTING BT ICAST (HOE KY-345 F/G(CBI-B) . REINFORCING PER ASTM A615 (GRADE 60). - TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W. - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 375.74' Rim to Invert: 9.34' Slack: 0.08" Sump: 0" Step Position:												
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset		
Invert 1	366.4'	0°	20"	18" RCP B WALL	23"	Hole 26	26"	25"	-4"	0"		
Invert 2												
Invert 3												
Invert 4												
Invert 5												
Invert 6												
Invert 7												
Invert 8												
RIGHT-SIDE UP VIEW (int. dimensions) UPSIDE-DOWN VIEW (int. dimenions)												
  Invert: 1 Degree: 0° Horz: 12" Hole: 26" Up(-): -4"  Invert: 1 Degree: 0° Horz: 12" Hole: 26" Up(-): -4"												
INSIDE WALL DIMENSIONS 												
Coating (Int): Coating (Ext):				Seam Up: Tongue Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 36" Height (Ext): 44"		Weight (Net): 3900 lb Volume (Net): 1cu.yd		
