

Contractor: Bear Construction LLC

TECH: J. Horsley

Plant: 100



Size: 28" x 28"

Rim to Invert: 2.7'


Floor Height: 6"

Slack: 0.396"

REINFORCING PER ASTM A615 (GRADE 60).
- WALLS (As .31) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

1) Hole - 26



Structure Total: 3456 lb

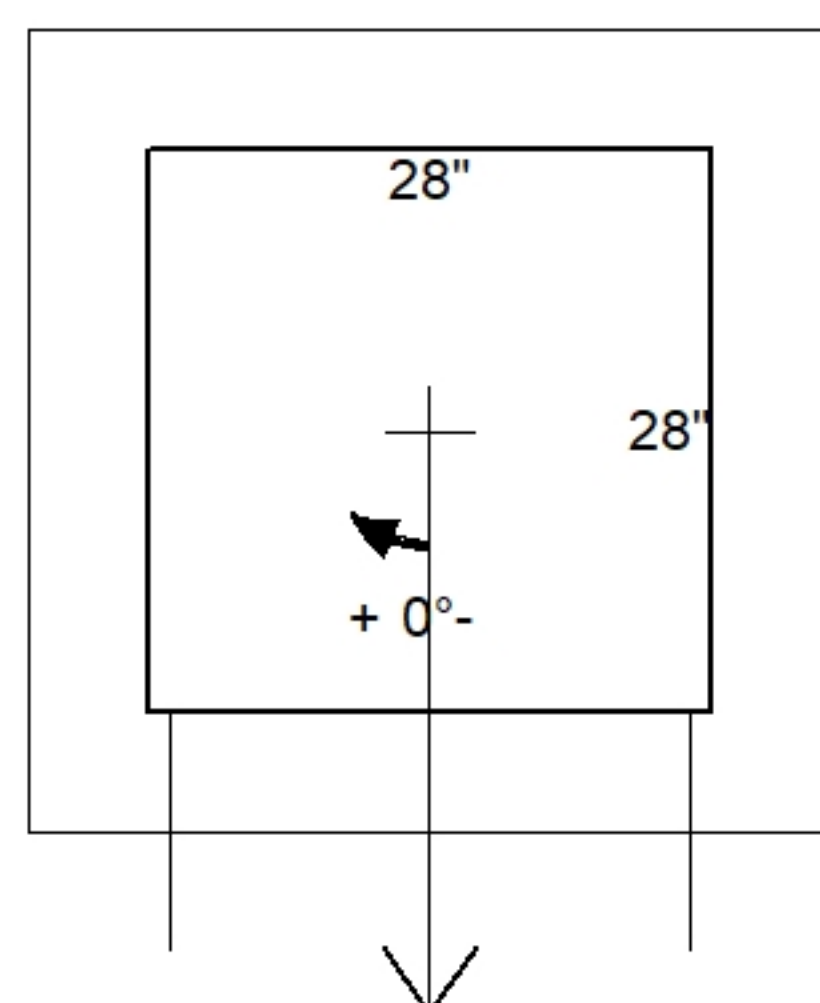

Invert: 1
Degree: 0°

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (⌵)	Ref
Rim	529.29'							
Reducer								
Invert 1	526.59'	0°	18" RCP B WALL	23"	26"	Hole 26	0"	P1
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Cast (Int. Dim.) - Interior Dimensions

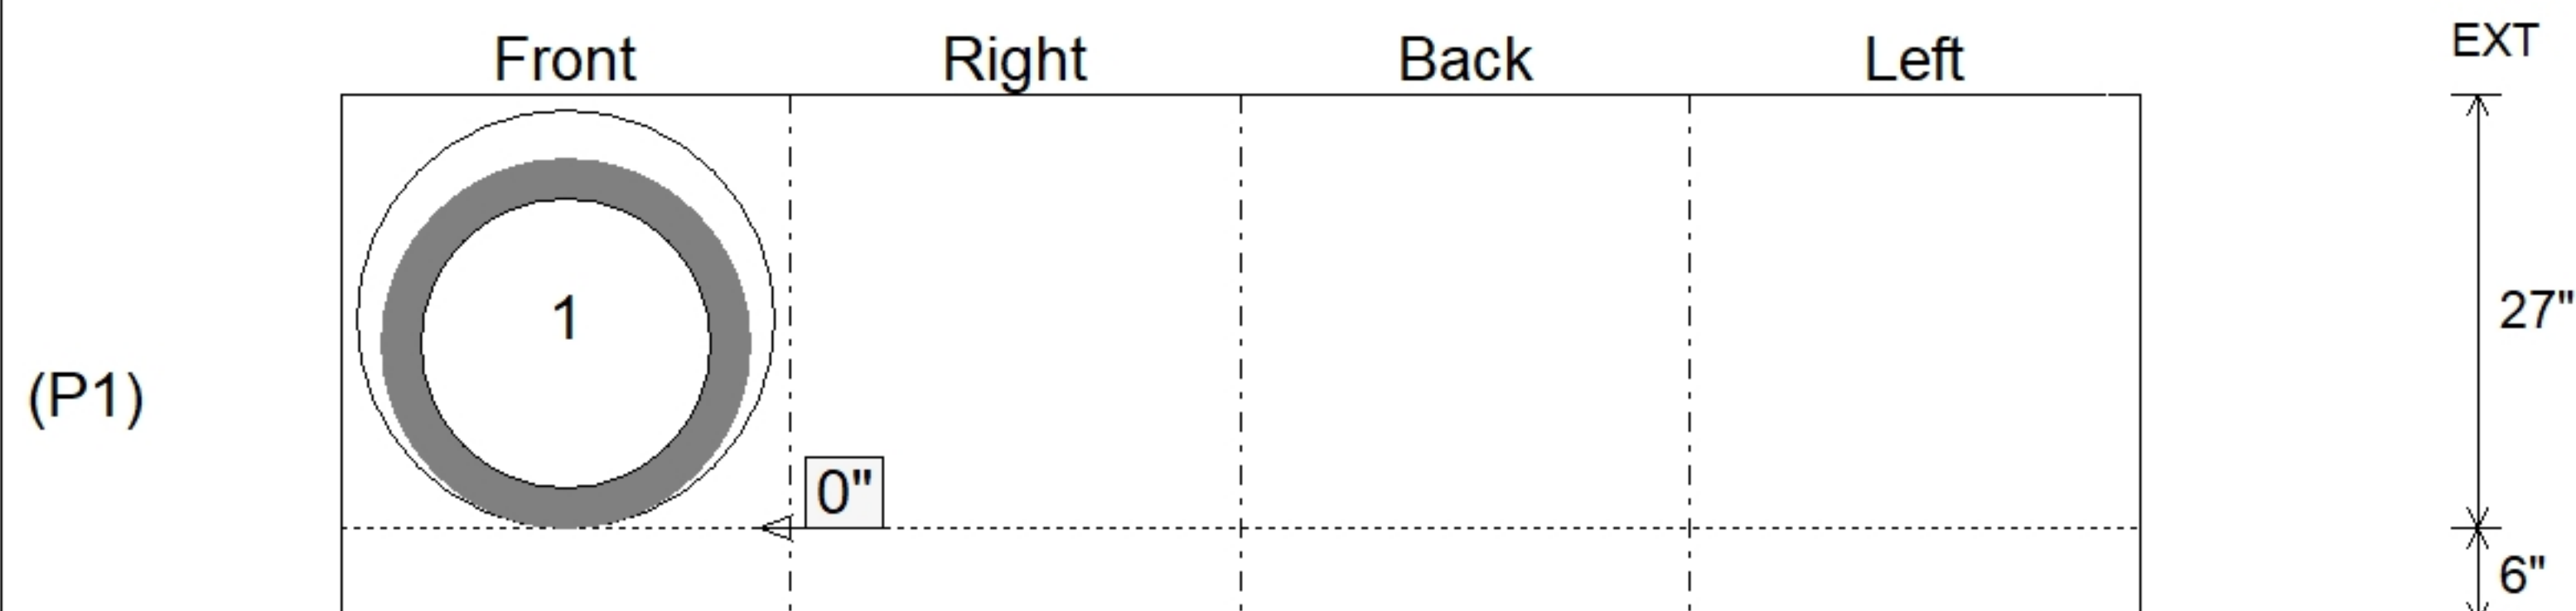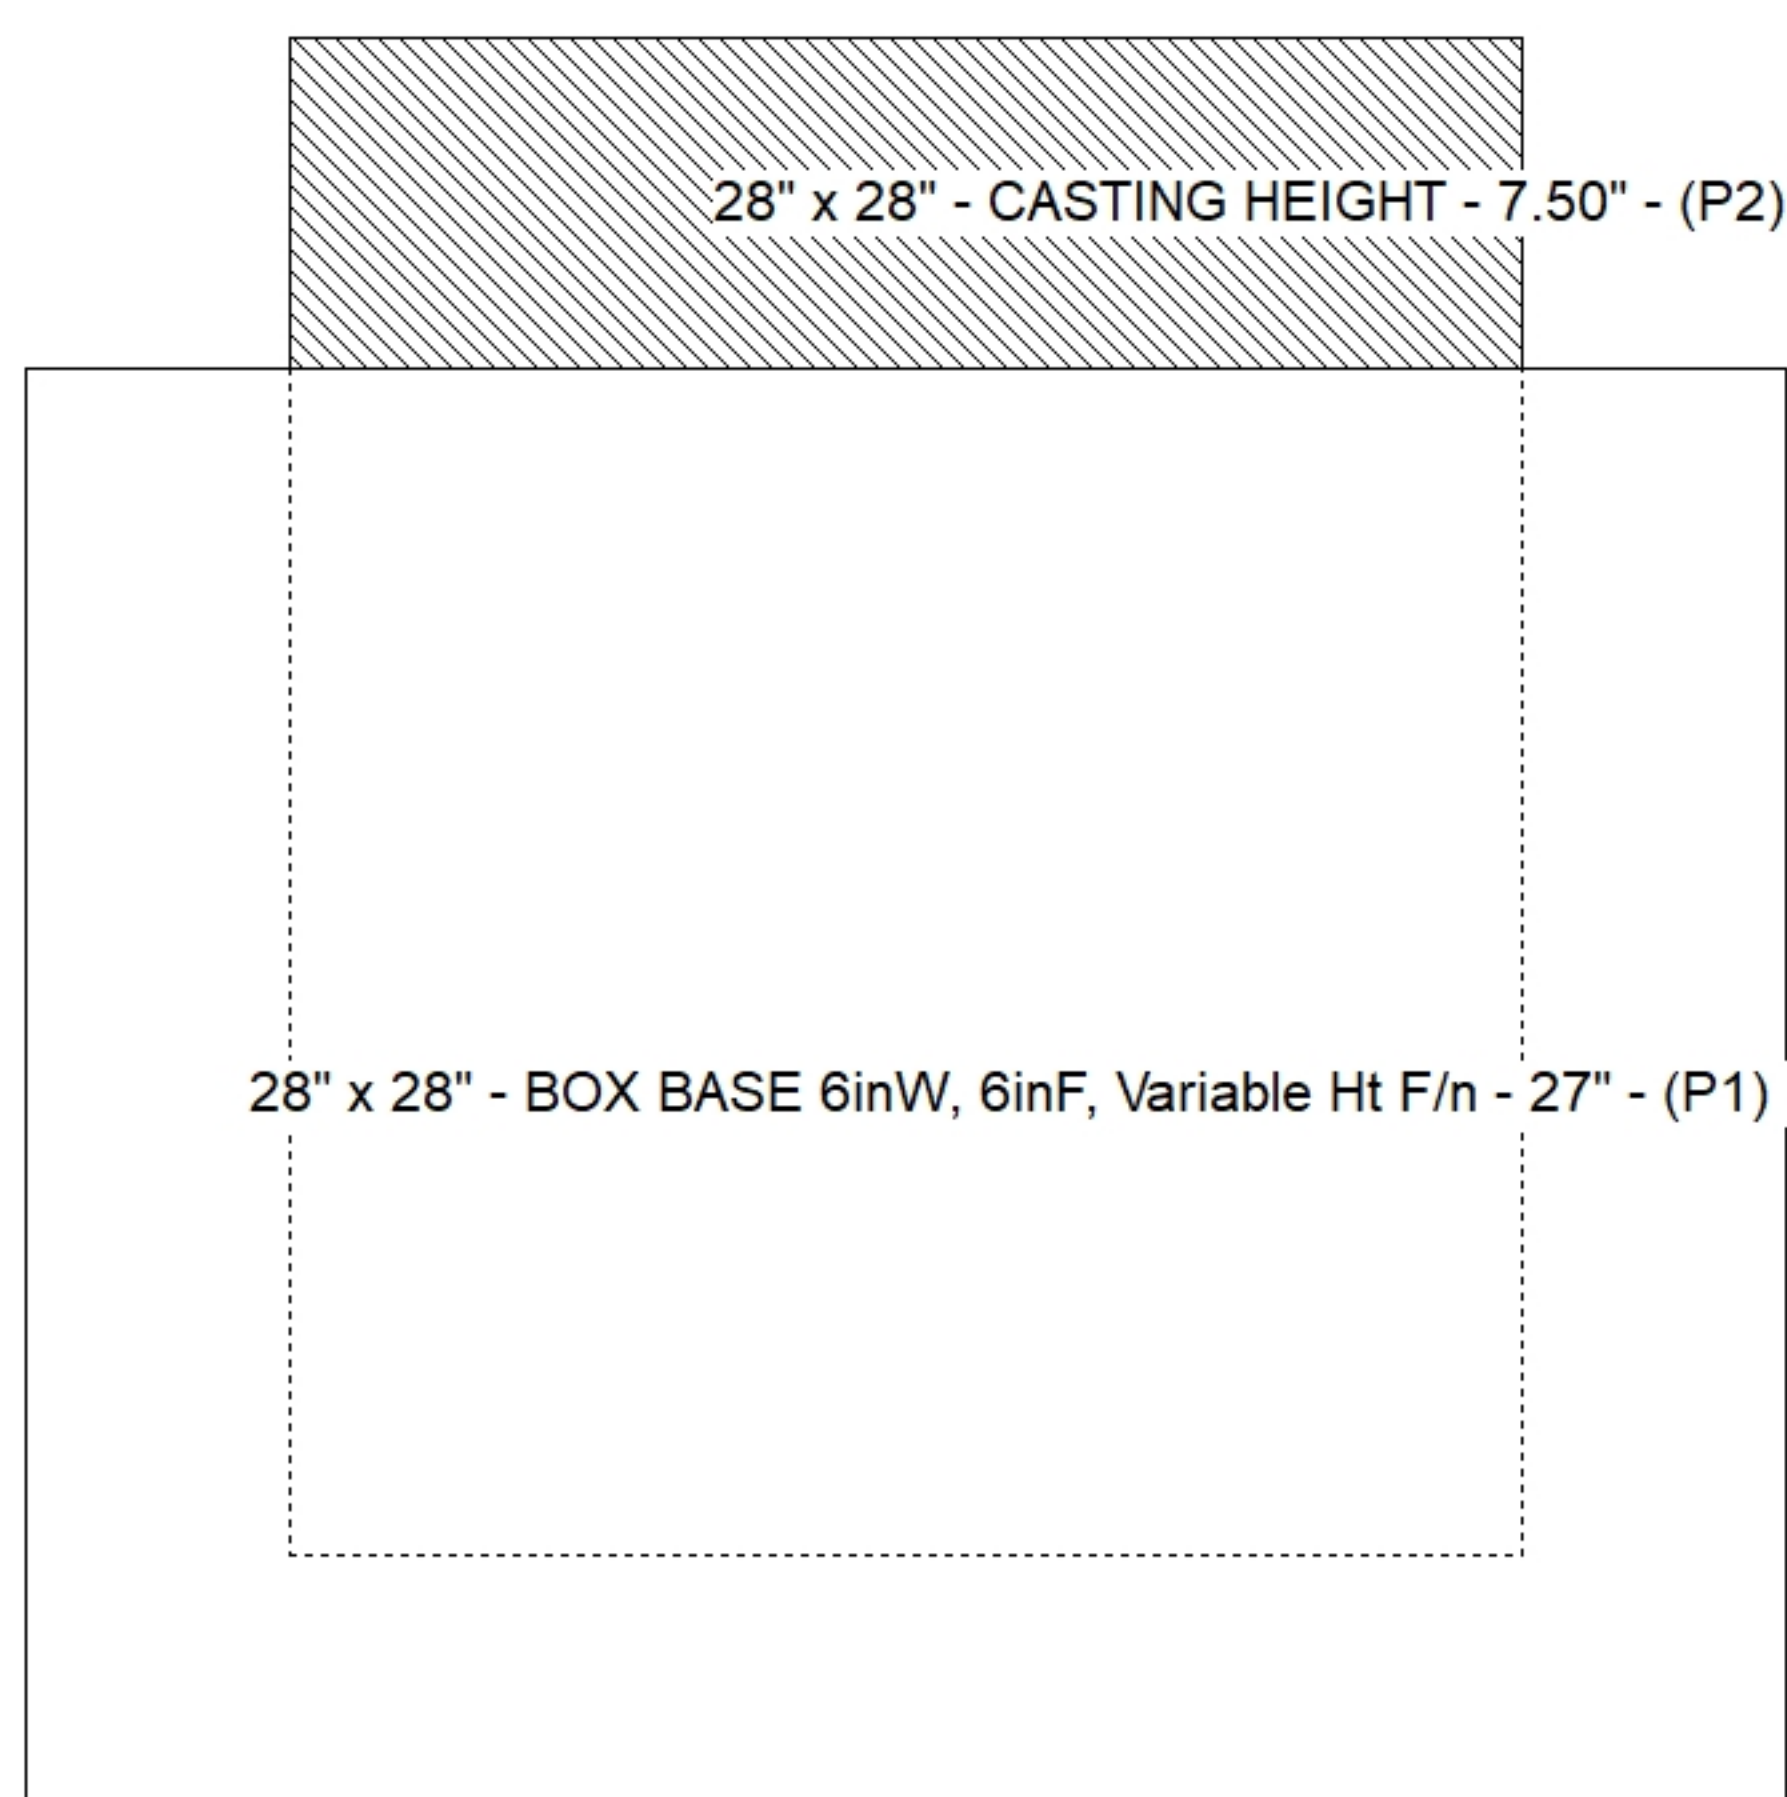

SUBMITTAL
APPROVED BY:
