



Job Name: 26-2153 - Southwire Material Hawesville Job Location: Hawesville, KY Contractor: Hodskins Services				Plant: 100 6/19/2026 6:35:46 PM		Tech: Jared - F PC: E. Bradley					
Structure ID: DBI 395.50											
P2		MH048RSVF		MH RISER Custom Ht F/G							
P4) 34" x 34" - CASTING HEIGHT - 7" P3) 48" - MH FLAT TOP w/34"x34" Hole F/F - 7" P2) 48" - MH RISER Custom Ht F/G - 58" P1) 48" - MH BASE Custom Ht T/n - 41" 1) CASTING - NEENAH R-3481 (F/G) 2) 48" - Conseal CS-102 1.00" 1) Hole - 32 1) DOGHOUSE INVRTD - 34"x30" 1) Hole - 18 8) MH Step ML-10-TDS-NCR - 10"				0 lb 873 lb 3596 lb 3722 lb 294 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 8485 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (NEENAH R-3481 (F/G)). REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.					
Rim: 404.7'				Rim to Invert: 9.2'		Slack: 0.4"		Sump: 3"		Step Position: 285°	
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1											
Invert 2	401.04'	145°	73.375"	24" RCP B WALL	30"	DOGHOUSE INVRTD 34"x30"	34" x 30"	37.782"	21.25"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

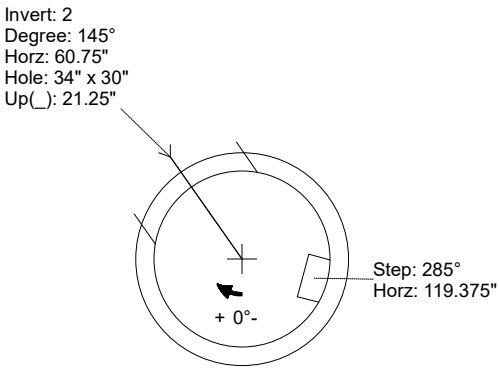

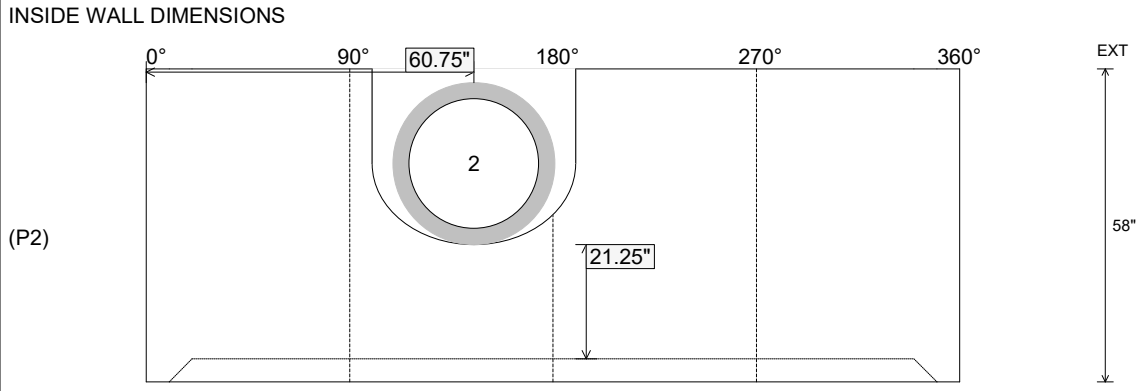

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5" Floor Height: 0"	Height (Int): 58" Height (Ext): 58"	Weight (Net): 3596 lb Volume (Net): 0.92cu.yd
----------------------------------	----------------------------------	--	--	--
