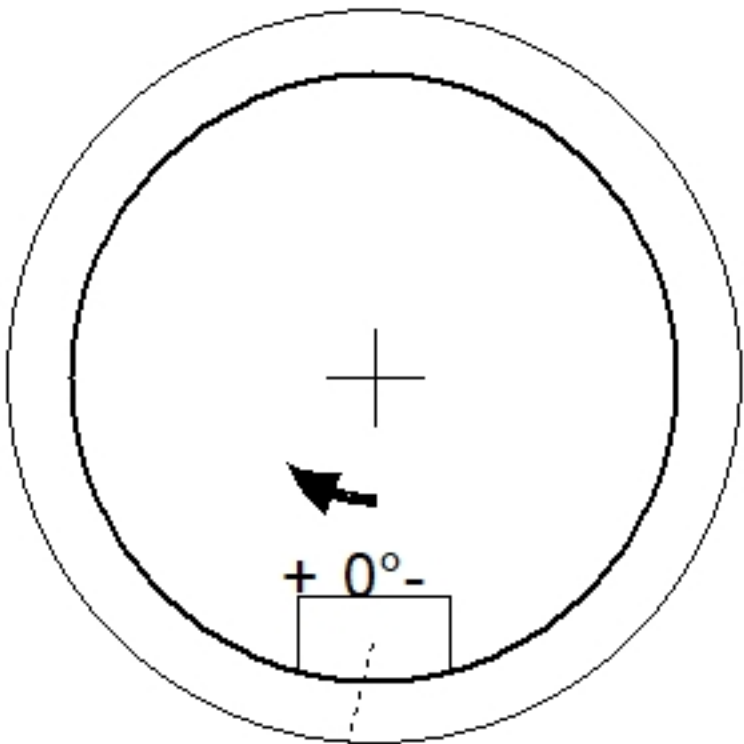


Job Name: 26-2171 - Lake Malone Campground Multi Park West					Plant: 100		Tech: Jared - F				
Job Location: Lewisburg, KY					6/19/2026 8:25:33 AM		PC: M. Sullivan				
Contractor: Sensabaugh Design & Construction, LLC											
Structure ID: SSMH-E1											
P1 P.I.P. BY OTHERS - BTM SLAB											
P4) 24" - CASTING HEIGHT - 7" P3) 48" - ECC CONE w/ 24" HOLE - 36" P2) 48" - MH RISER Custom Ht - 70" P1) 48" - P.I.P. BY OTHERS - BTM SLAB - 0" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-315 F/C Sanitary 2) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) DOGHOUSE - 12"x18" 1) PSX - 8QRS-S NYLO 1) PSX - 12-06 NYLO 9) MH Step ML-10-TDS-NCR - 10"					0 lb 3000 lb 4637 lb 0 lb 0 lb 0 lb 1440 lb 258 lb 0 lb 0 lb 0 lb 6 lb 8 lb 0 lb ----- Structure Total: 9350 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING SUPPLIED BY ICAST (HOE MC-315 F/C "SANITARY"). . REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12)				
Rim: 567.82' Rim to Invert: 8.87' Slack: 1.44" Sump: 8" Step Position: 0°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
(P4) (P3) (P2) (P1) << RIGHT-SIDE UP VIEW (int. dimensions)  Step: 0° Horz: 0" UPSIDE-DOWN VIEW (int. dimenions) INSIDE WALL DIMENSIONS (P1) 0° 90° 180° 270° 360° EXT X0"											
Coating (Int): Coating (Ext):			Seam Up: Flat Seam Dn: n/a		Wall Thickness: 5" Floor Height: 0"		Height (Int): 0" Height (Ext): 0"		Weight (Net): 0 lb Volume (Net): 0cu.yd		
