

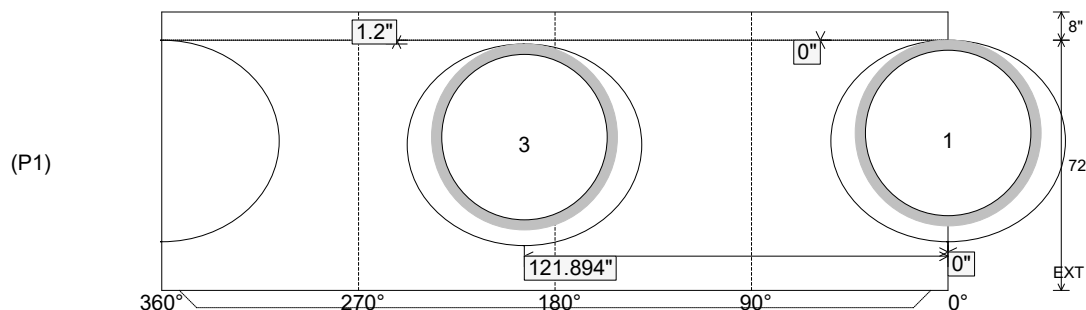
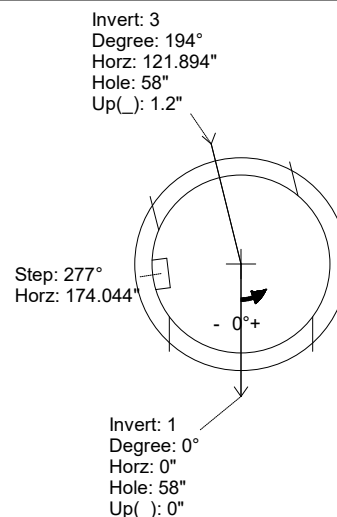
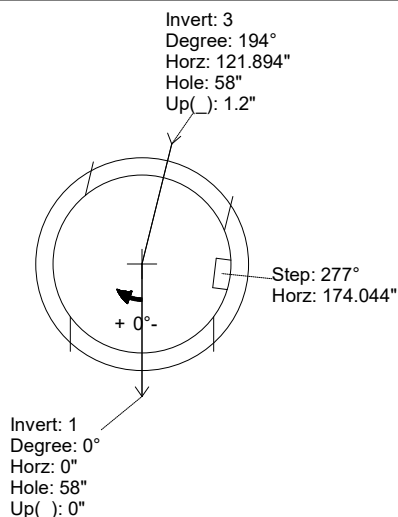
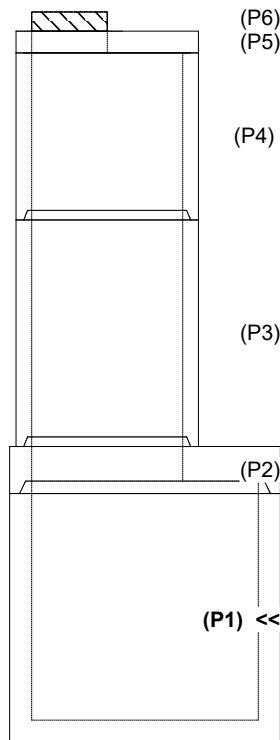
Plant: Beaver Dam

8/18/2026 12:38:47 PM

0 lb
1214 lb
3254 lb
5030 lb
3864 lb
10888 lb
0 lb
0 lb
0 lb
0 lb
0 lb
0 lb

****INDOT STATE PROJECT****

1. (NEENAH R-3405 PROVIDED BY OTHERS)
2. INDOT MH TYPE K / ASTM C478 SPEC'S.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. NO INVERT CHANNEL.
5. REINFORCING PER ASTM A615 (GRADE 60).
 - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
 - RISER/WALLS (As .12)
 - FLOOR (As .62) #5 BARS AT 6" C.C.E.W.

[illegible]

Weight (Net): 10888 lb
Volume (Net): 2.78cu.yd
