

Contractor: Core & Main LP

Plant: Beaver Dam, KY




Slack: 2.46"

1. PER ASTM C-913 SPECIFICATIONS
2. CONCRETE: 4,000 PSI AT 28 DAYS
3. REINFORCEMENT: #5 BAR @ 12" C.C. E.W. (GRADE 60)
4. NO STEPS & NO INVERT CHANNEL
5. 6.5" CASTING SUPPLIED BY OTHERS


P2) 24" x 36" - CASTING HEIGHT - 6.5"
P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 43"
1) 24" x 36" - Conseal CS-102 1.00"
1) Hole - 24
1) Hole - 20

0 lb
5269 lb
0 lb
0 lb
0 lb


Structure Total: 5269 lb

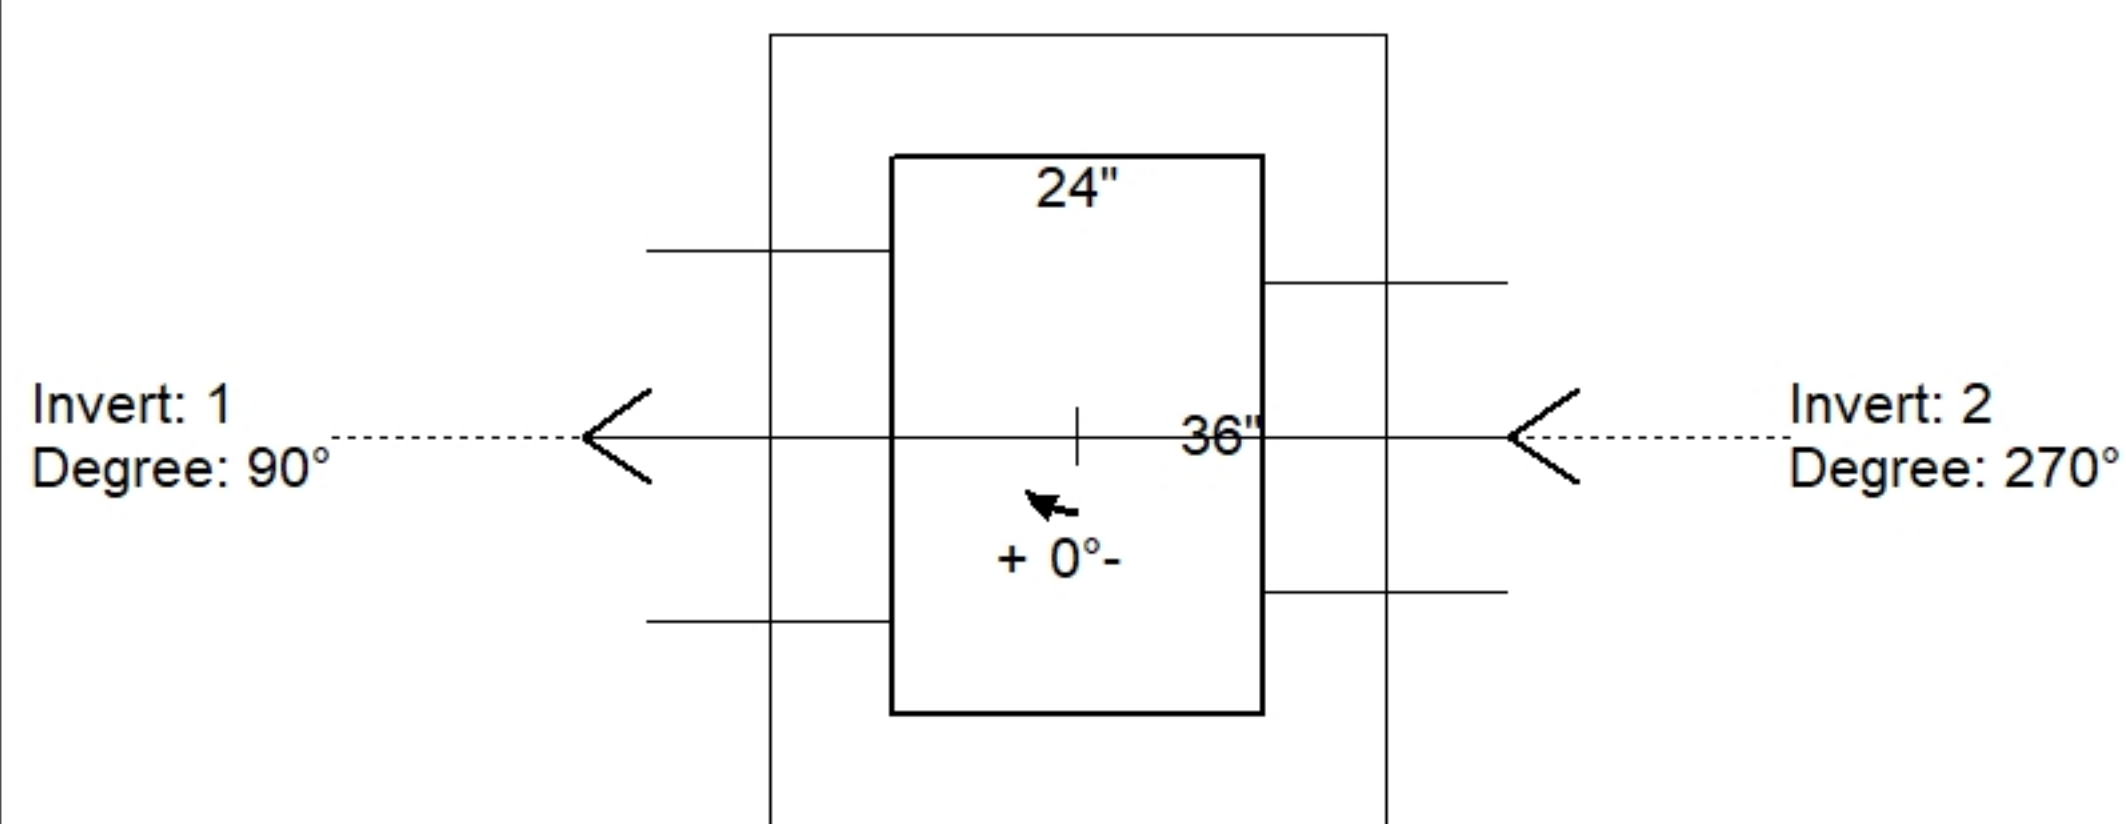

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	513.15'							
Reducer								
Invert 1	508.82'	90°	18" HDPE	21.2"	24"	Hole 24	-1.6"	P1
Invert 2	508.82'	270°	15" HDPE	17.6"	20"	Hole 20	-1.3"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

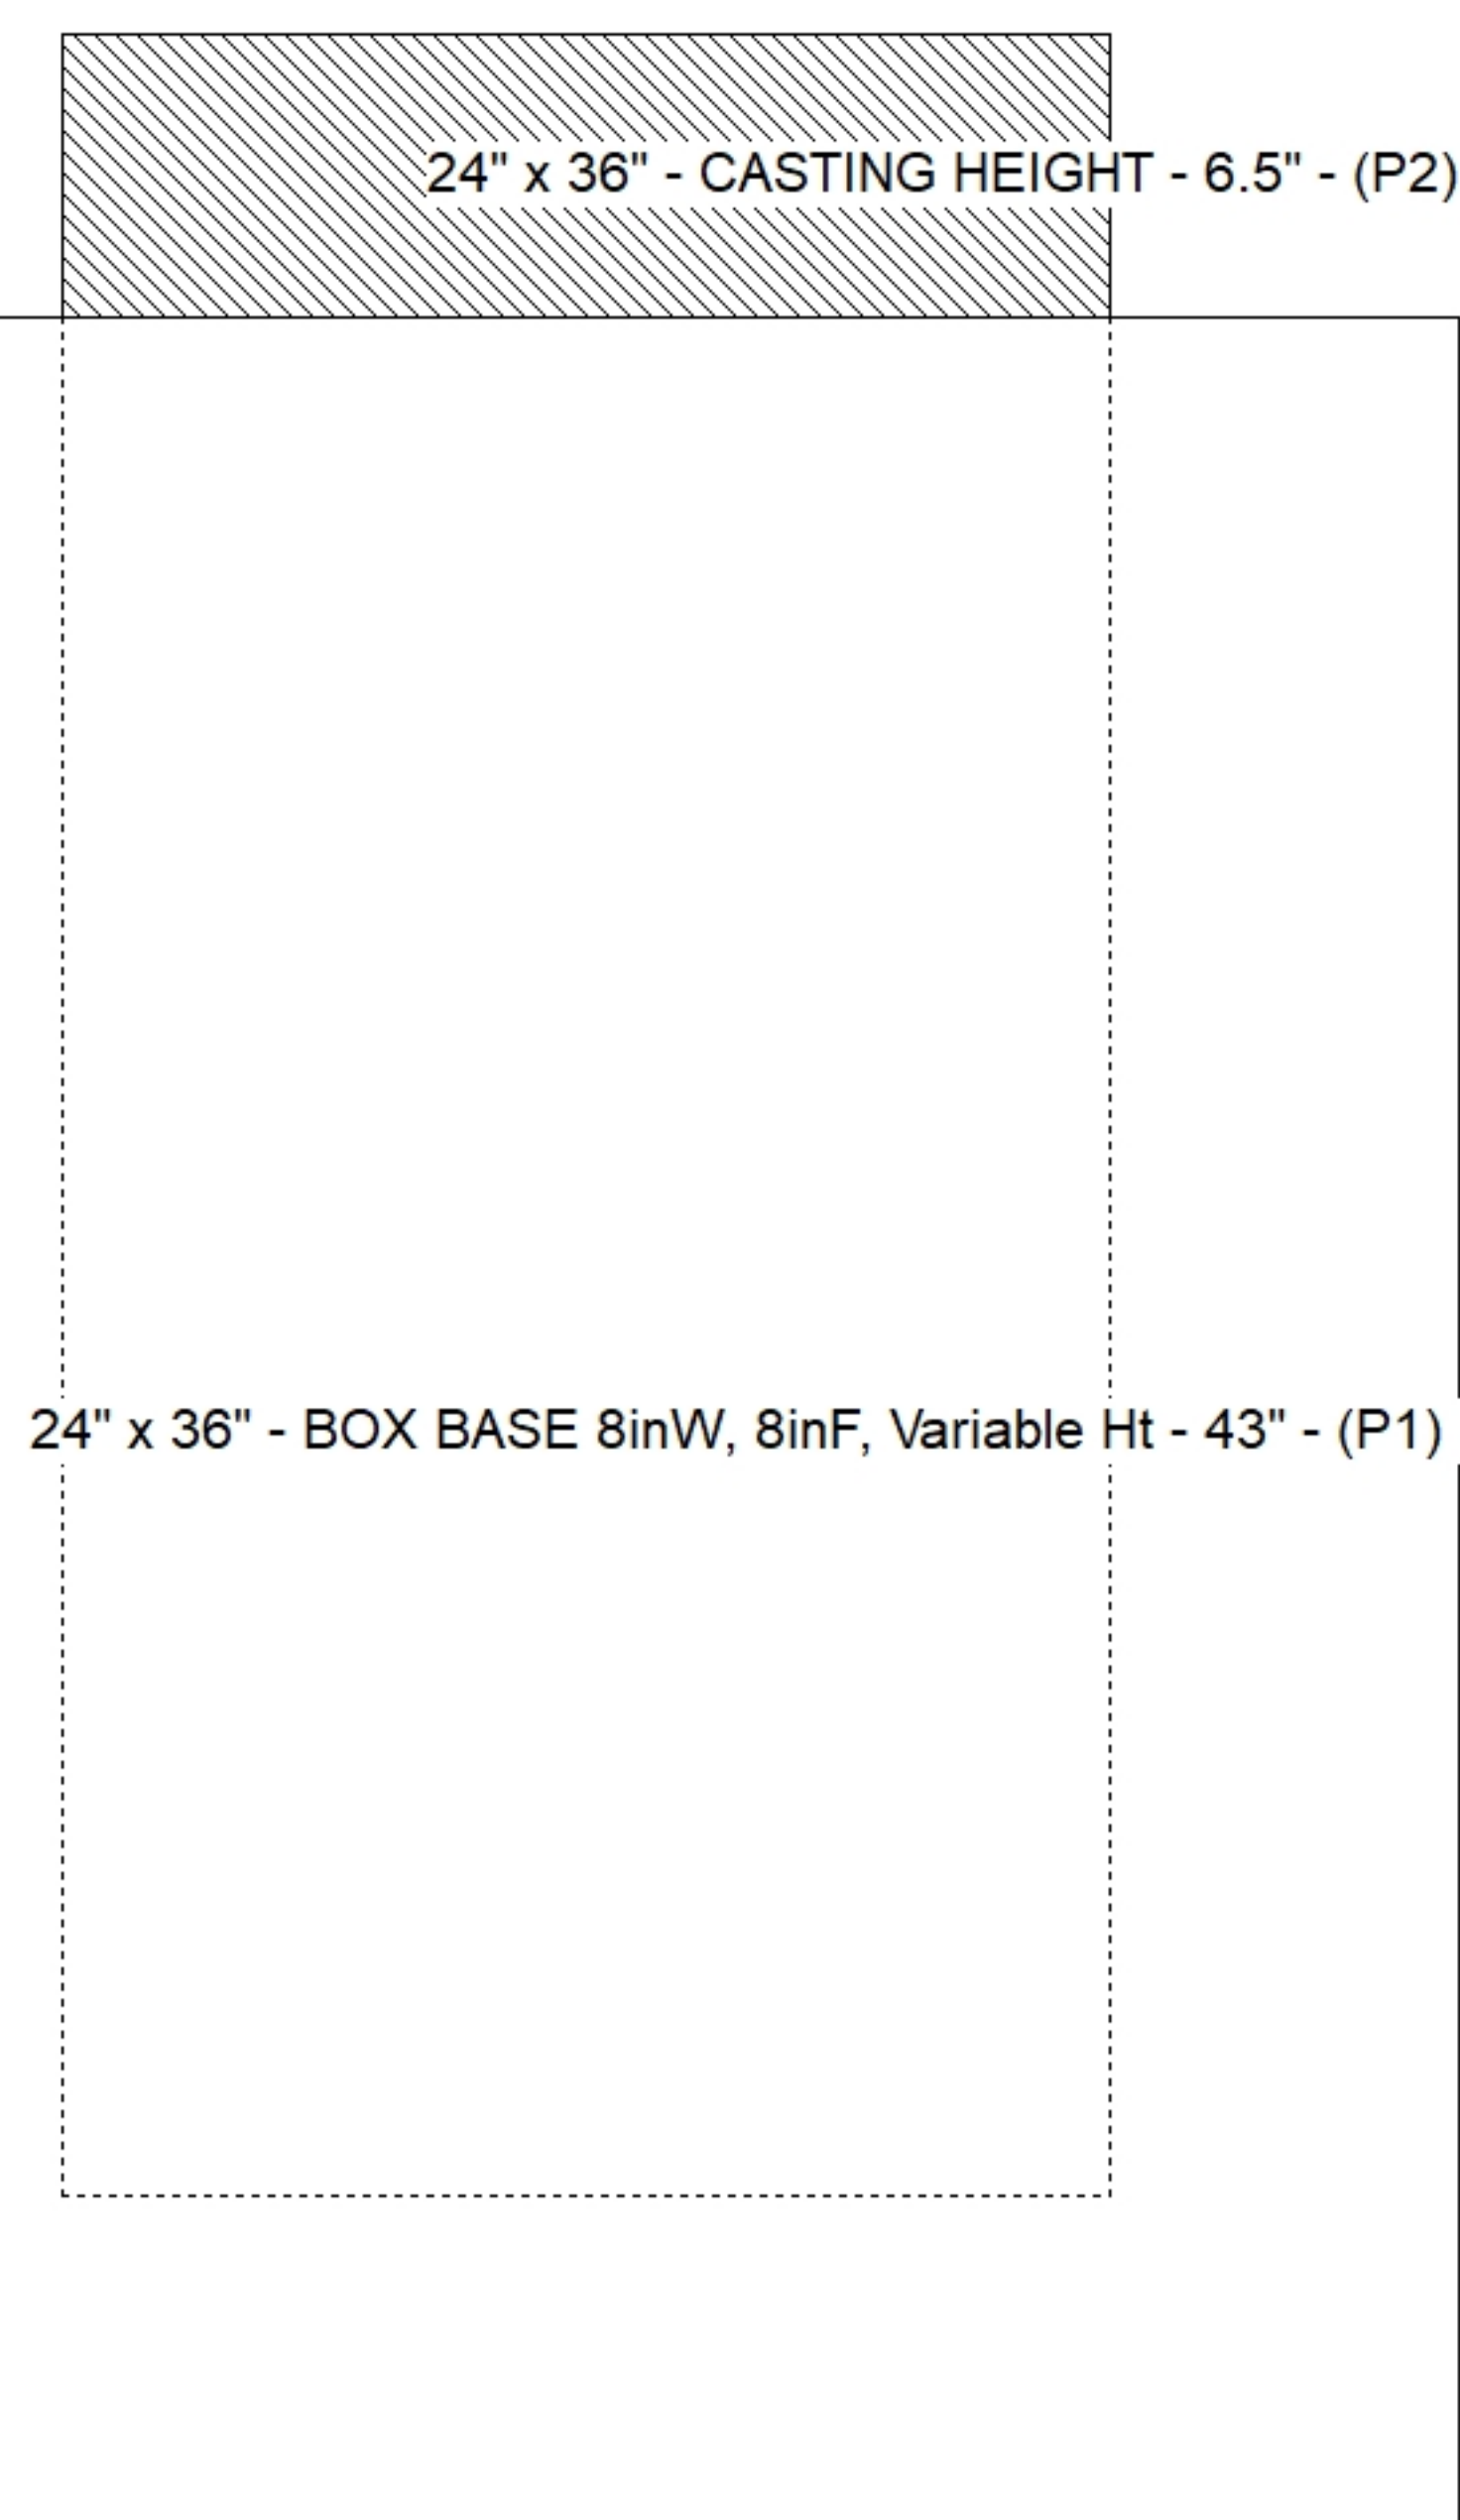

Default - Interior Dimensions

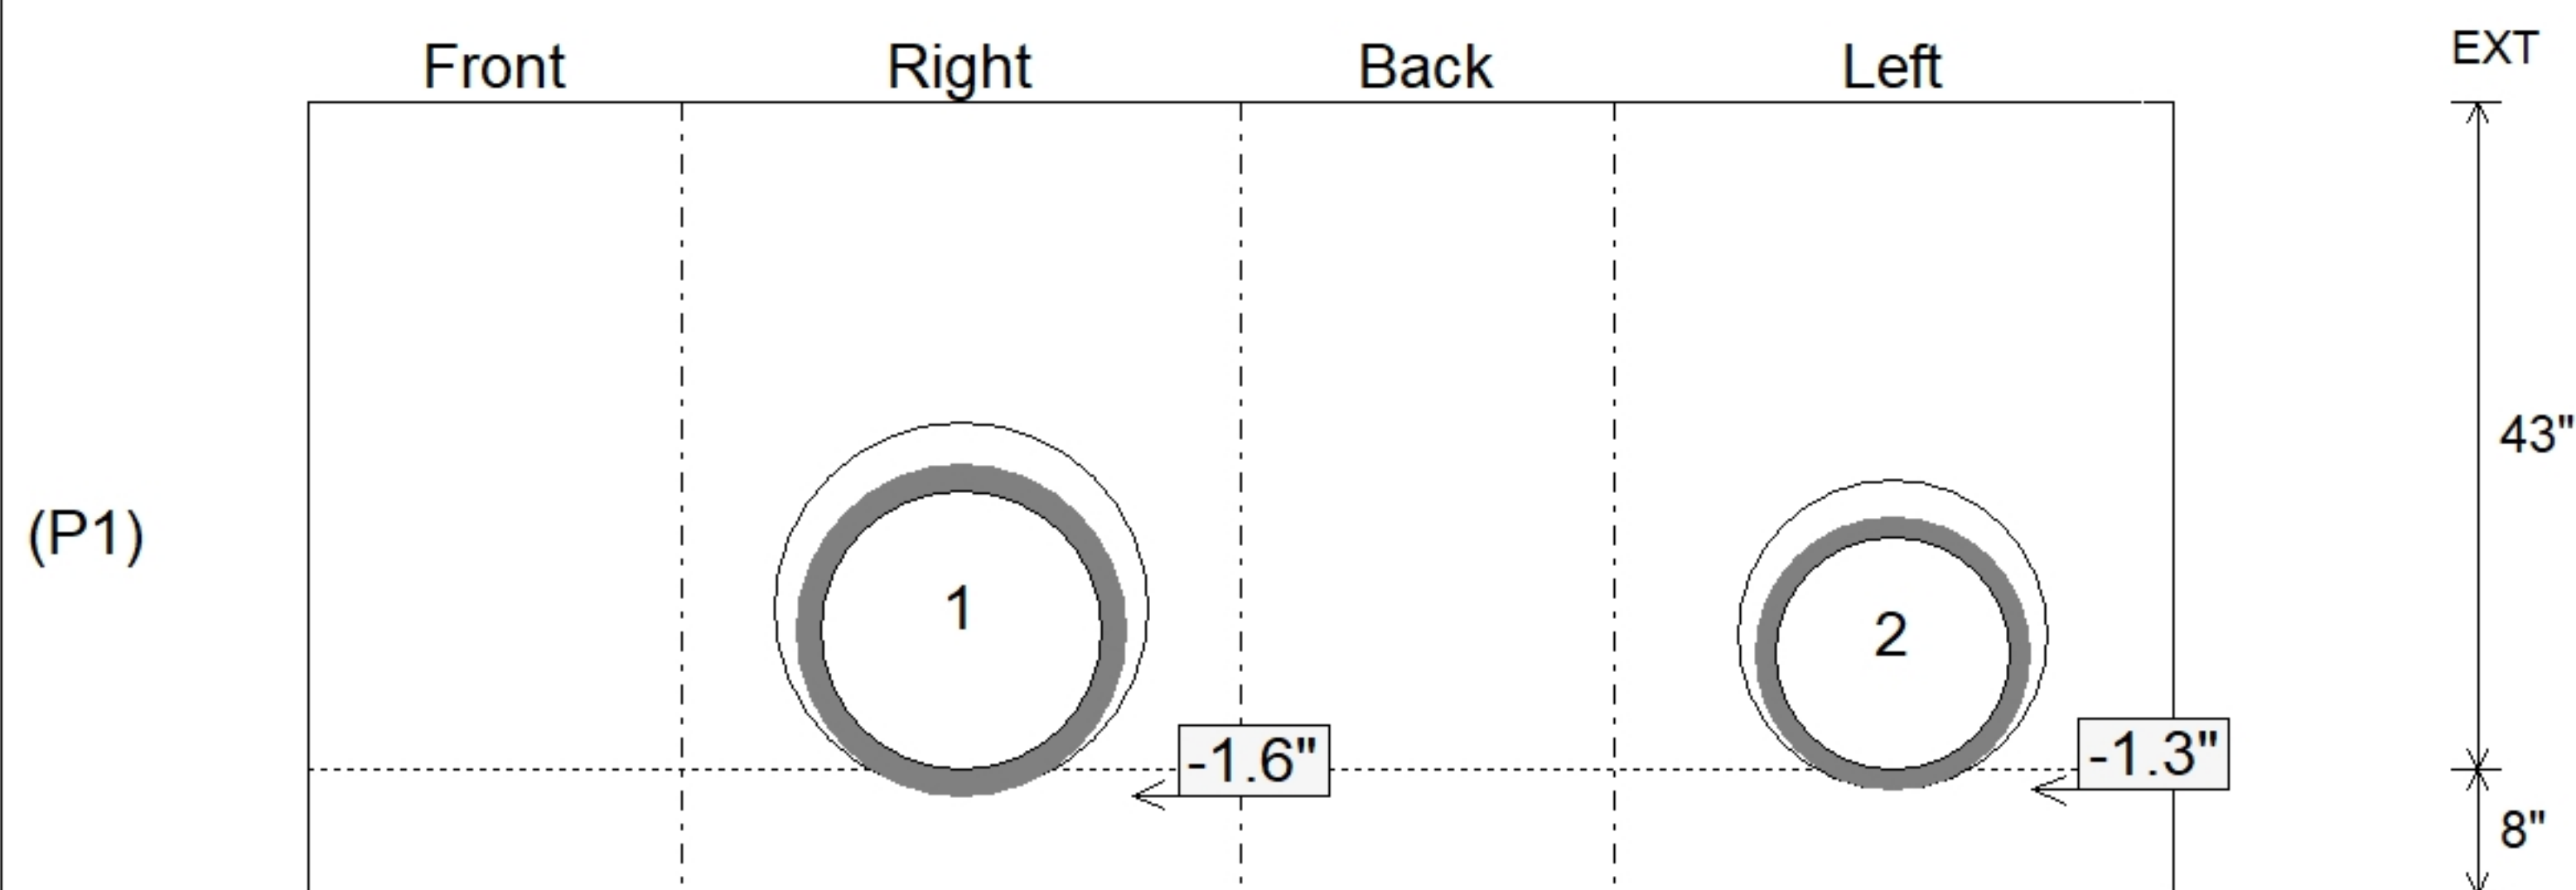

Submittal Drawing
10/15/2026 7:58:29 AM

SUBMITTAL
APPROVED BY:
