

Contractor: Core & Main LP

Plant: Beaver Dam, KY




Slack: 2.13"

1. PER ASTM C-478 SPECIFICATIONS
2. CONCRETE: 4,000 PSI AT 28 DAYS
3. REINFORCEMENT:
 - FLAT LID: #5 BAR @ 6" C.C. E.W. (GRADE 60)
 - BASE: PER ASTM A615
4. NO INVERT CHANNEL
5. STEPS AT 90 DEGREES
6. 4" CASTING SUPPLIED BY OTHERS


P3) 30" x 30" - CASTING HEIGHT - 4"
P2) 60" - MH FLAT TOP w/30"x30" Hole - 13"
P1) 60" - MH BASE Custom Ht - 70"
1) 60" - Conseal CS-102 1.00"
1) 30" x 30" - Conseal CS-102 1.00"
2) Hole - 44
6) MH Step ML-10-TDS-NCR - 10"

0 lb
2400 lb
8358 lb
0 lb
0 lb
0 lb
0 lb


Structure Total: 10758 lb

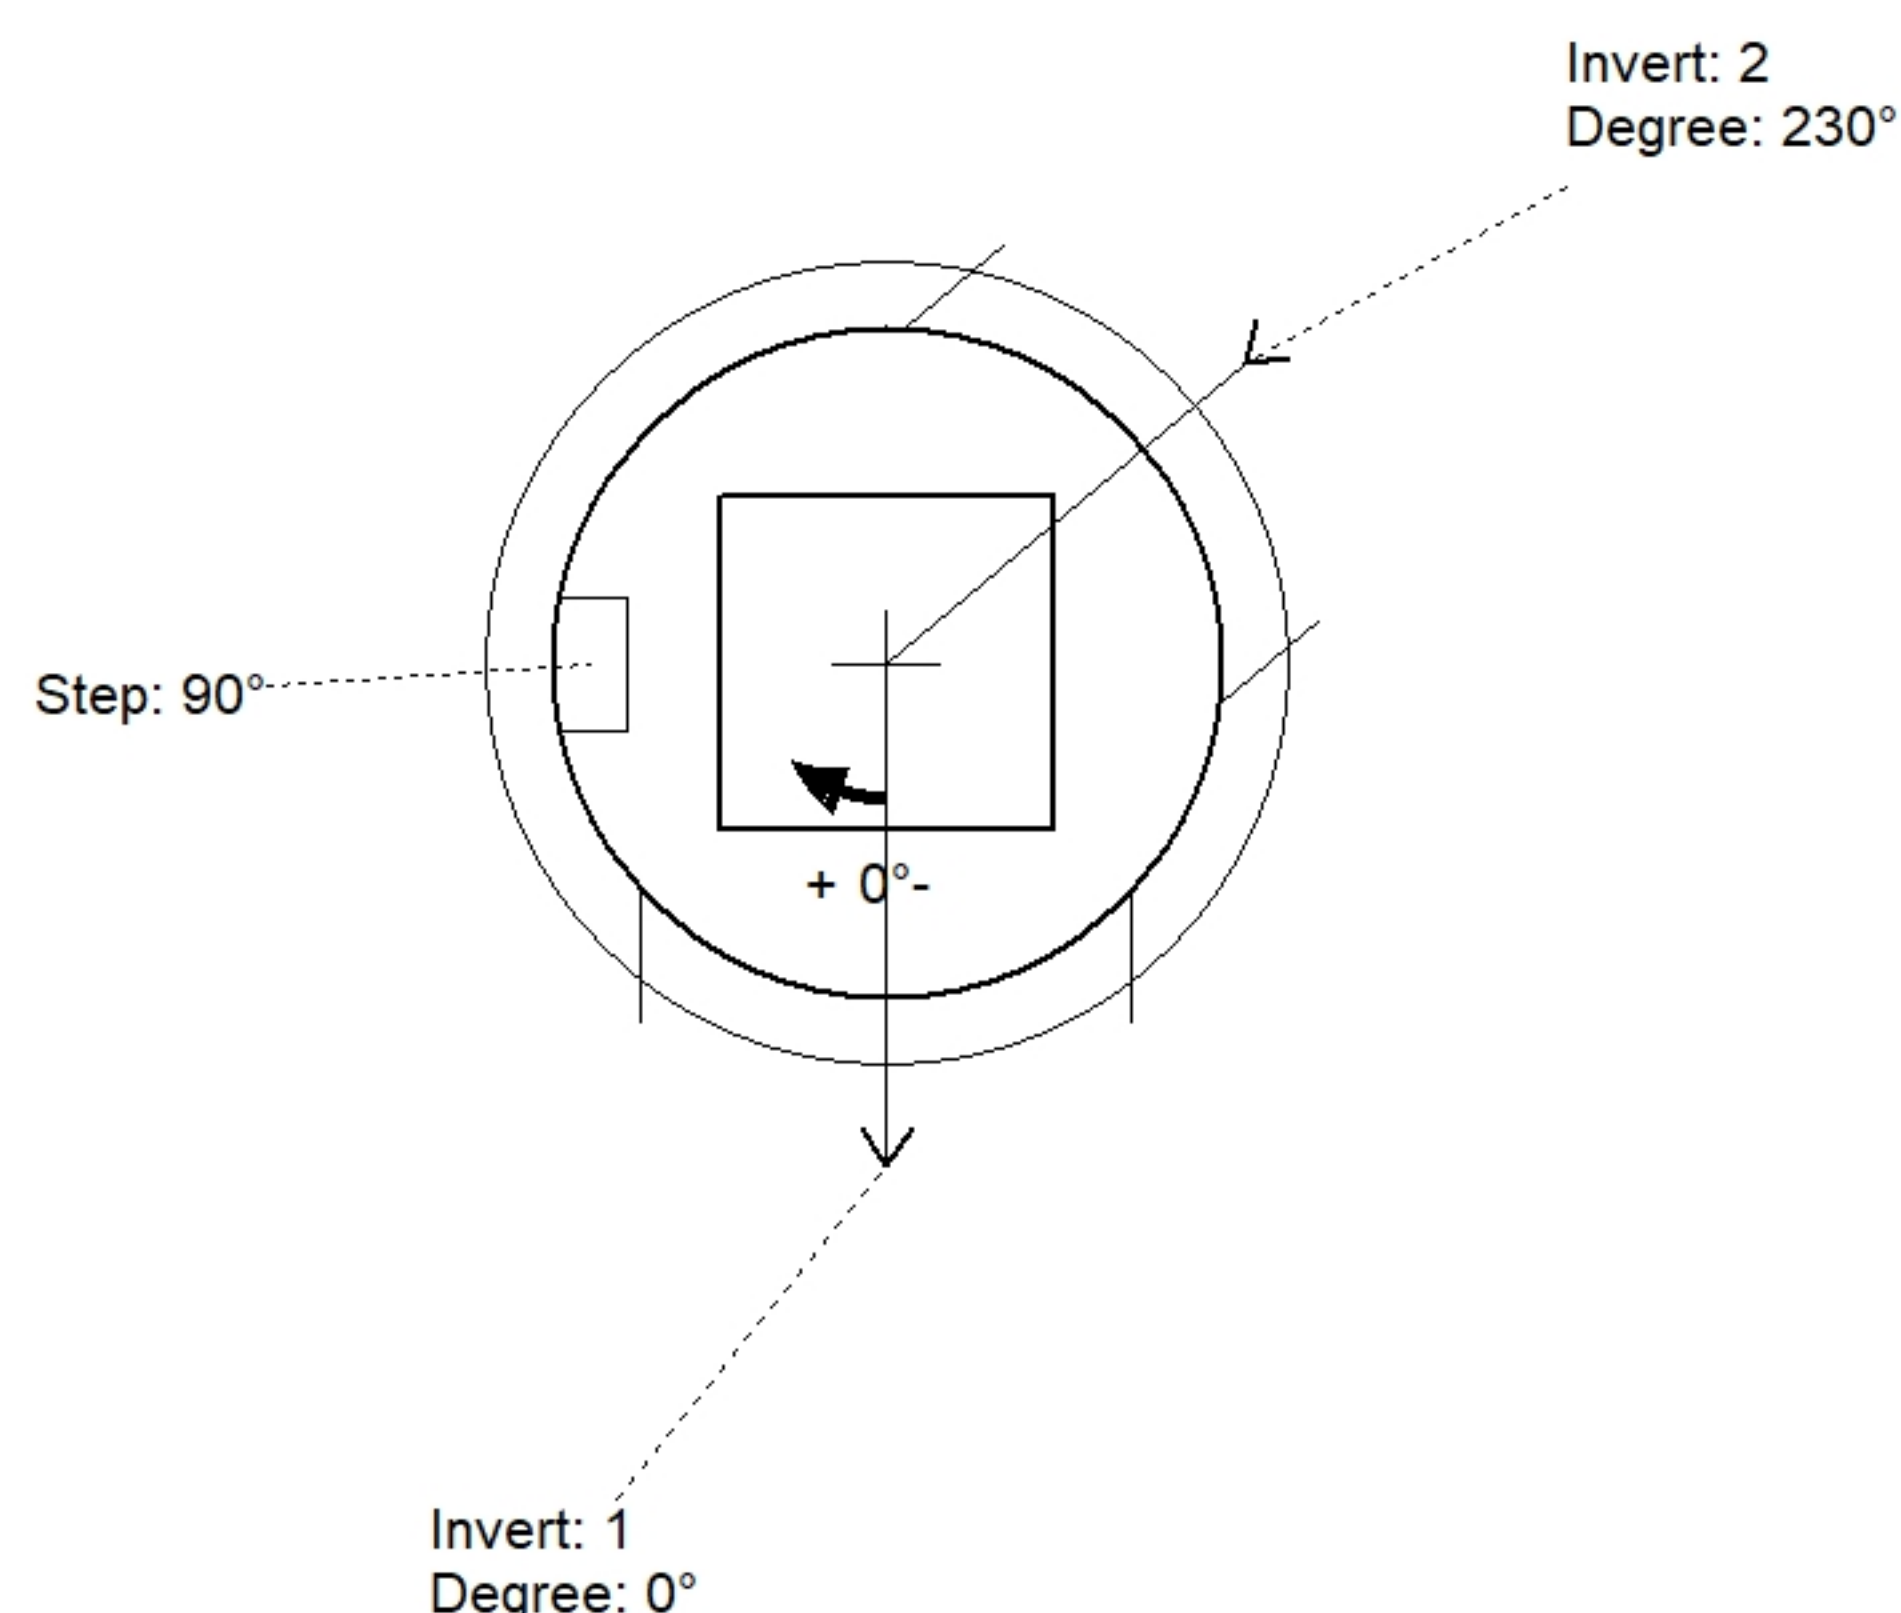

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	511.3'							
Reducer								
Invert 1	504.11'	0°	36" HDPE	41.7"	44"	Hole 44	0"	P1
Invert 2	504.11'	230°	36" HDPE	41.7"	44"	Hole 44	0"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

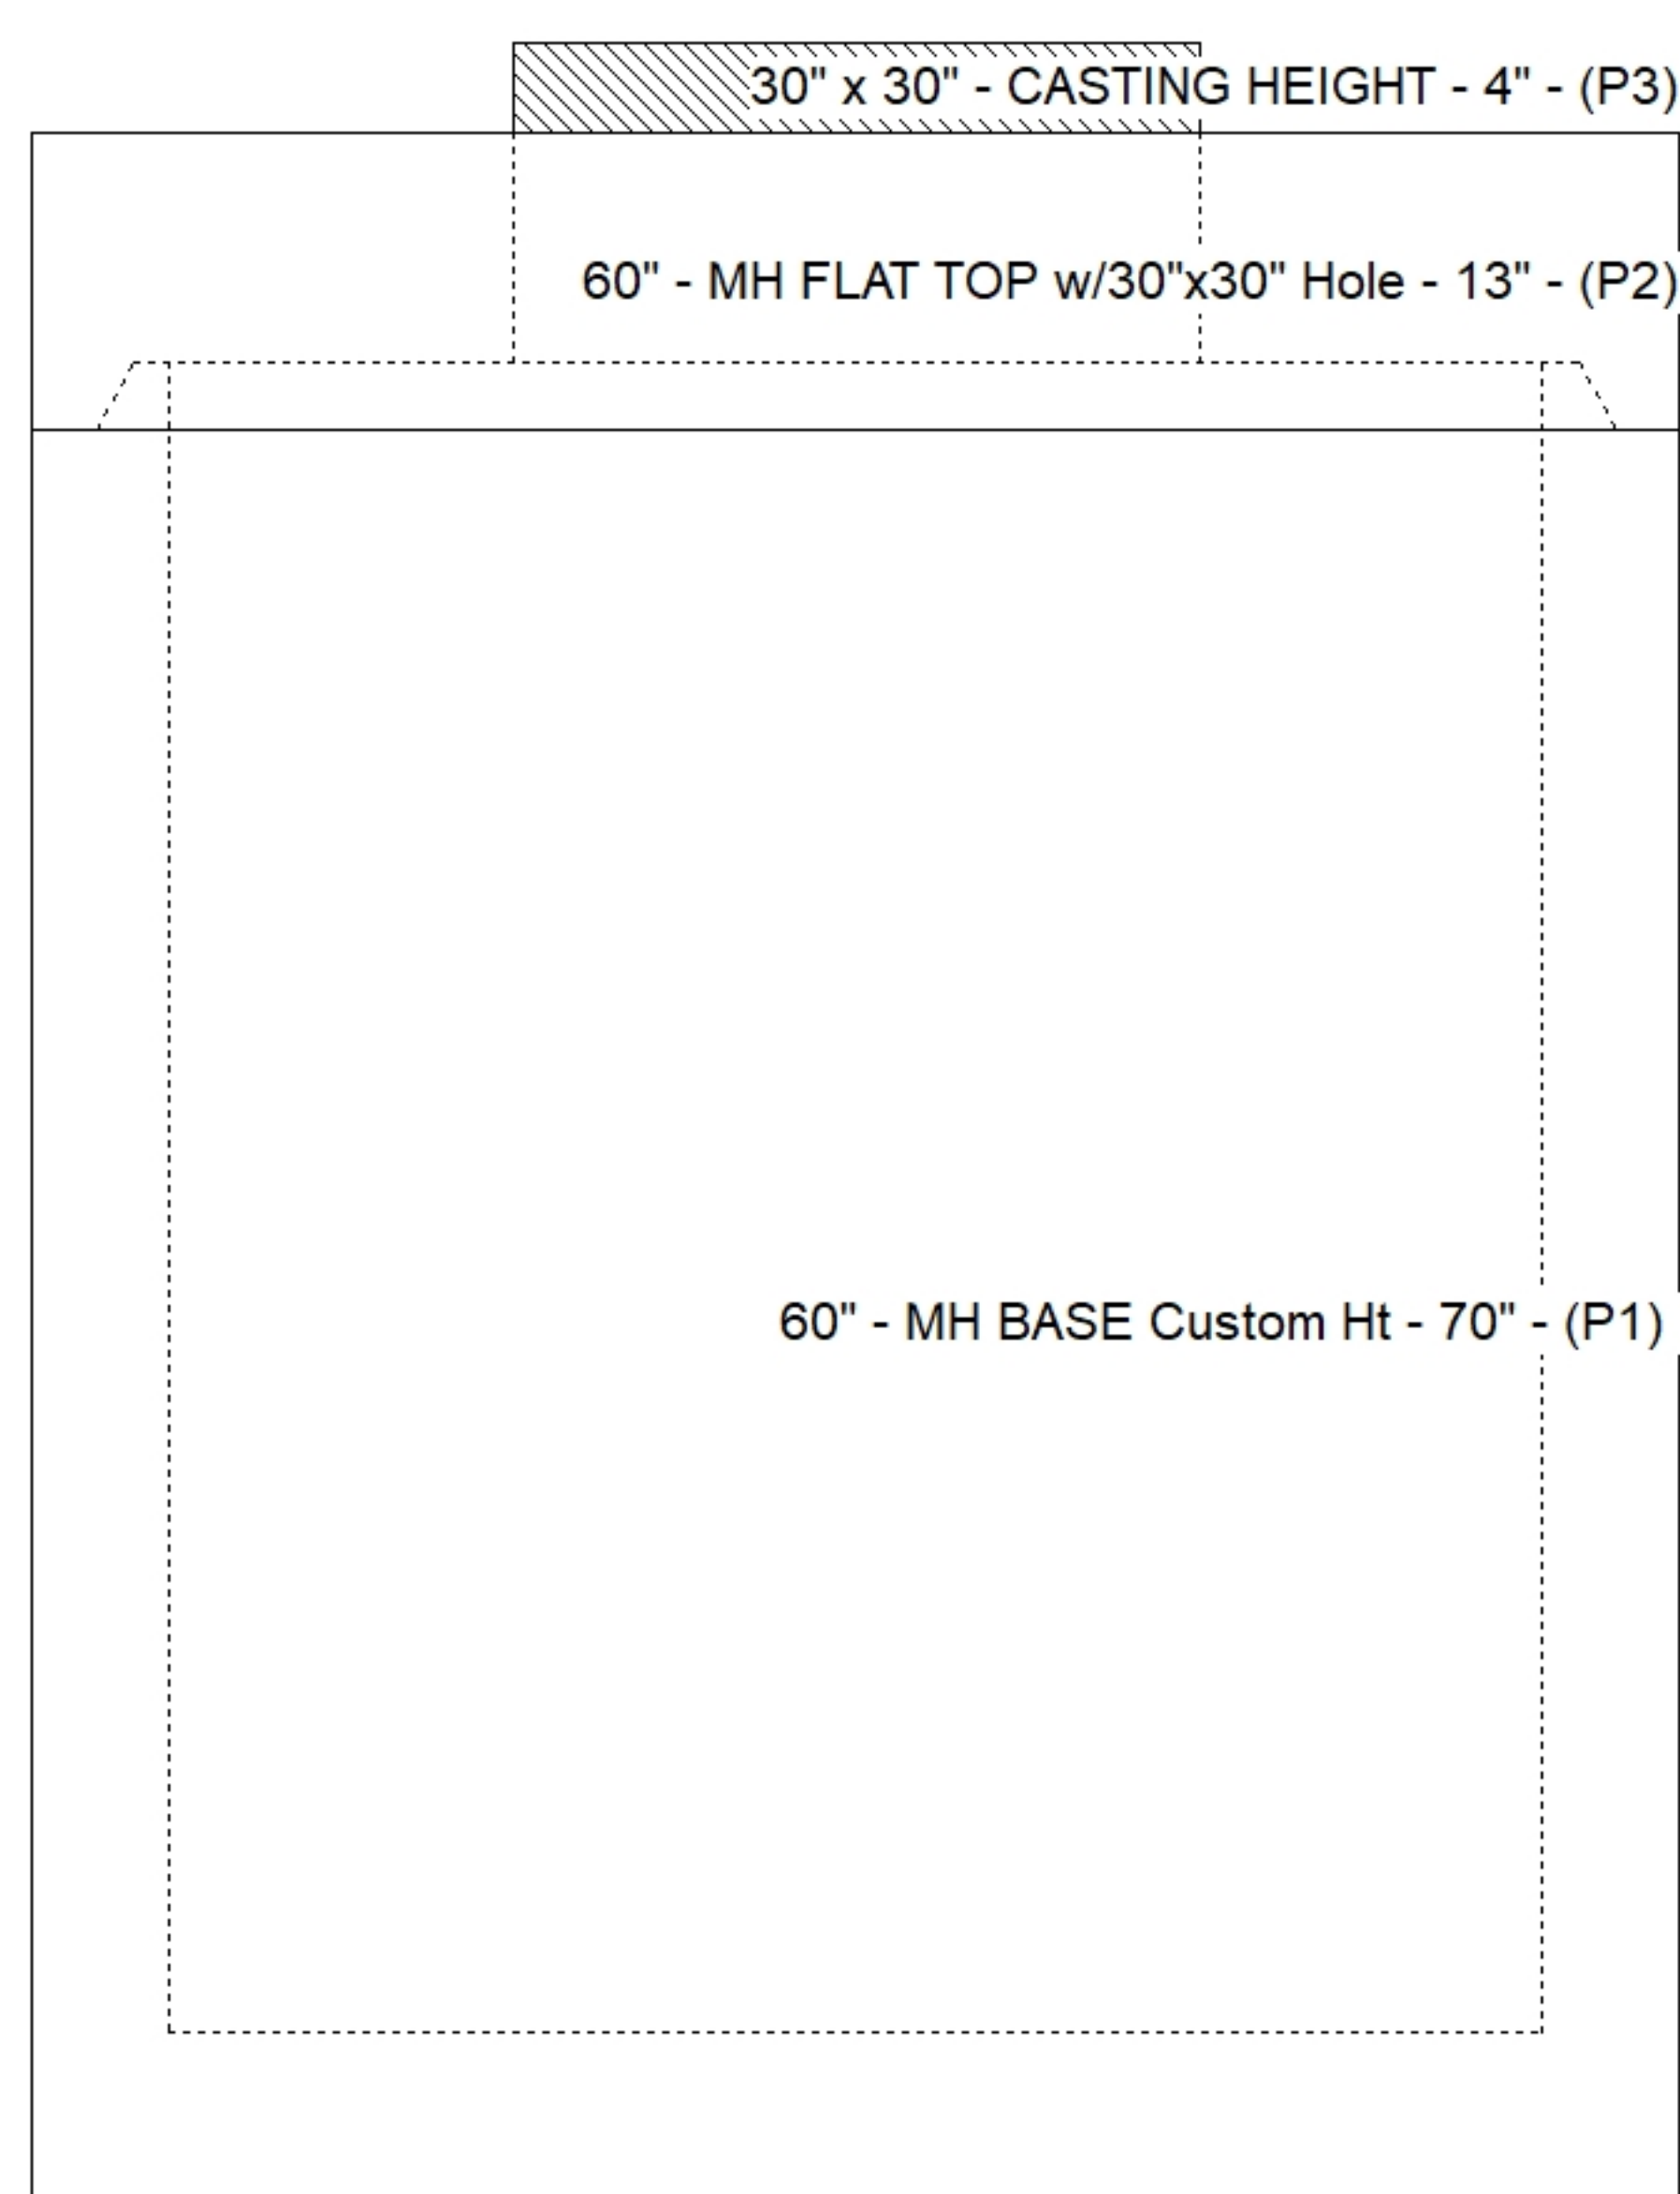

Default - Interior Dimensions

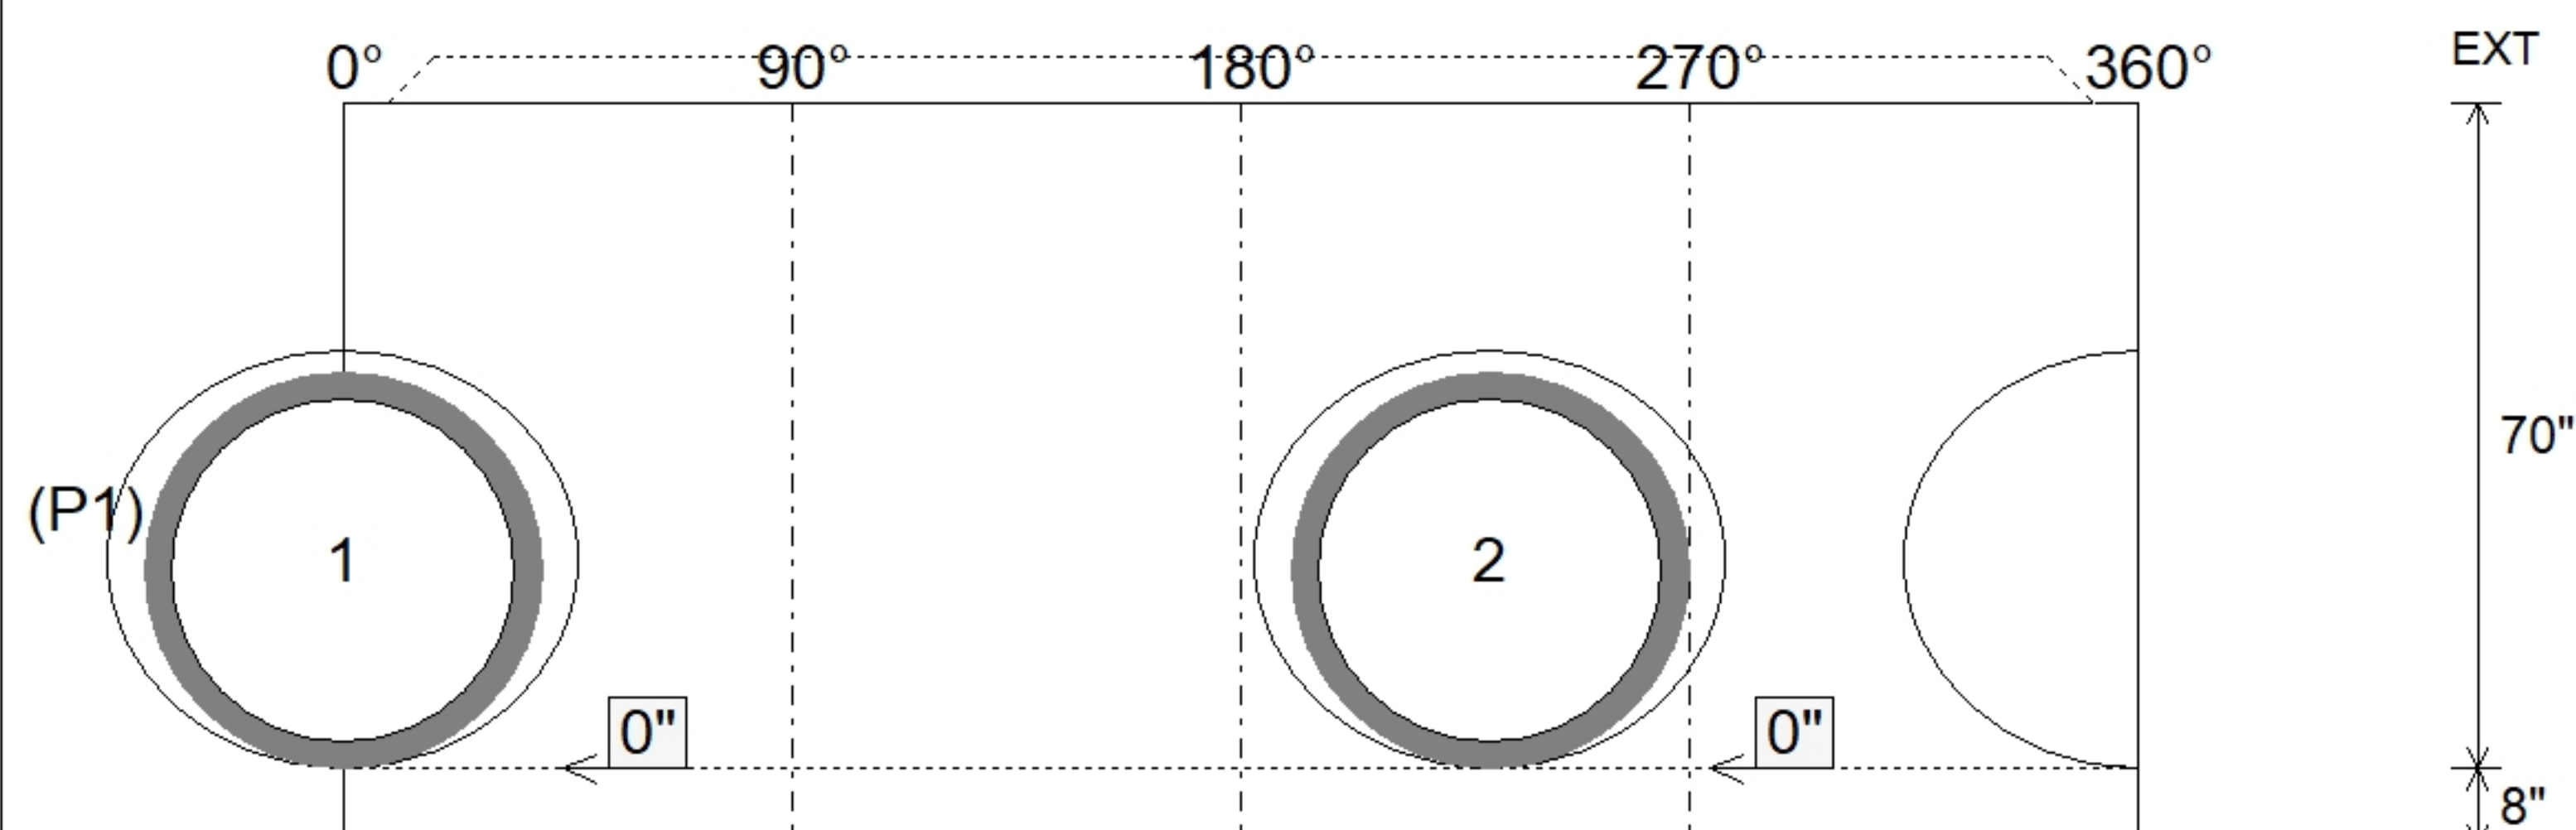

Submittal Drawing
10/15/2026 7:58:36 AM

SUBMITTAL
APPROVED BY:
