

Contractor: The Allen Company, Inc.


Plant: Beaver Dam




Slack: 1.24"

1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. REINFORCING PER ASTM A615 (GRADE 60).
 - CONE (As .12)
 - RISER/WALLS (As .12)
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.
4. CASTING BY OTHERS
5. ADMIXTURE = CONBLOCK-CDA RED


Structure Total: 7295 lb

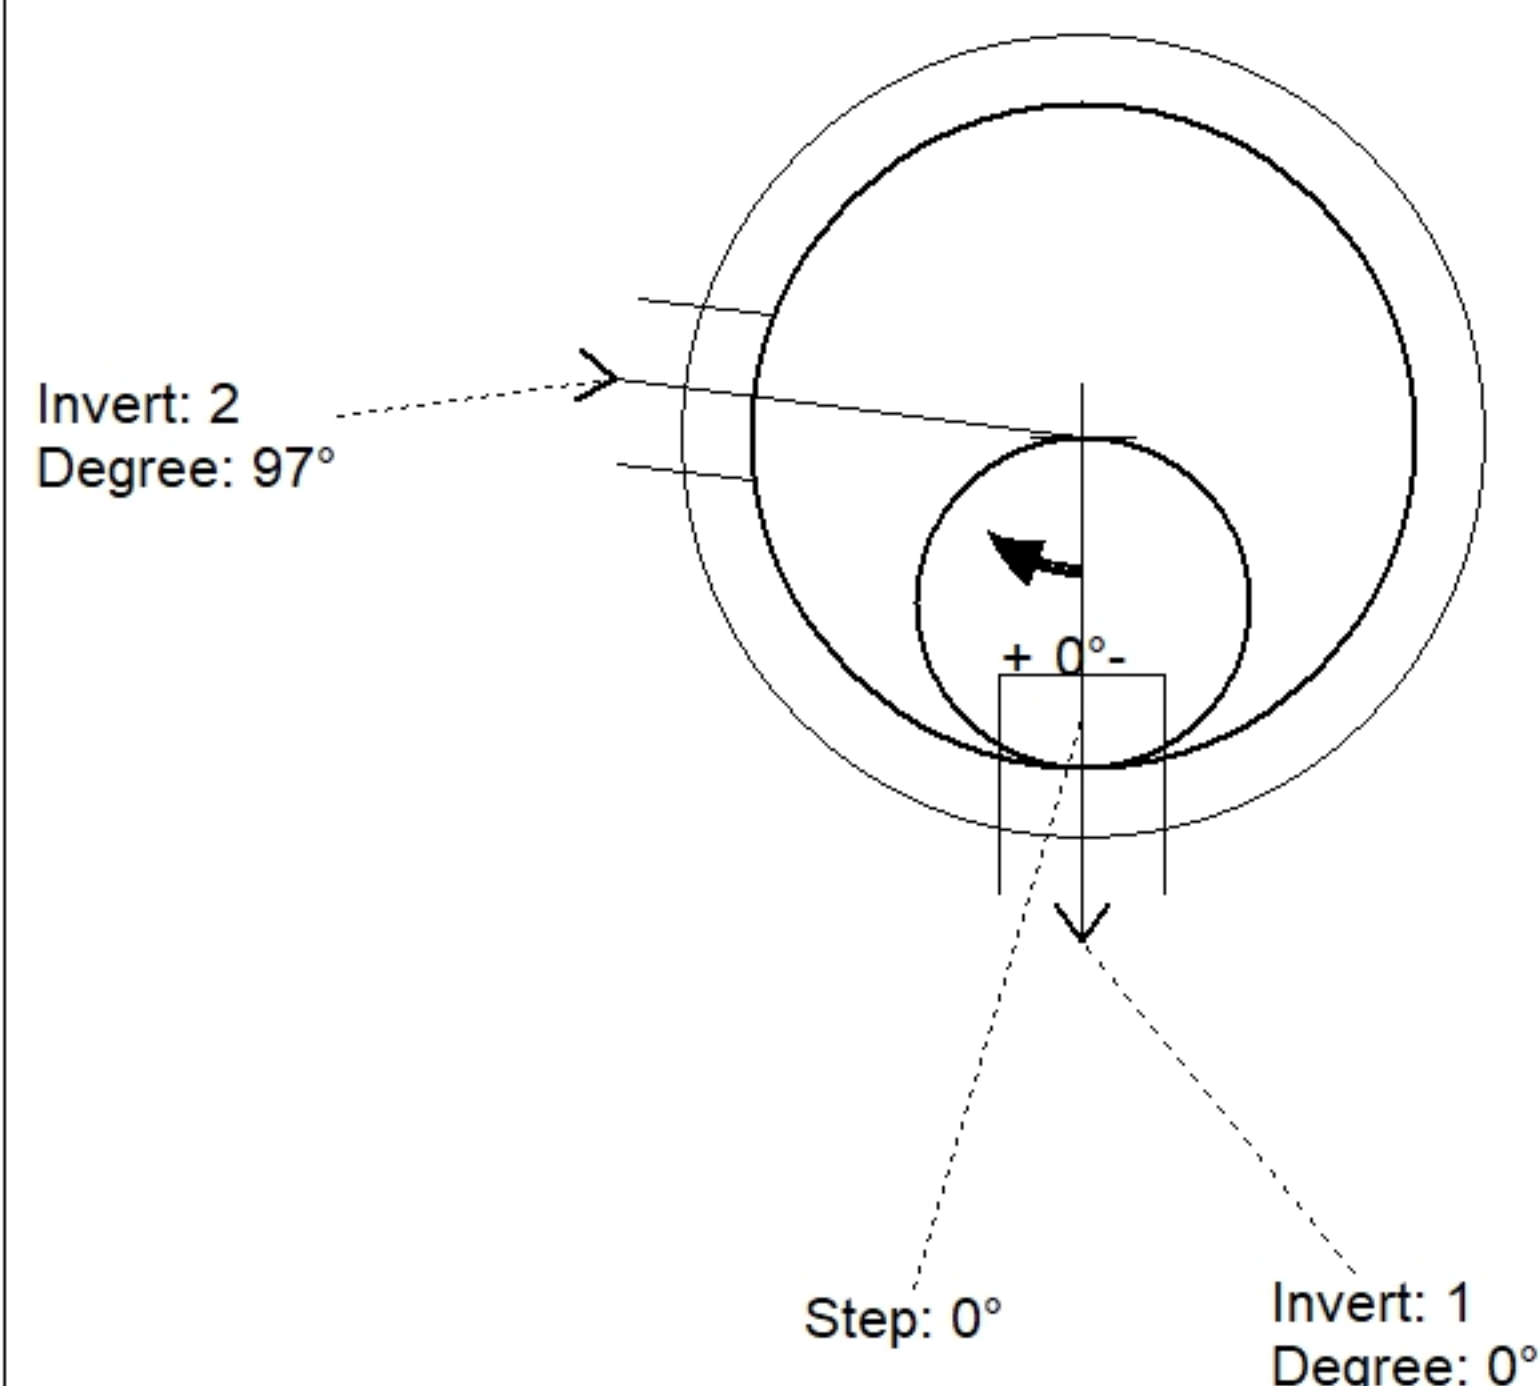

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	942.65'							
Reducer								
Invert 1	936.63'	0°	8" PVC SDR35	8.5"	12"	PSX 12-08 NYLO	0"	P1
Invert 2	937.19'	97°	8" PVC SDR35	8.5"	12"	PSX 12-08 NYLO	6.72"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

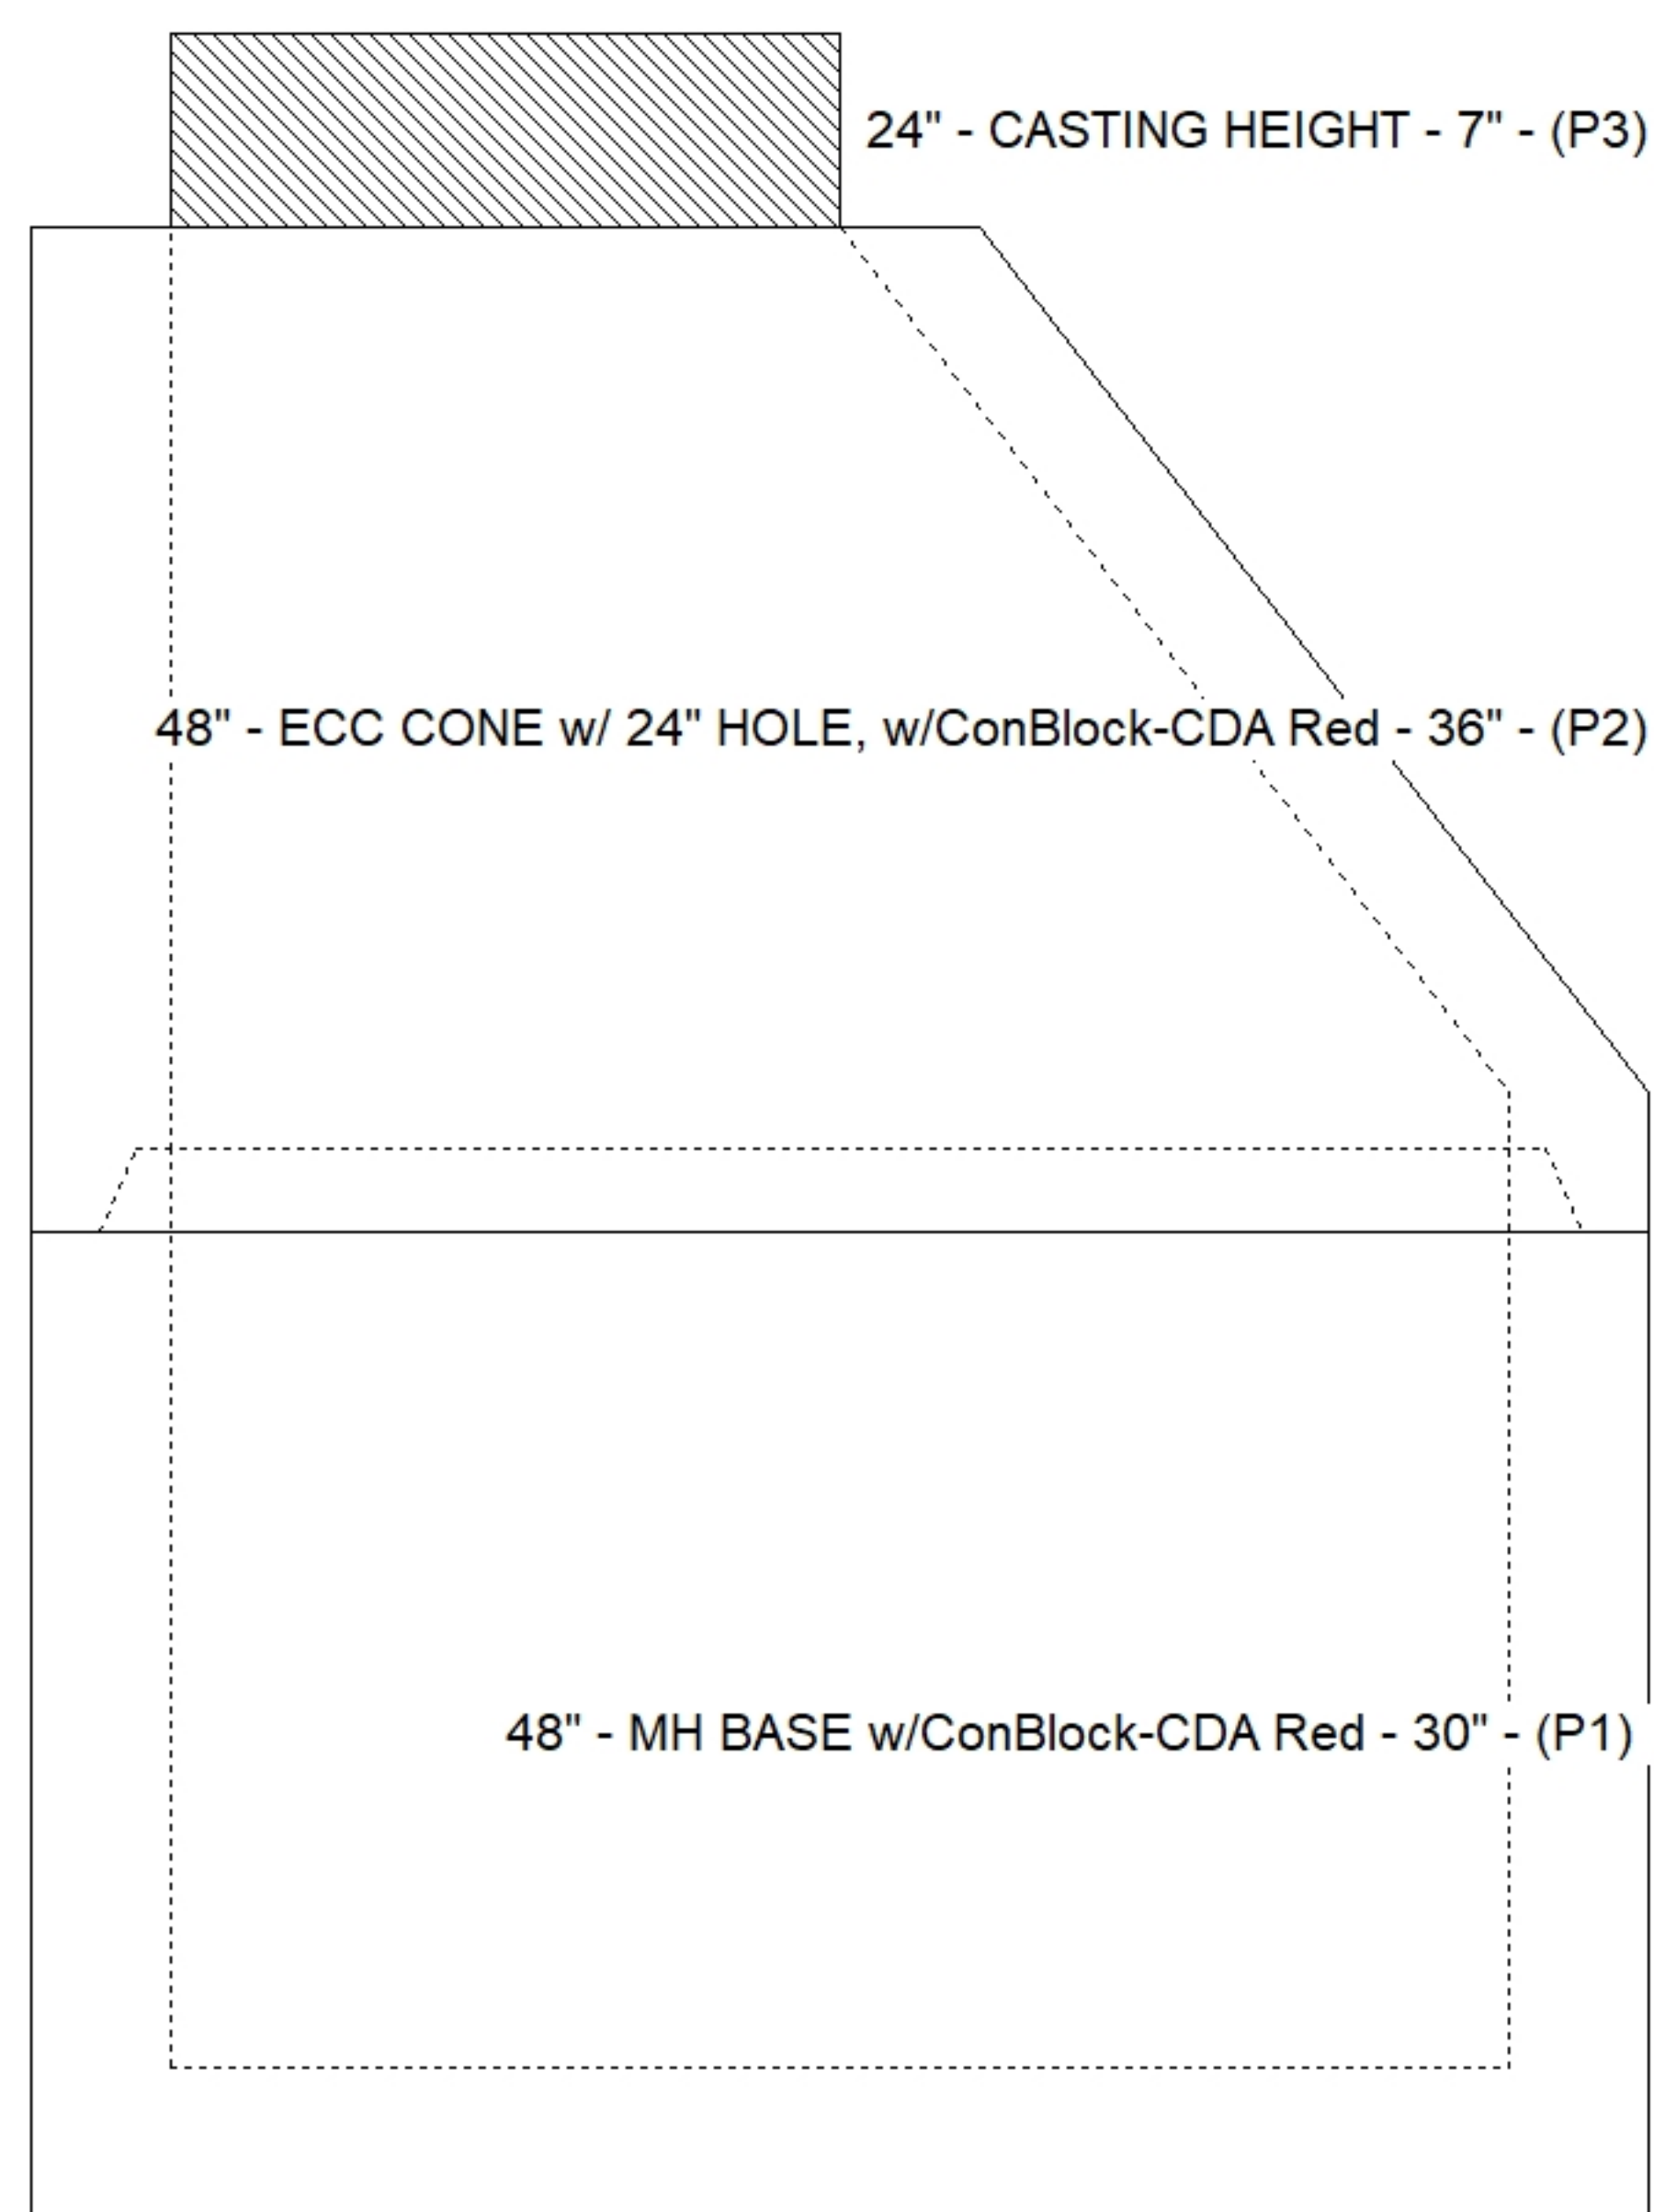

Default - Interior Dimensions

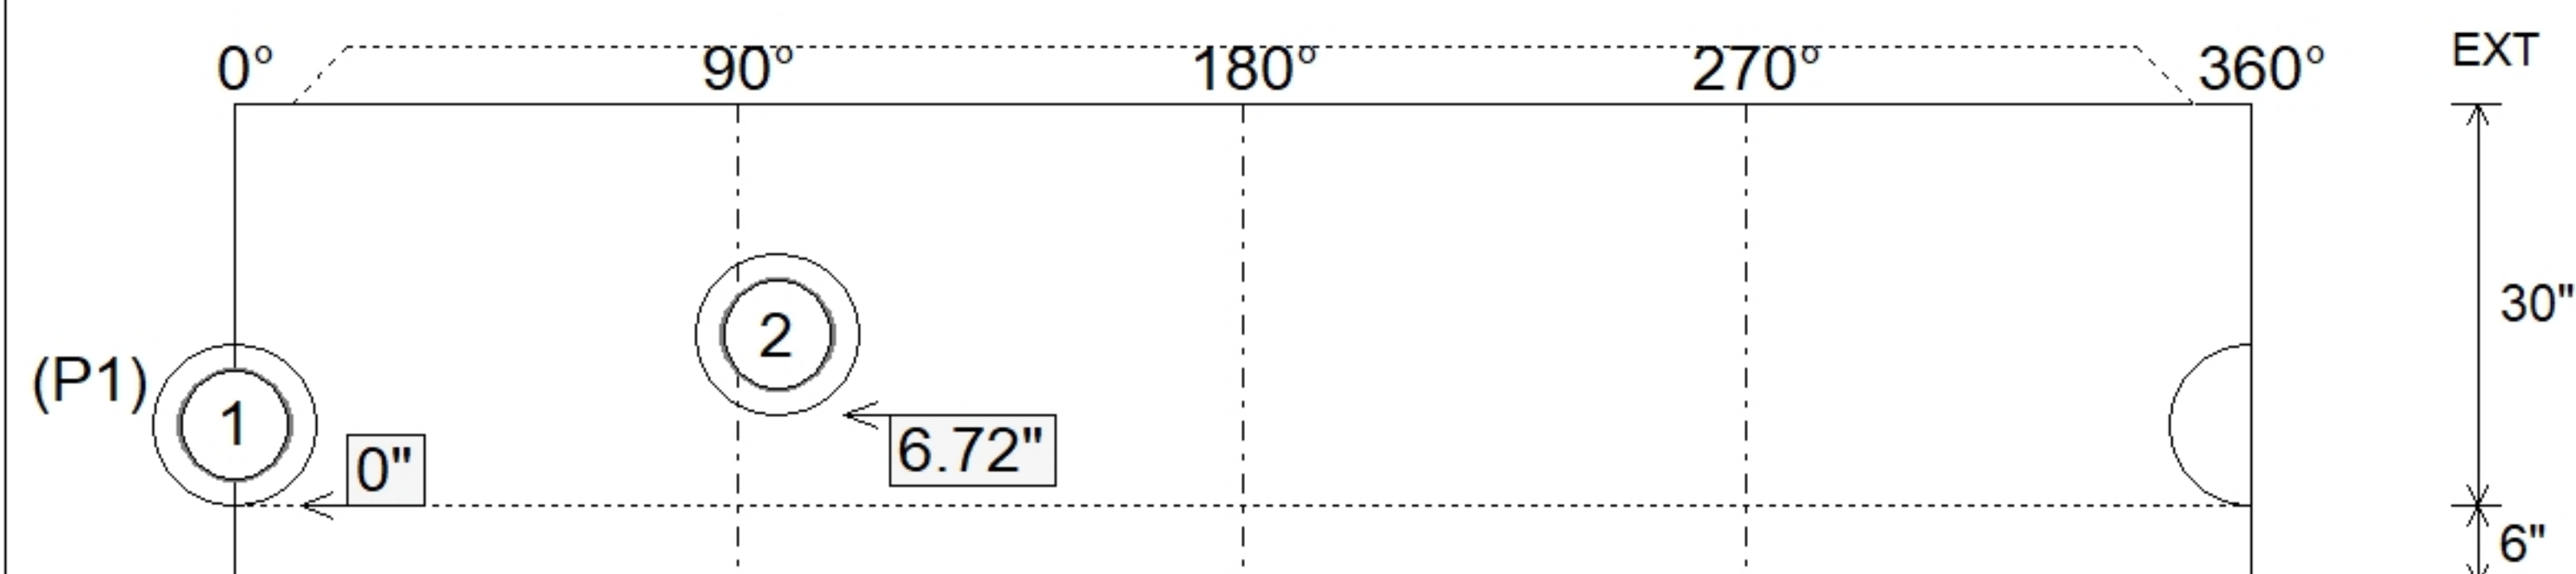

SUBMITTAL
APPROVED BY:
