

Contractor: Steve Pleasant Excavating

Plant: Beaver Dam



Size: 36" x 48"

Rim to Invert: 3.45'

Floor Height: 8"



Slack: 0.4"

1. KYTC DBI TYPE 4 / ASTM C913 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. NO STEPS & NO INVERT CHANNEL.
4. CASTING BY ICAST (HOE KY-410).
5. STUB #5 BARS 20" OUT TOP OF WALLS (SPA@12"C/C)

REINFORCING PER ASTM A615 (GRADE 60).
- WALLS (As .31) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.




0 lb
5709 lb
178 lb
0 lb
0 lb

Structure Total: 5887 lb

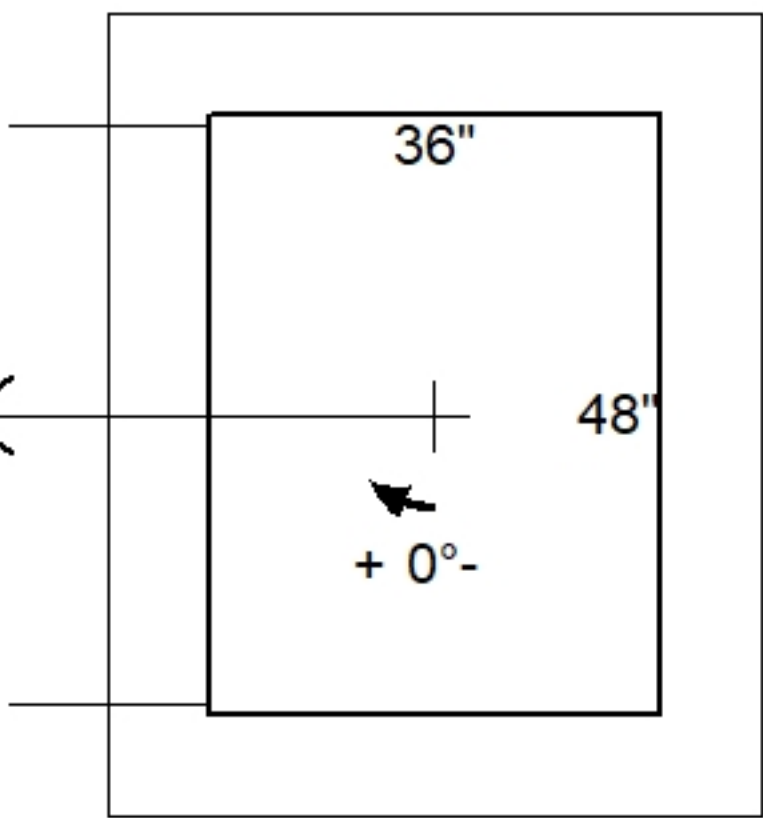

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	432.1'							
Reducer								
Invert 1	428.65'	90°	30" ADS N-12	35.1"	46" x 33"	DOGHOUSE INVRTD 46"x33"	-1.5"	P1
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

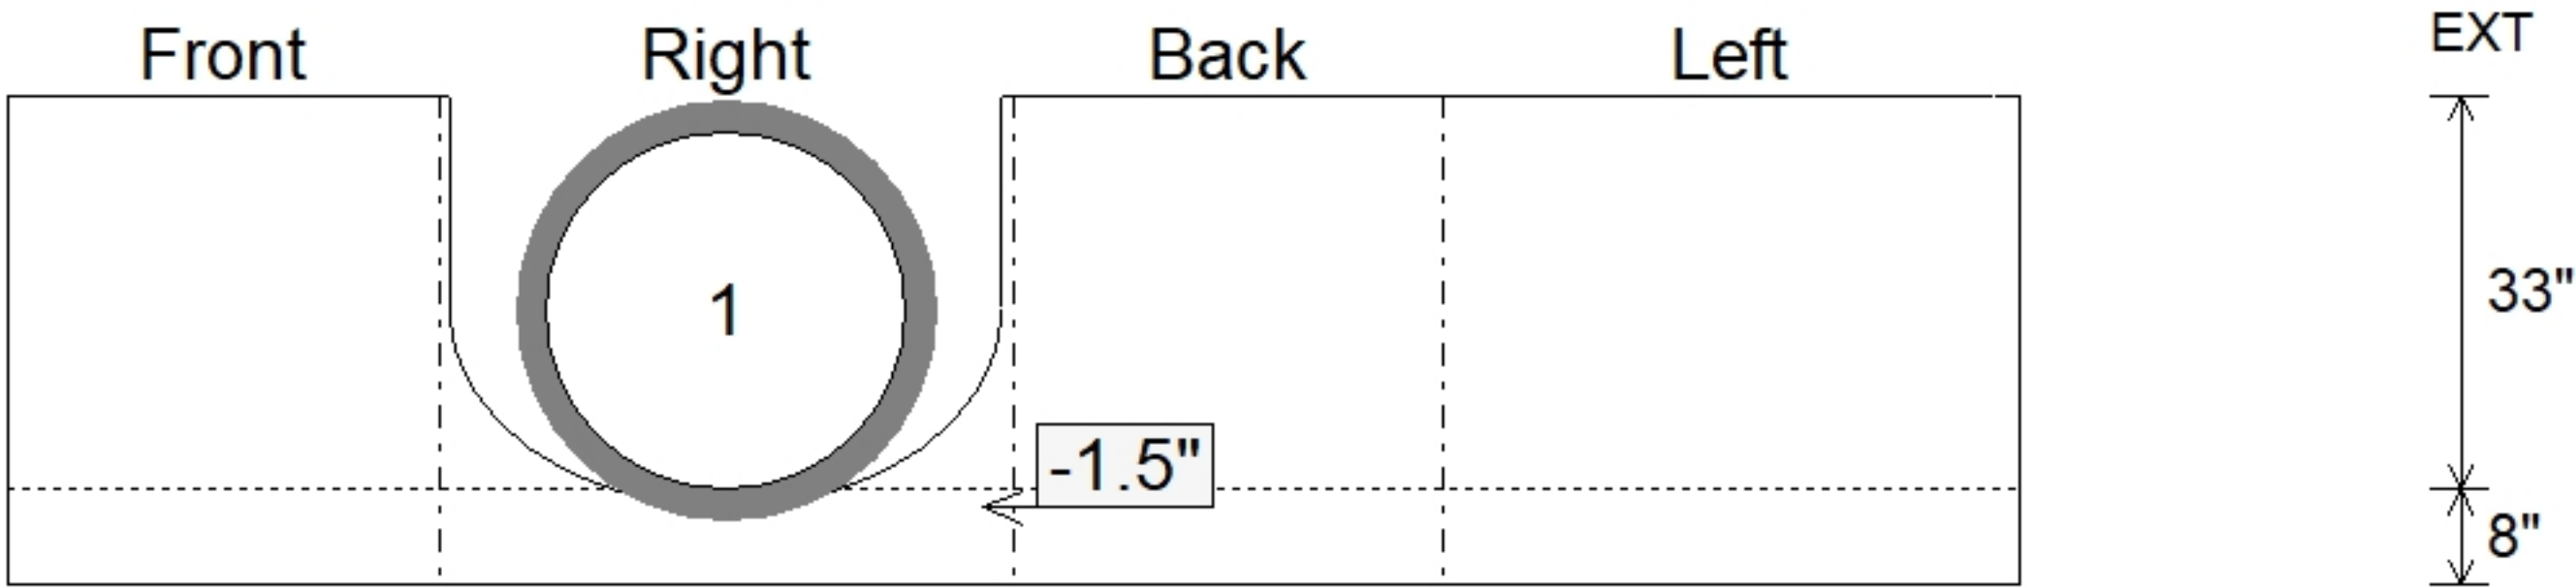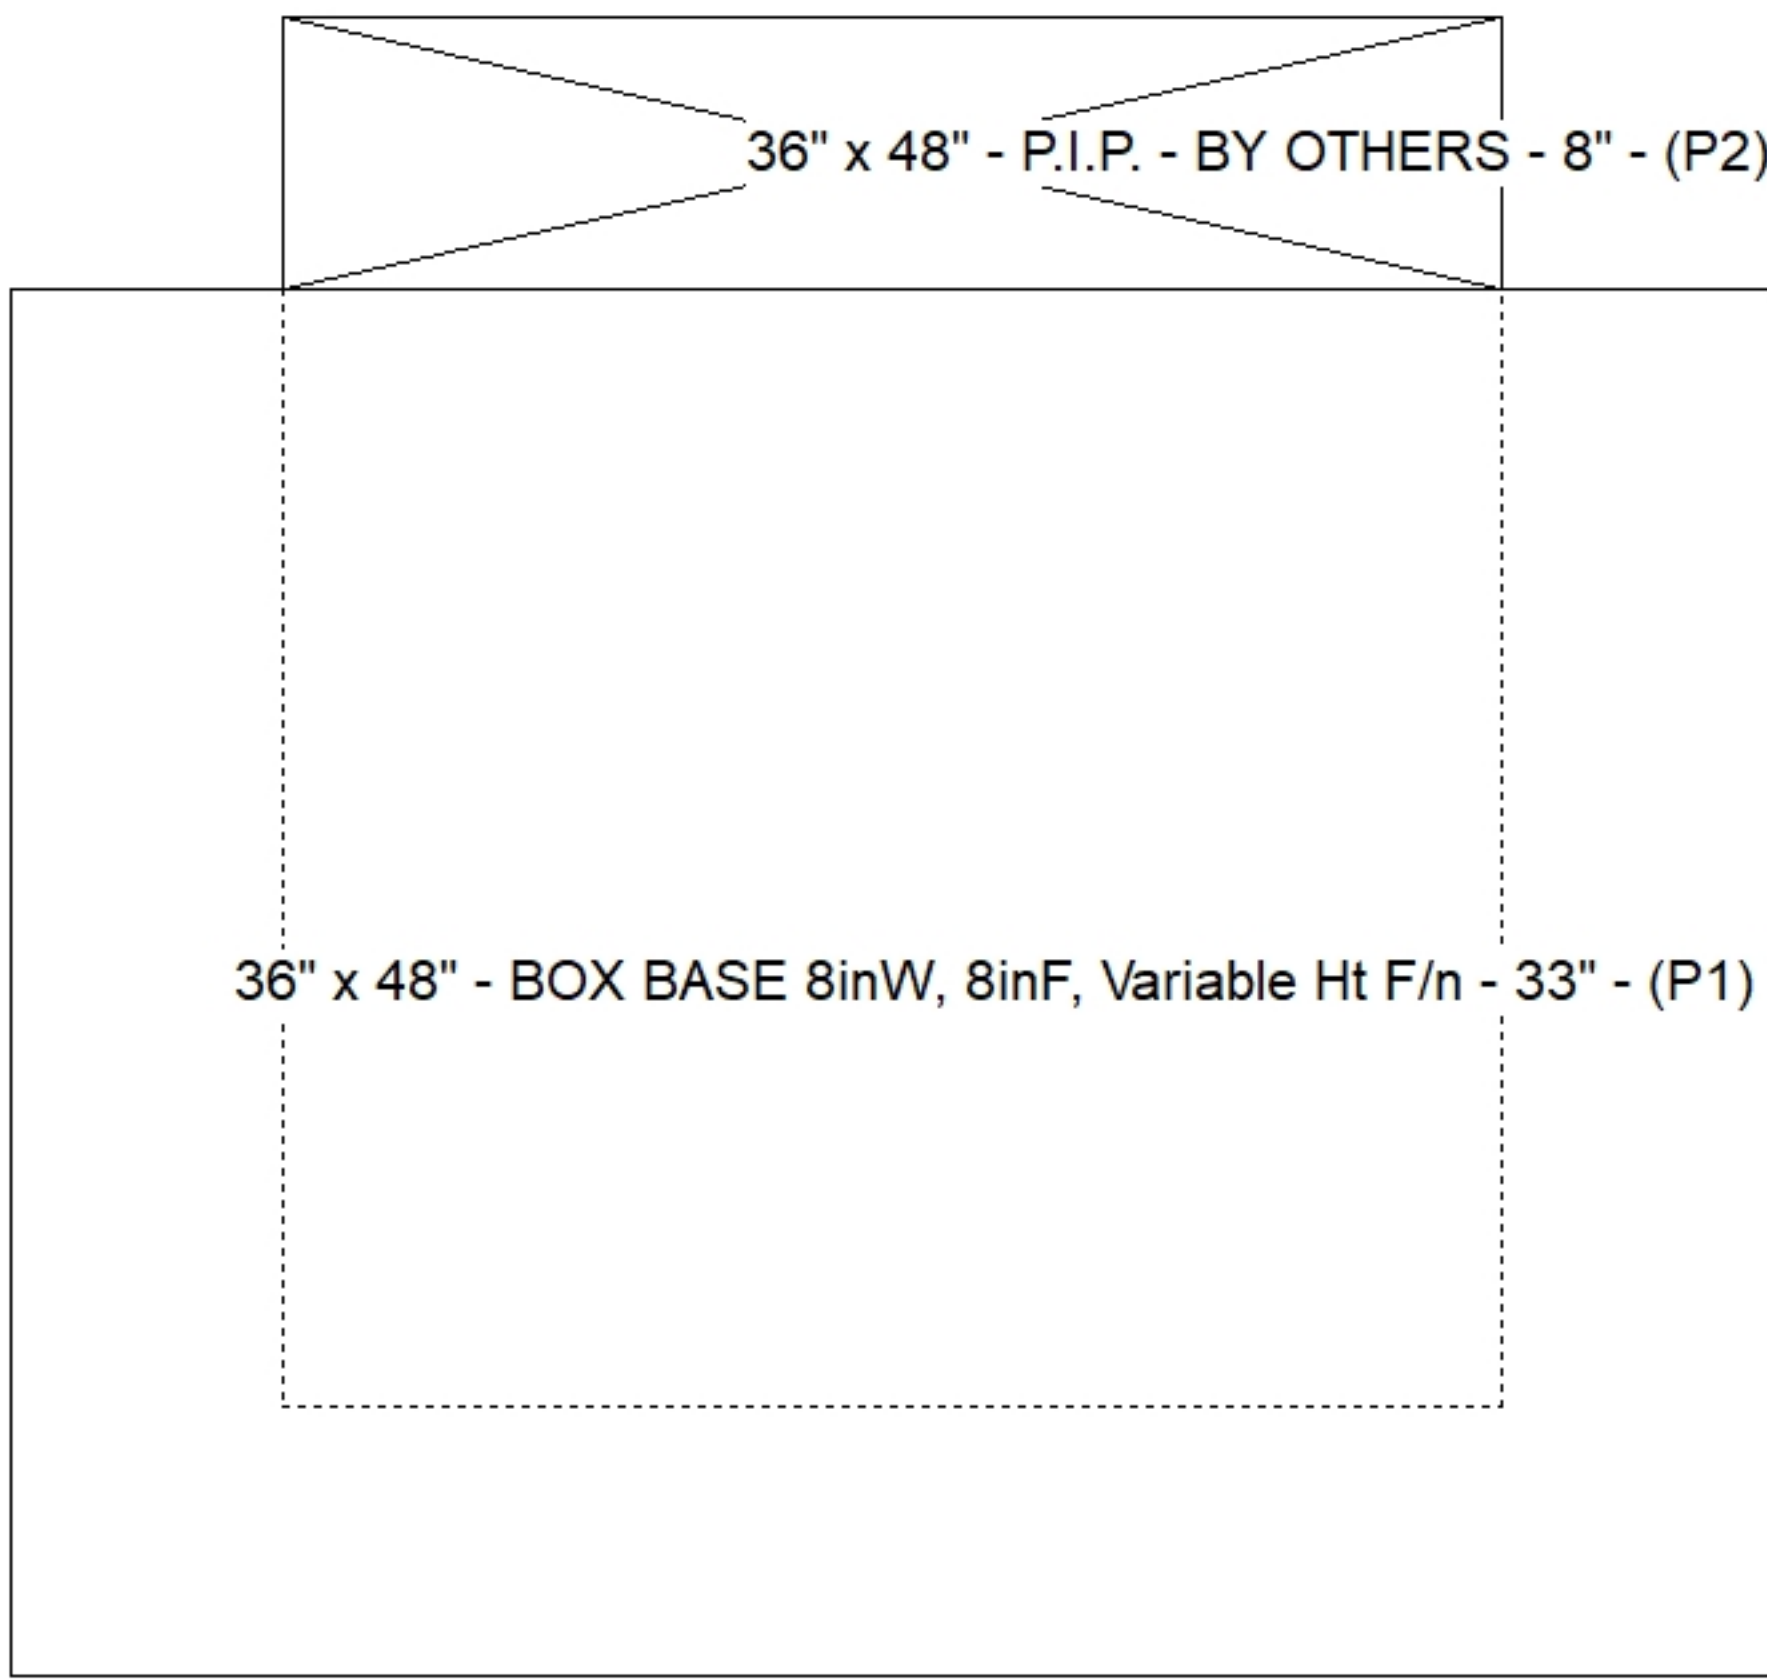

Submittal Drawing
7/20/2026 10:43:17 AM

SUBMITTAL
APPROVED BY:
