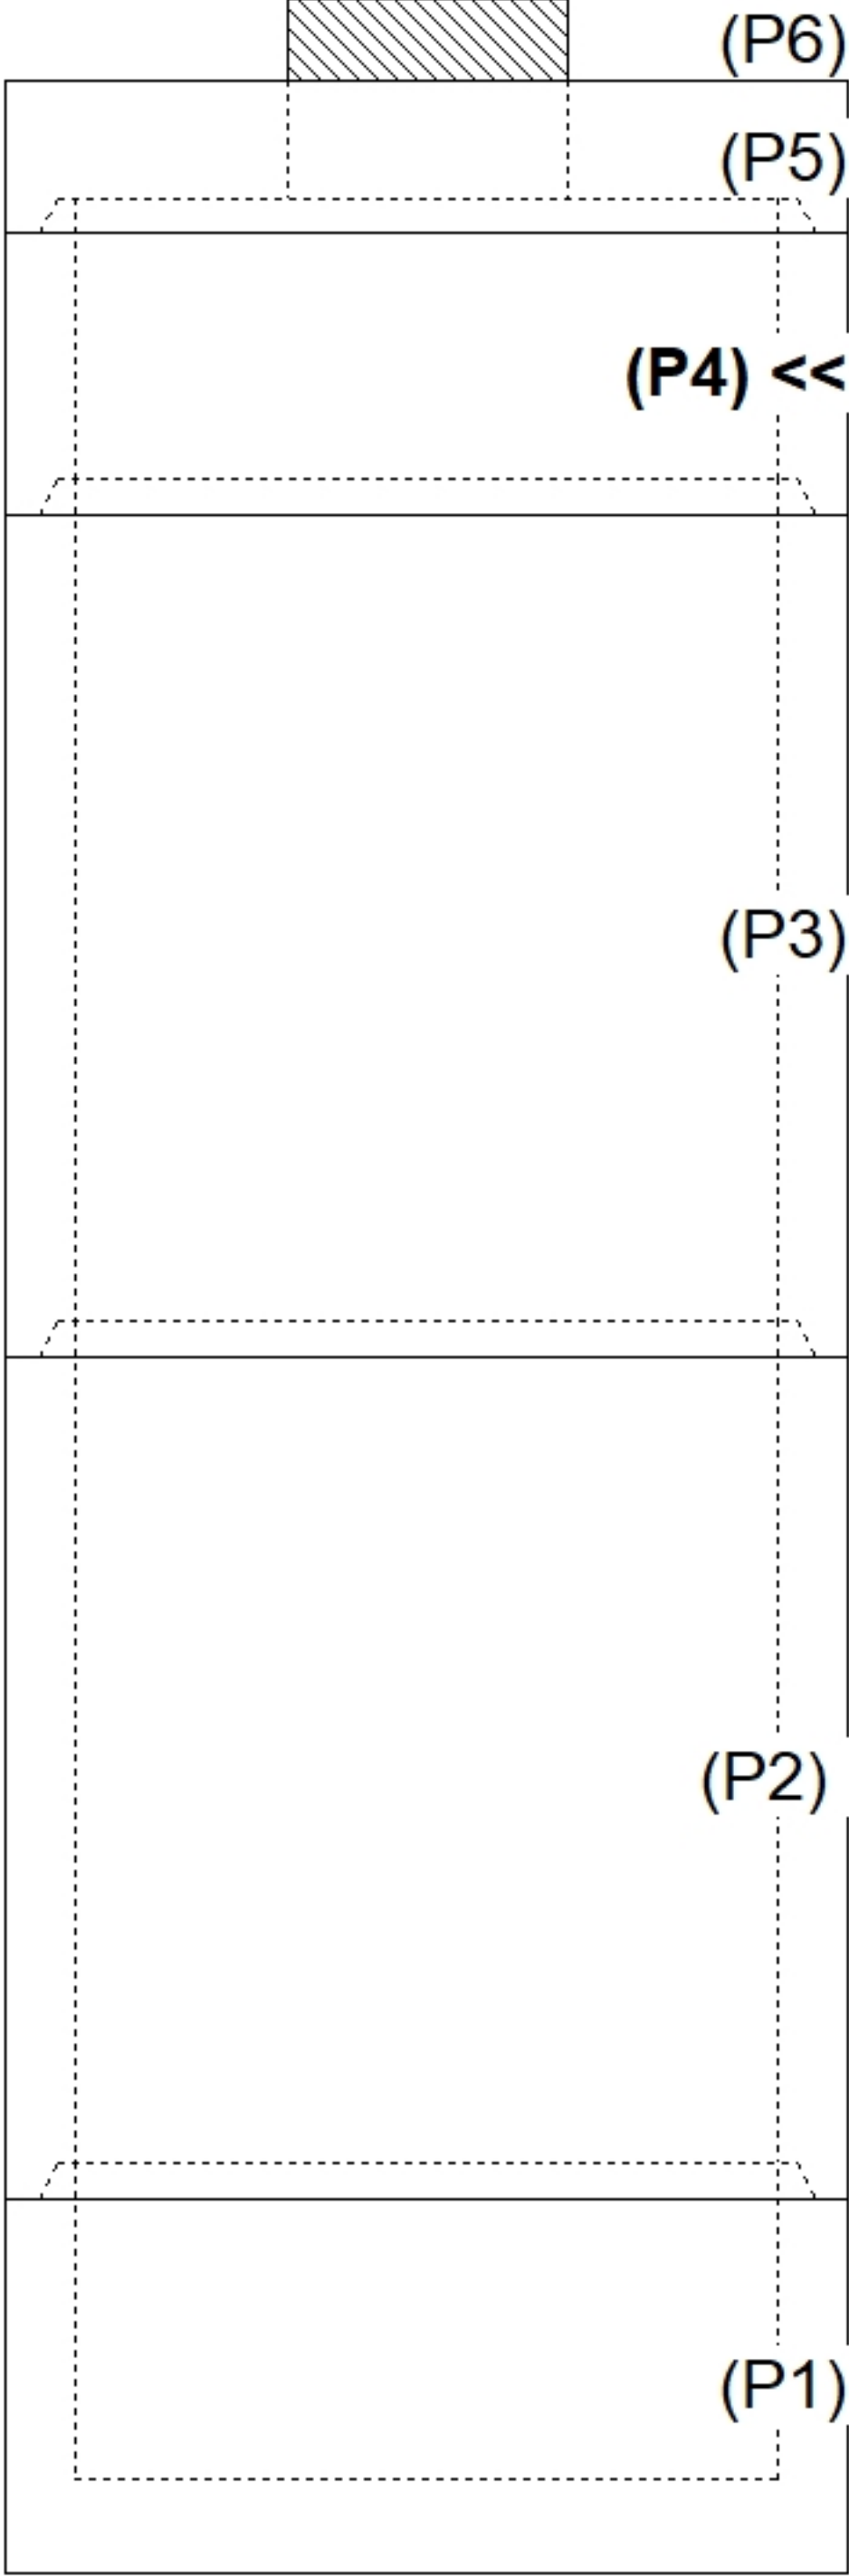
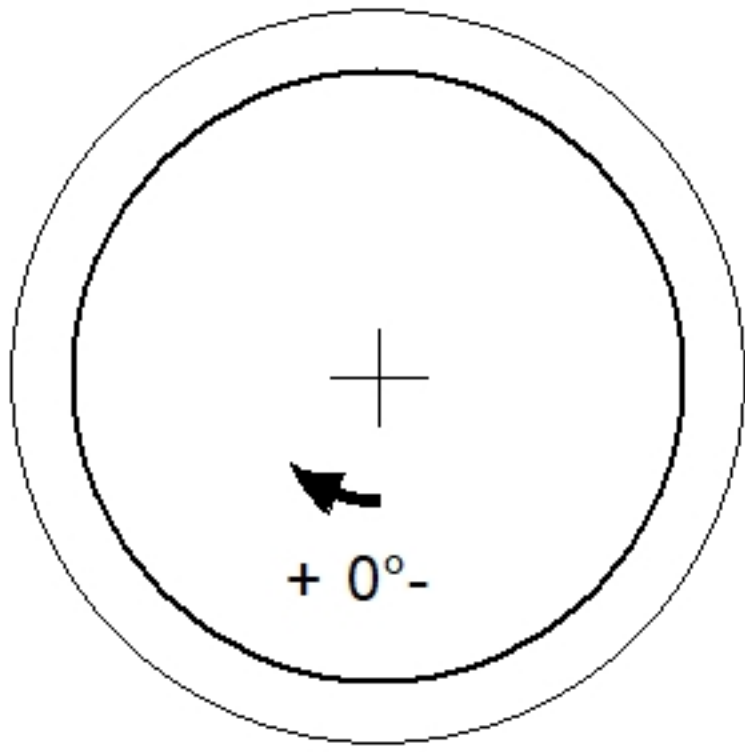
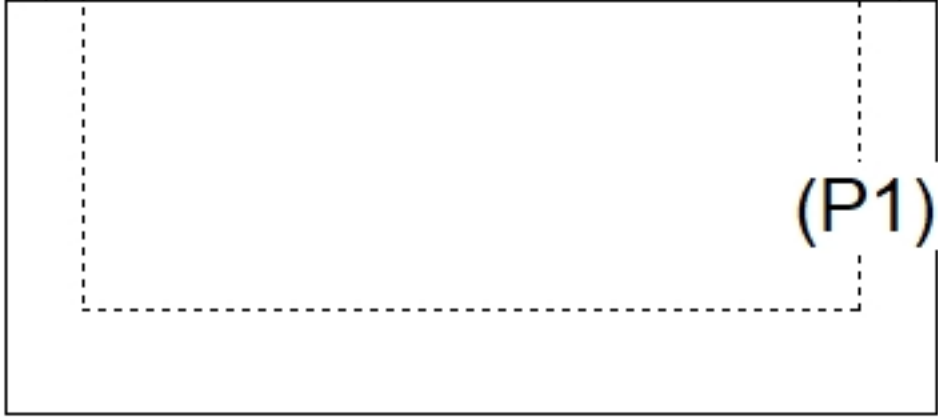
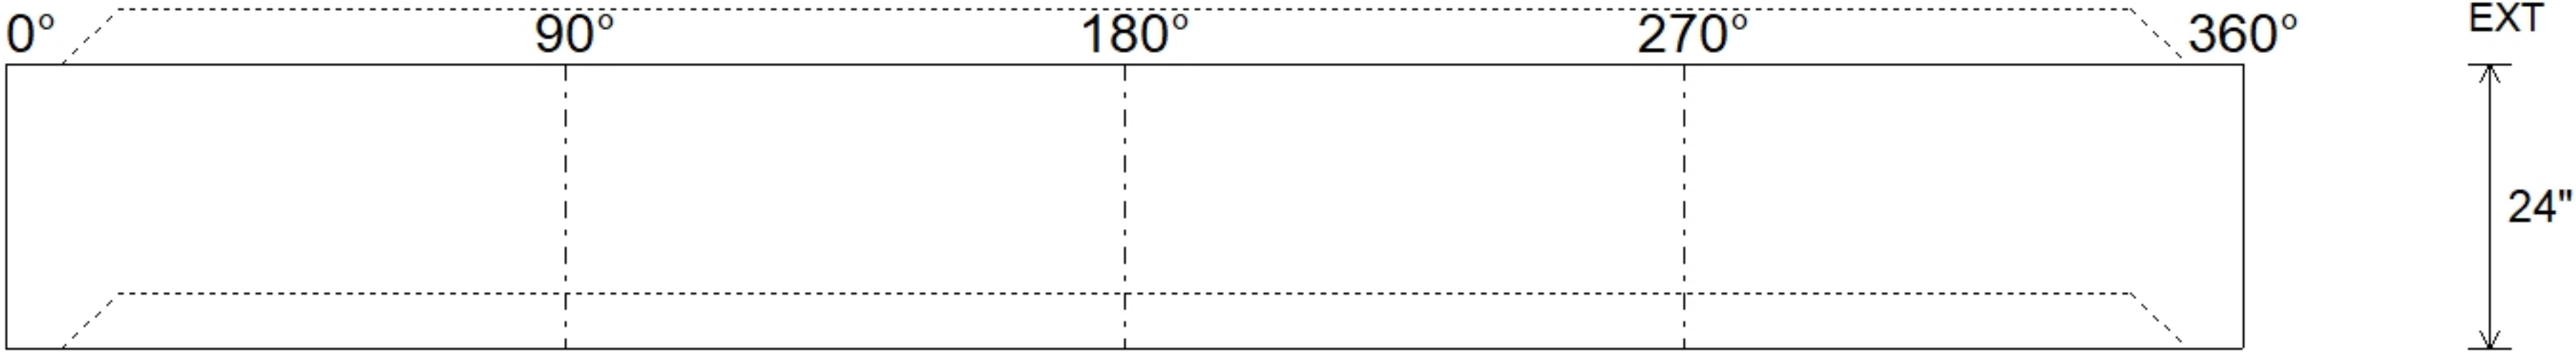


Job Name: 26-2736 ADS UA Local 52 Job Location: Louisville, KY Contractor: ADS Advanced Drainage Systems, Inc.					Plant: Beaver Dam 7/9/2026 9:09:21 AM		Tech: S. Felletter PC: T. Ryan						
Structure ID: S110													
P4			MH060RS24			MH RISER T/G							
P6) 24" - CASTING HEIGHT - 7" P5) 60" - MH FLAT TOP w/24" Ctr. Hole F/G - 13" P4) 60" - MH RISER T/G - 24" P3) 60" - MH RISER T/G - 72" P2) 60" - MH RISER T/G - 72" P1) 60" - MH BASE T/n - 24" 1) ASSEMBLY REQUIRED 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-375 F/C Storm 4) 60" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) Hole - 12						0 lb 2674 lb 2505 lb 7516 lb 7402 lb 5239 lb 0 lb 0 lb 0 lb 271 lb 0 lb 0 lb 0 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-375 F/C "STORM"). . REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - RISER/WALLS (As .18) - FLOOR (As .37) #5 BARS AT 10" C.C.E.W.					
Rim: 549.66' Rim to Invert: 11.04' Slack: 1.48" Sump: 81" Step Position:						Structure Total: 25607 lb							
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset			
Invert 1													
Invert 2													
Invert 3													
Invert 4													
Invert 5													
Invert 6													
Invert 7													
Invert 8													
RIGHT-SIDE UP VIEW (int. dimensions)													
													
INSIDE WALL DIMENSIONS													
													
Coating (Int): Coating (Ext):				Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 6" Floor Height: 0"		Height (Int): 24" Height (Ext): 24"		Weight (Net): 2505 lb Volume (Net): 0.64cu.yd			
