



Job Name: 26-2783 - Kentucky Livestock Innovation Center Job Location: Versailles, KY Contractor: Lagco Inc.					Plant: Beaver Dam 10/13/2026 12:57:17 PM		Tech: J. Coppage PC: M. Sullivan			
Structure ID: CI-2A1										
P1 BX2436-08BVF BOX BASE 8inW, 8inF, Variable Ht										
P2) 24" x 36" - CASTING HEIGHT - 6" P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 33" 1) CASTING - HOE 525 LV SET (F/G/H) 1) 24" x 36" - Conseal CS-102 1.00" 1) Hole - 16 1) Hole - 14 1) Hole - 6					0 lb 4506 lb 442 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 4948 lb		Structure Notes: 1. JR HOE HOE-525 LV SET PROVIDED BY ICAST 2. PER LEFUCG CBI TYPE D/ ASTM C913 SPEC'S. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (grade 60). - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 853.3' Rim to Invert: 3.3' Slack: 0.6" Sump: 0" Step Position:										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	850'	0°	20"	12" HDPE	14.5"	Hole 16	16"	16"	-1.25"	0"
Invert 2	850.1'	90°	26"	10" HDPE	11.4"	Hole 14	14"	14"	0.5"	0"
Invert 3	851.8'	180°	20"	4" HDPE (perf pipe)	4.8"	Hole 6	6"	6"	21.2"	0"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

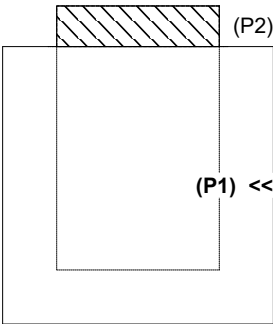

(P2)

(P1) <<

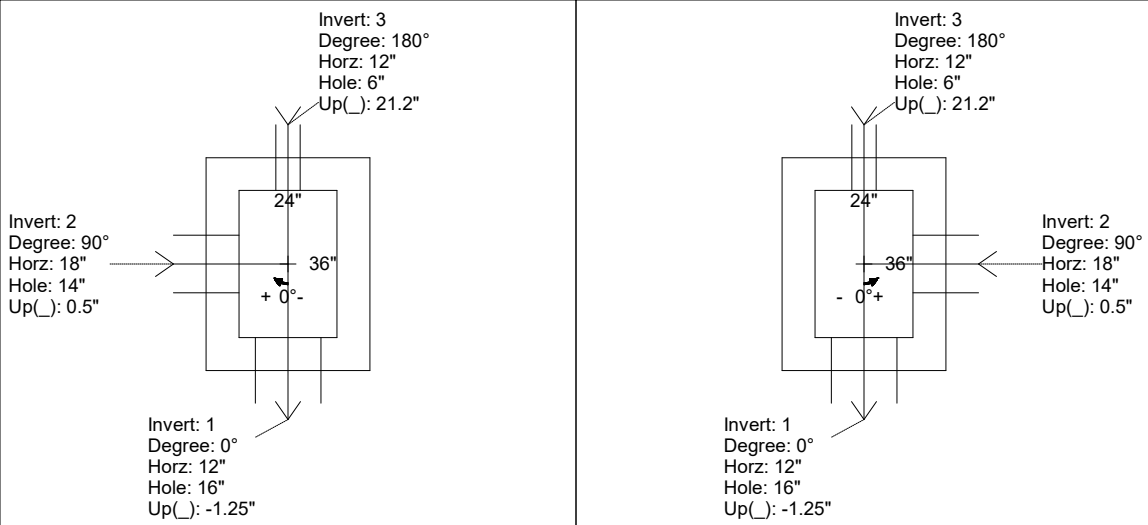


Invert: 3
Degree: 180°
Horz: 12"
Hole: 6"
Up(): 21.2"

Invert: 2
Degree: 90°
Horz: 18"
Hole: 14"
Up(): 0.5"

Invert: 1
Degree: 0°
Horz: 12"
Hole: 16"
Up(): -1.25"

(P1)

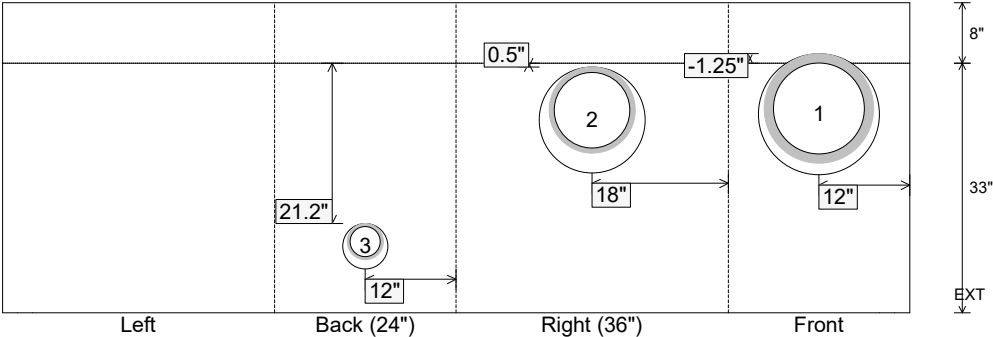

Left Back (24") Right (36") Front

EXT

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 33" Height (Ext): 41"	Weight (Net): 4506 lb Volume (Net): 1.15cu.yd
----------------------------------	-------------------------------	--	--	--
