



Job Name: 26-2783 - Kentucky Livestock Innovation Center Job Location: Versailles, KY Contractor: Lagco Inc.					Plant: Beaver Dam 10/13/2026 12:57:19 PM		Tech: J. Coppage PC: M. Sullivan			
Structure ID: CI-6B										
P1 BX2436-08BVF BOX BASE 8inW, 8inF, Variable Ht										
P2) 24" x 36" - CASTING HEIGHT - 6" P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 48" 1) CASTING - HOE 525 LV SET (F/G/H) 1) 24" x 36" - Conseal CS-102 1.00" 2) Hole - 24 1) Hole - 18 1) Hole - 6					0 lb 5465 lb 442 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 5907 lb		Structure Notes: 1. JR HOE HOE-525 LV SET PROVIDED BY ICAST 2. PER LEFUCG CBI TYPE D/ ASTM C913 SPEC'S. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (grade 60). - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 850' Rim to Invert: 4.51' Slack: 0.12" Sump: 0" Step Position:										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	845.49'	90°	26"	18" HDPE	21.2"	Hole 24	24"	24"	-1.6"	0"
Invert 2	845.59'	180°	20"	12" HDPE	14.5"	Hole 18	18"	18"	-0.05"	0"
Invert 3	848.3'	180°	20"	4" HDPE (perf pipe)	4.8"	Hole 6	6"	6"	33.32"	0"
Invert 4	845.59'	245°	22.191"	18" HDPE	21.2"	Hole 24	24"	26.481"	-0.4"	5"
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

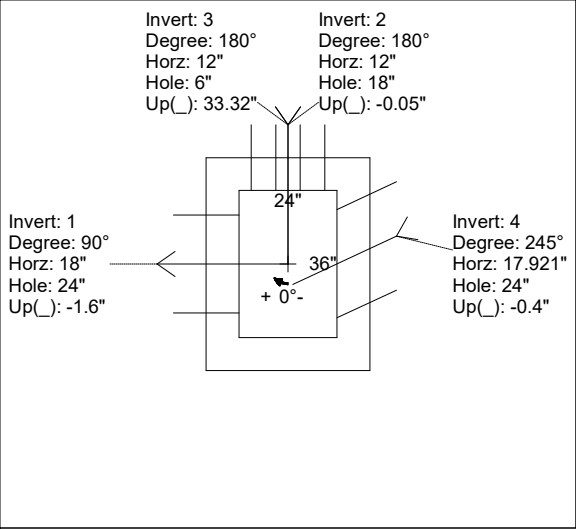

UPSIDE-DOWN VIEW (int. dimensions)

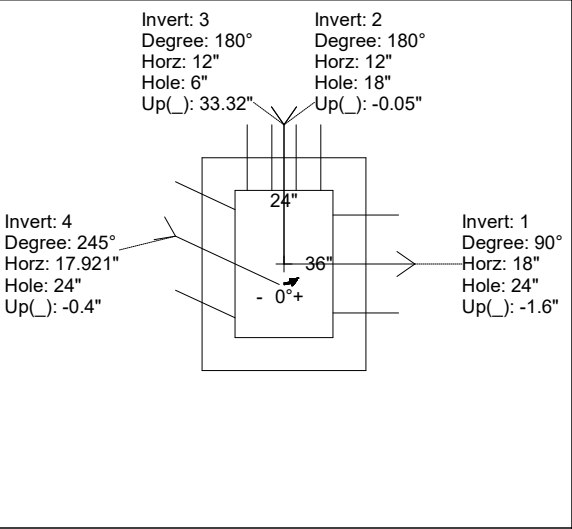

INSIDE WALL DIMENSIONS

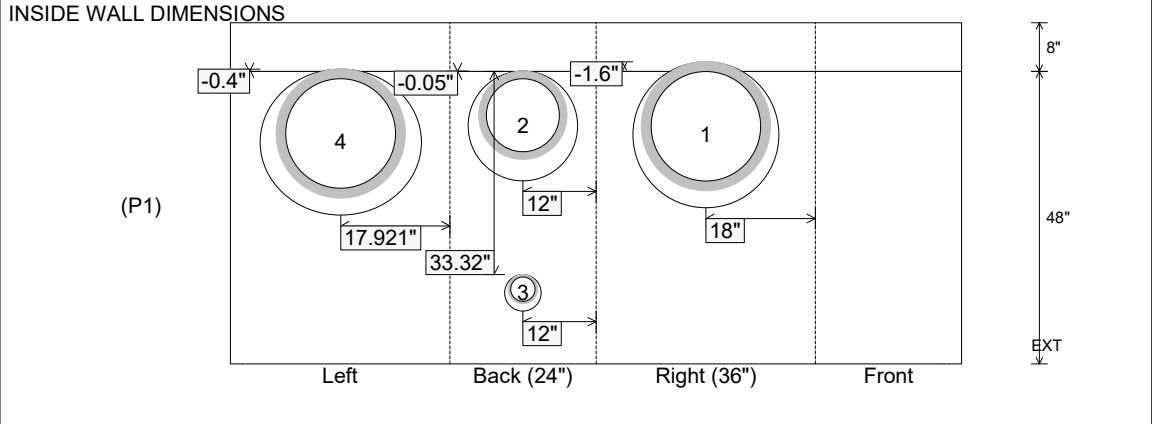

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 48" Height (Ext): 56"	Weight (Net): 5465 lb Volume (Net): 1.4cu.yd
----------------------------------	-------------------------------	--	--	---
