




Job Name: 26-2783 - Kentucky Livestock Innovation Center Job Location: Versailles, KY Contractor: Lagco Inc.					Plant: Beaver Dam 10/13/2026 12:57:03 PM		Tech: J. Coppage PC: M. Sullivan			
Structure ID: DI-3B2										
P1 BX2424-08BAVF BOX BASE 8inW, 8inF, Variable Ht										
P2) 24" x 24" - CASTING HEIGHT - 4" P1) 24" x 24" - BOX BASE 8inW, 8inF, Variable Ht - 32" 1) CASTING - HOE 280T F/G 1) 24" x 24" - Conseal CS-102 1.00" 1) Hole - 12 1) Hole - 6					0 lb 3729 lb 182 lb 0 lb 0 lb 0 lb ----- Structure Total: 3911 lb		Structure Notes: . 1. JR HOE HOE-280T F/G PROVIDED BY ICAST. 2. PER ASTM C913 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .12) #5 BARS AT 12" C.C.E.W. - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.			
Rim: 854.85' Rim to Invert: 3' Slack: 0" Sump: 0" Step Position:										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1	851.85'	0°	20"	8" HDPE	9.1"	Hole 12	12"	12"	-0.55"	0"
Invert 2	853.1'	180°	20"	4" HDPE (perf pipe)	4.8"	Hole 6	6"	6"	14.6"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

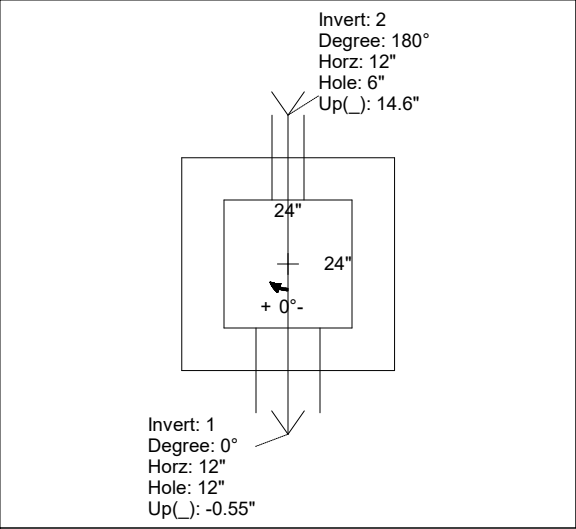

RIGHT-SIDE UP VIEW (int. dimensions)

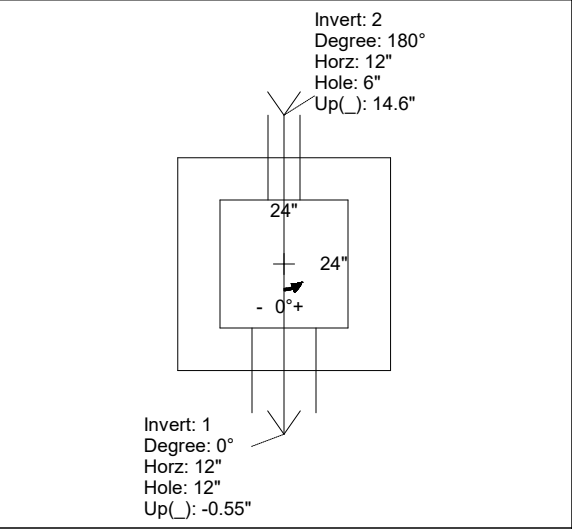


UPSIDE-DOWN VIEW (int. dimensions)

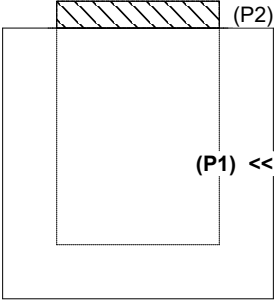

(P1) << (P2)

INSIDE WALL DIMENSIONS

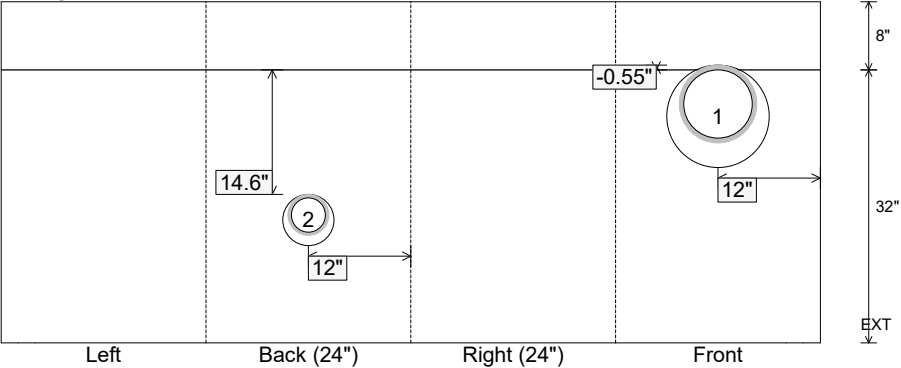

Left Back (24") Right (24") Front

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 32" Height (Ext): 40"	Weight (Net): 3729 lb Volume (Net): 0.95cu.yd
----------------------------------	-------------------------------	--	--	--
