




Job Name: 26-2783 - Kentucky Livestock Innovation Center Job Location: Versailles, KY Contractor: Lagco Inc.				Plant: Beaver Dam 10/13/2026 12:57:08 PM		Tech: J. Coppage PC: M. Sullivan				
Structure ID: DI-4A2										
P1 BX2424-08BAVF				BOX BASE 8inW, 8inF, Variable Ht						
P2) 24" x 24" - CASTING HEIGHT - 4" P1) 24" x 24" - BOX BASE 8inW, 8inF, Variable Ht - 47" 1) CASTING - HOE 280T F/G 1) 24" x 24" - Conseal CS-102 1.00" 1) Hole - 18 1) Hole - 12 1) Hole - 14						0 lb 4752 lb 182 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 4934 lb		Structure Notes: 1. JR HOE HOE-280T PROVIDED BY ICAST. 2. PER ASTM C913 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .12) #5 BARS AT 12" C.C.E.W. - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.		
Rim: 855.25' Rim to Invert: 4.3' Slack: 0.6" Sump: 0" Step Position:										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	850.95'	0°	20"	12" HDPE	14.5"	Hole 18	18"	18"	-1.25"	0"
Invert 2	851.05'	180°	20"	8" HDPE	9.1"	Hole 12	12"	12"	0.65"	0"
Invert 3	851.05'	245°	16.191"	10" HDPE	11.4"	Hole 14	14"	15.447"	0.5"	5"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

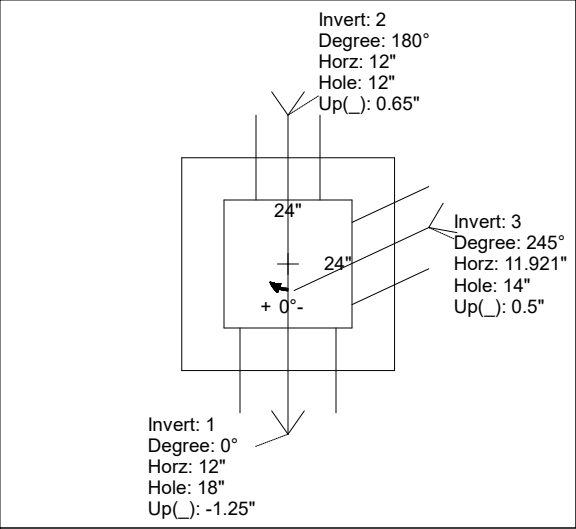


RIGHT-SIDE UP VIEW (int. dimensions)

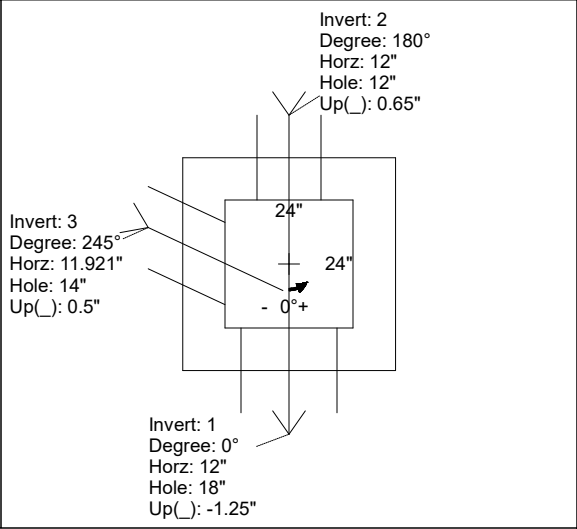

UPSIDE-DOWN VIEW (int. dimensions)

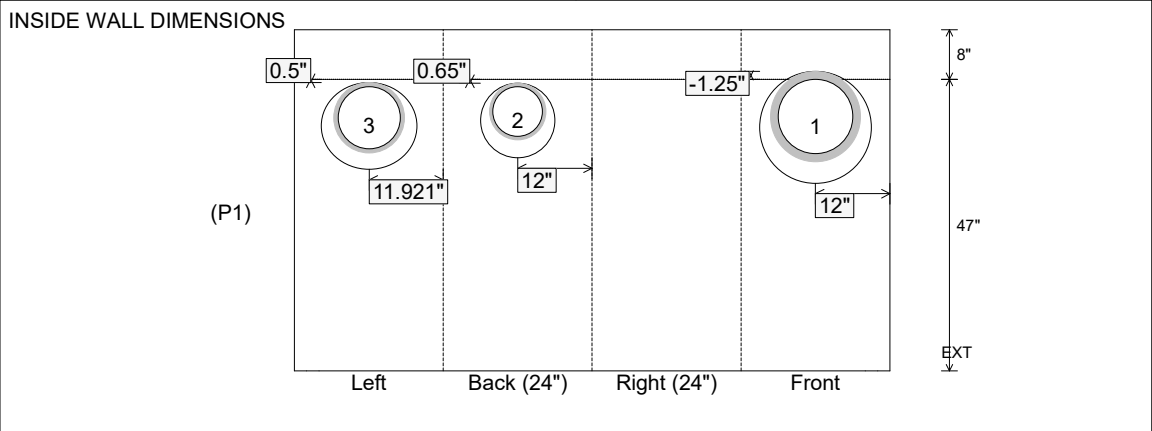

INSIDE WALL DIMENSIONS

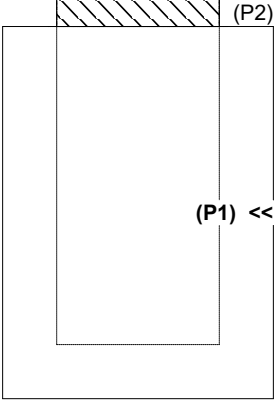

(P1) << (P2)

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 47" Height (Ext): 55"	Weight (Net): 4752 lb Volume (Net): 1.21cu.yd
----------------------------------	-------------------------------	--	--	--
