

Contractor: Core & Main LP

Plant: Beaver Dam



Size: 72" x 144"

Rim to Invert: 2.167'

Floor Height: 6"


Slack: 0"

2. CONCRETE = 4,500 PSI AT 28 DAYS.
3. SECONDARY POUR REQ'D - BAFFLE WALL.
4. REINFORCING PER ASTM A615 (GRADE 60)
FOR H-20 DESIGN LOADING.
- TOP SLAB (As .47) #5 BARS AT 8" C.C.E.W.
- WALLS (As .47) #5 BARS AT 8" C.C.E.W.
- FLOOR (As .47) #5 BARS AT 8" C.C.E.W.

2) PSX - 12-06 NYLO

0 lb
8190 lb
21177 lb
2190 lb
0 lb
16 lb


Structure Total: 31573 lb

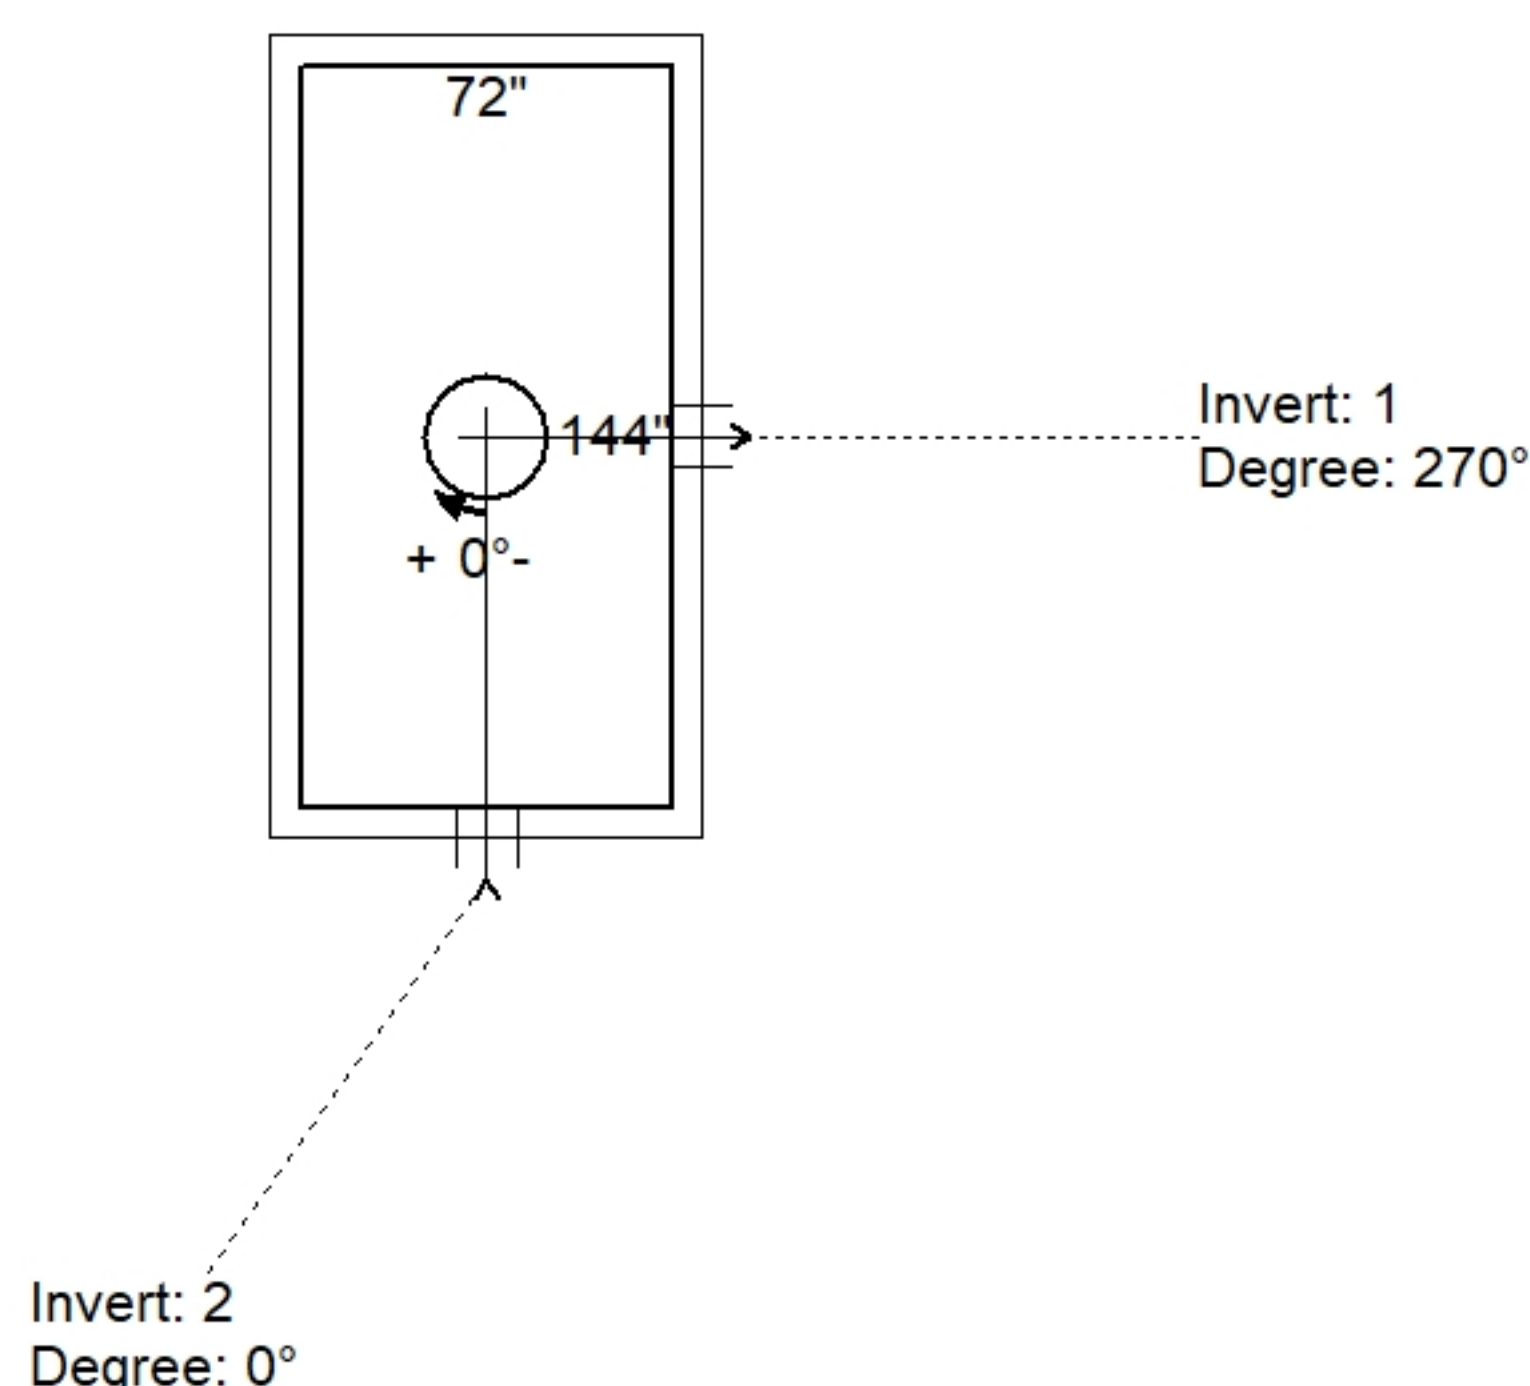

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (⌵)	Ref
Rim	6'							
Reducer								
Invert 1	3.833'	270°	6" PVC SDR35	6.25"	12"	PSX 12-06 NYLO	43"	P1
Invert 2	4'	0°	6" PVC SDR35	6.25"	12"	PSX 12-06 NYLO	45"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

72" x 144" - BOX BASE 6inW, 6inF, Variable Ht F/n - 64" - (P1)

Default - Interior Dimensions

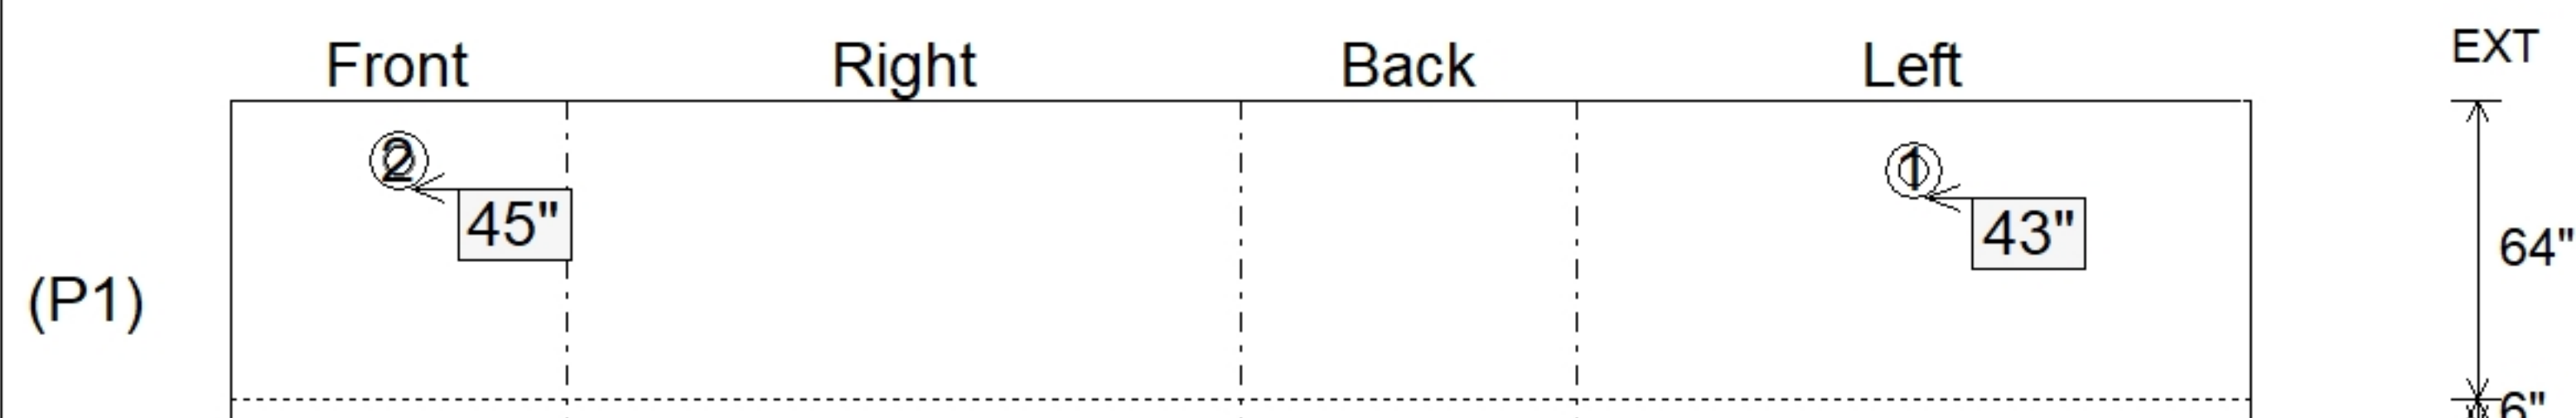

SUBMITTAL
APPROVED BY:
