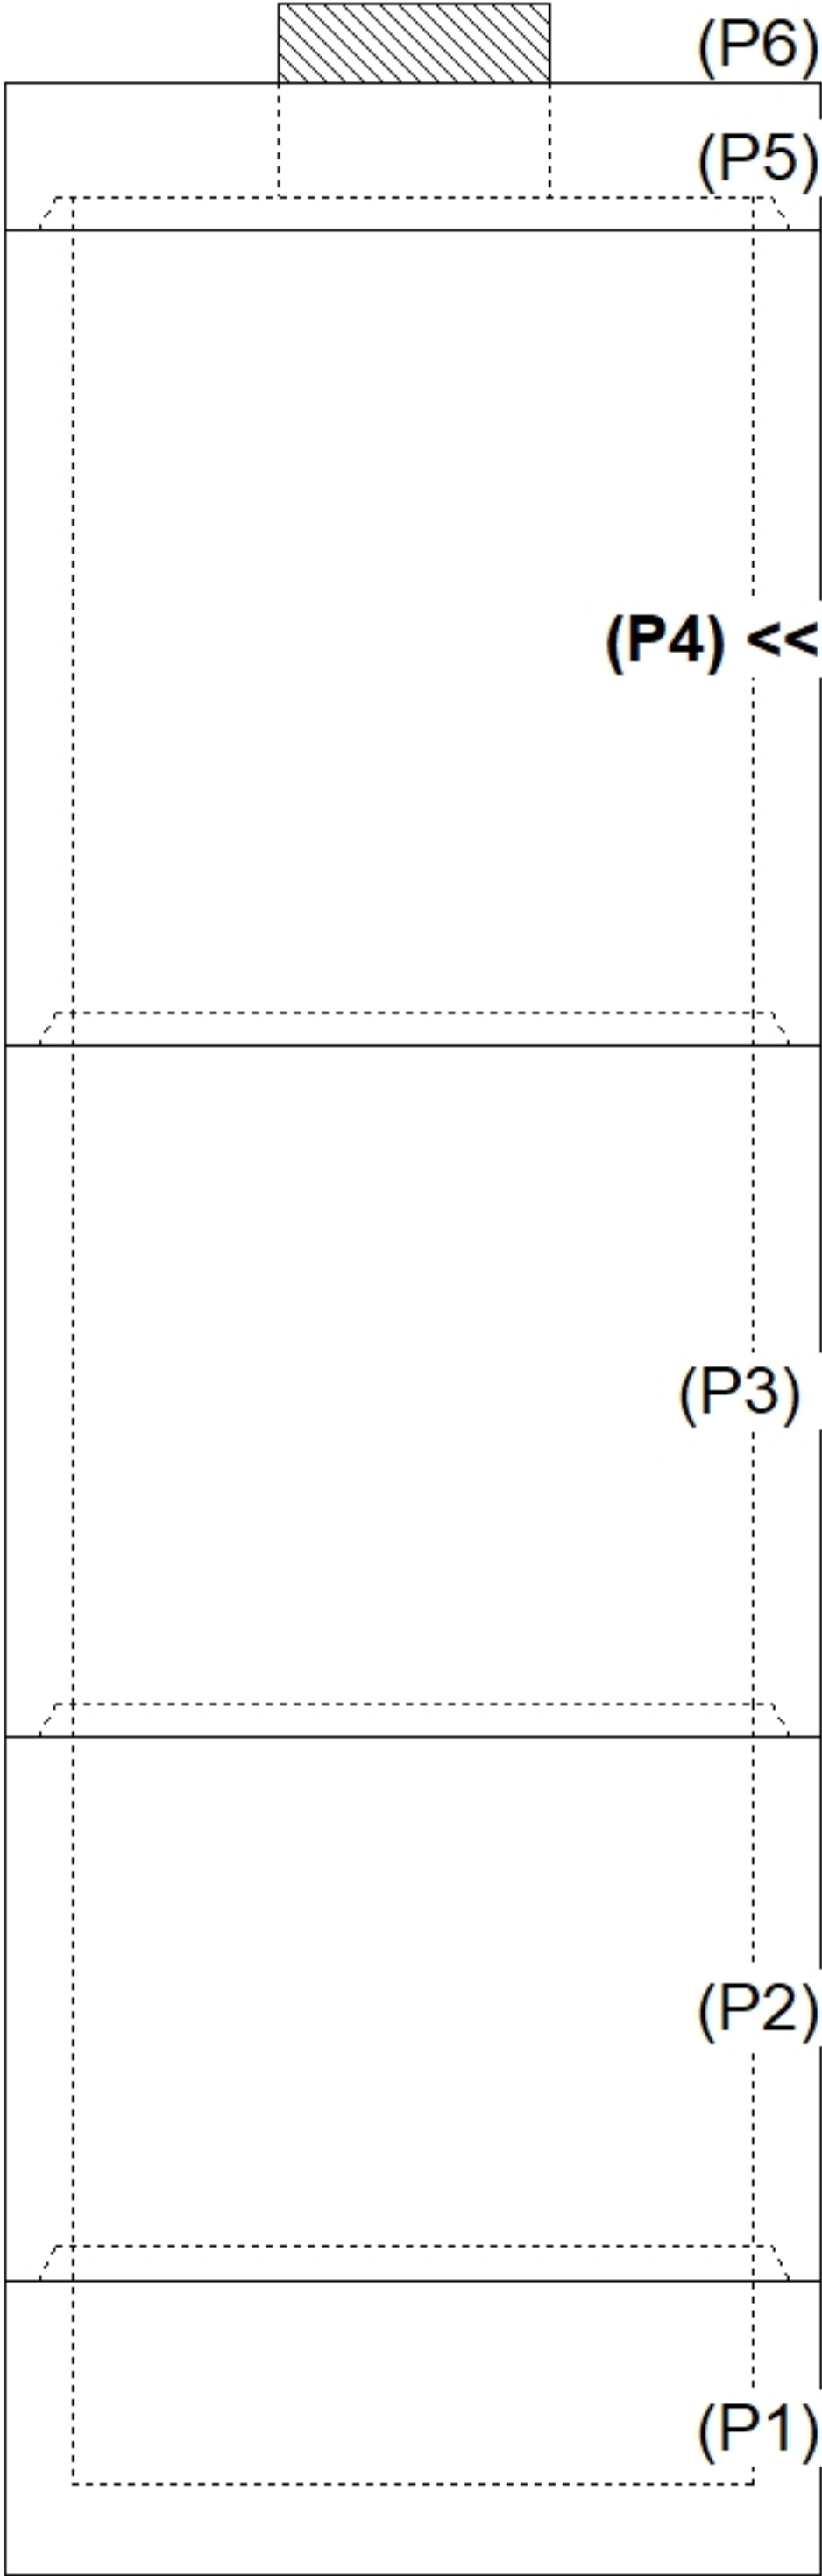
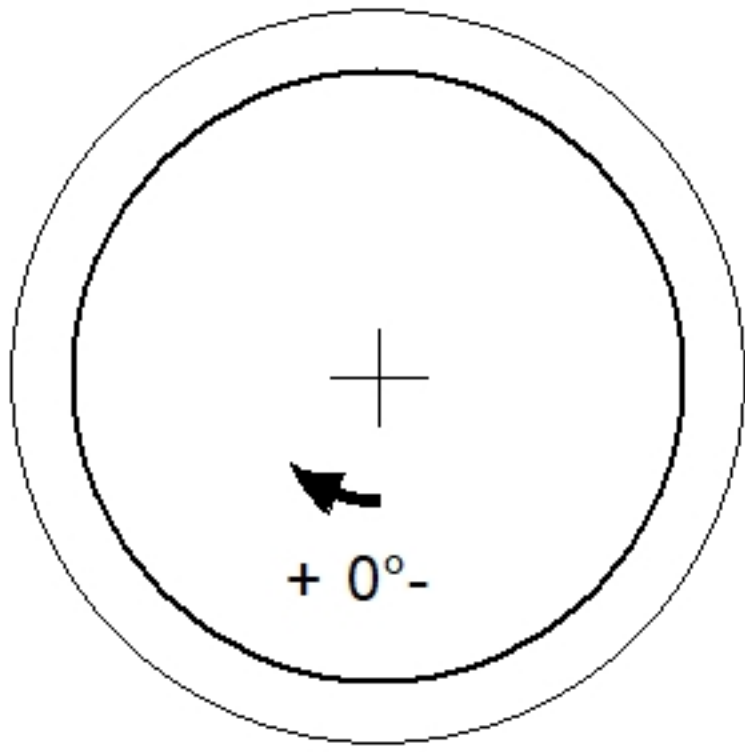
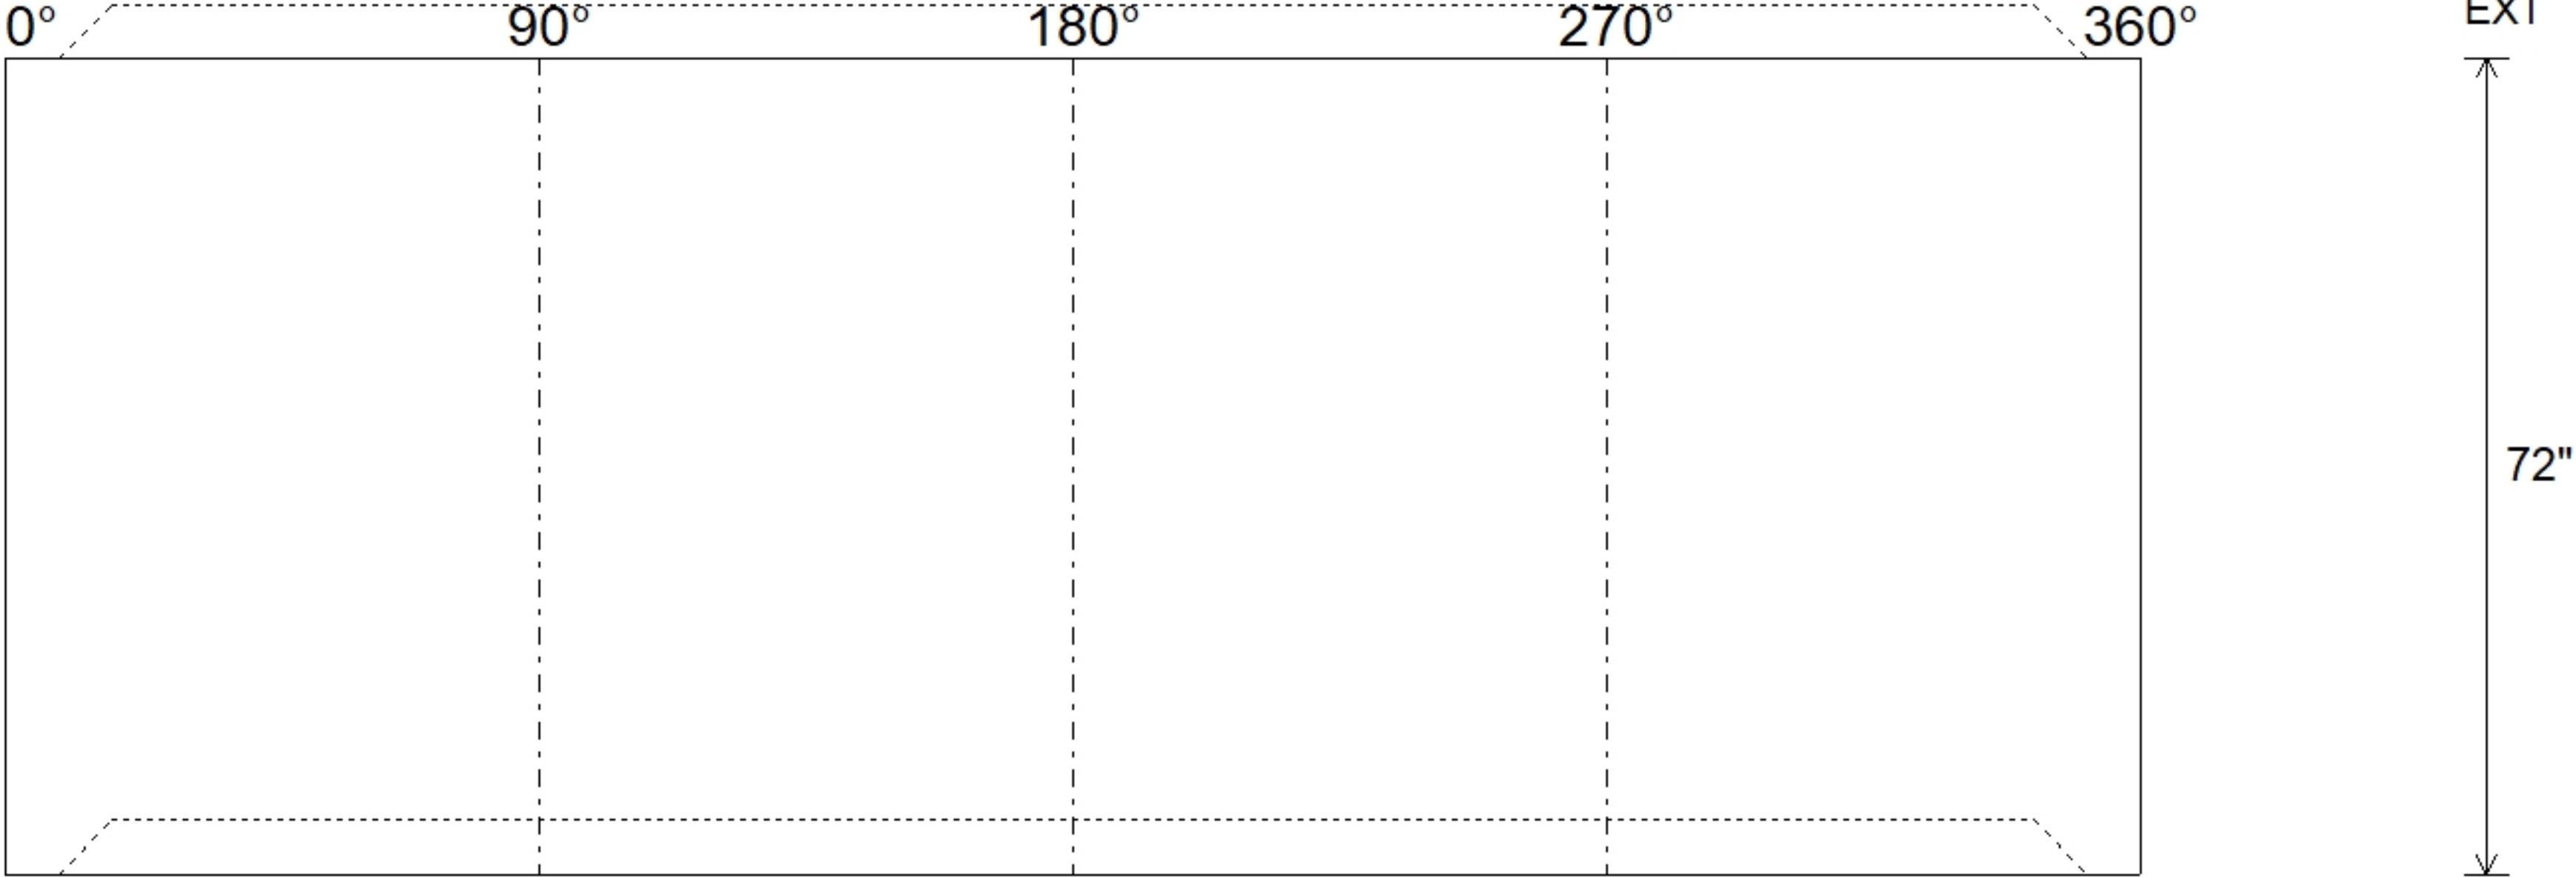


Job Name: 26-2976 ADS St. Charles at Park Hills Job Location: Park Hills, KY Contractor: ADS Advanced Drainage Systems, Inc.					Plant: Beaver Dam 7/23/2026 12:18:13 PM		Tech: S. Felletter PC: T. Ryan						
Structure ID: 4													
P4			MH060RS72			MH RISER T/G							
P6) 24" - CASTING HEIGHT - 7" P5) 60" - MH FLAT TOP w/24" Ctr. Hole F/G - 13" P4) 60" - MH RISER T/G - 72" P3) 60" - MH RISER Custom Ht T/G - 61" P2) 60" - MH RISER T/G - 48" P1) 60" - MH BASE T/n - 18" 1) ASSEMBLY REQUIRED 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-375 F/C Storm 4) 60" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) Hole - 38						0 lb 2674 lb 7516 lb 5148 lb 5011 lb 4612 lb 0 lb 0 lb 0 lb 271 lb 0 lb 0 lb 0 lb Structure Total: 25232 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-375 F/C "STORM"). 4. LIFT ANCHORS TO BE ON THE OUTSIDE OF THE STRUCTURE. 5. P2 & P3 RISERS TO BE MECHANICALLY ATTACHED PRIOR TO INTERNAL INSTALLATION/DELIVERY. - REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - RISER/WALLS (As .18) - FLOOR (As .37) #5 BARS AT 10" C.C.E.W.					
Rim: 828.73'		Rim to Invert: 11.58'		Slack: 0.96"		Sump: 81"		Step Position:					
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset			
Invert 1													
Invert 2													
Invert 3													
Invert 4													
Invert 5													
Invert 6													
Invert 7													
Invert 8													
RIGHT-SIDE UP VIEW (int. dimensions)													
													
INSIDE WALL DIMENSIONS													
													
Coating (Int): Coating (Ext):				Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 6" Floor Height: 0"		Height (Int): 72" Height (Ext): 72"		Weight (Net): 7516 lb Volume (Net): 1.92cu.yd			
