

Job Name: 26-3040 Shun Pike Storm  
Job Location: Nicholasville, KY  
Contractor: PECCO Eng

Plant: Beaver Dam

Tech: S. Felletter

7/20/2026 10:32:32 AM

PC: E. Bradley



## Structure ID: 1

**P4 GR24x36x6x3**

**GRADE RING 6"W F/F**

P5) 24" x 36" - CASTING HEIGHT - 4"  
P4) 24" x 36" - GRADE RING 6"W F/F - 3"  
P3) 24" x 36" - GRADE RING 6"W F/F - 3"  
P2) 24" x 36" - GRADE RING 6"W F/F - 3"  
P1) 24" x 36" - KNOCKOUT BASE 6"W/F - STOCK F/n - 42"  
1) CASTING - HOE 518 F/G  
4) 24" x 36" - Con Seal CS-102 1.00"


Structure Total:

0 lb  
218 lb  
218 lb  
218 lb  
2466 lb  
354 lb  
0 lb  
-----  
3473 lb

**Structure Notes:** 1. PER ASTM C913 SPECIFICATIONS.  
2. CONCRETE = 4,000 PSI AT 28 DAYS.  
3. NO INVERT CHANNEL.  
4. REINFORCING PER ASTM A615 (GRADE 60).  
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.  
- WALLS (As .12) #5 BARS AT 12" C.C.E.W.  
- FLOOR (As .12) #5 BARS AT 12" C.C.E.W.

### NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE = 4,000 PSI @ 28 DAYS.
3. REINFORCING: #4 BAR AS SHOWN (GRADE 60 KSI).
4. LIFTS: 2 EA. CONAC .8 TON WIRE ROPE ANCHORS REQUIRED.

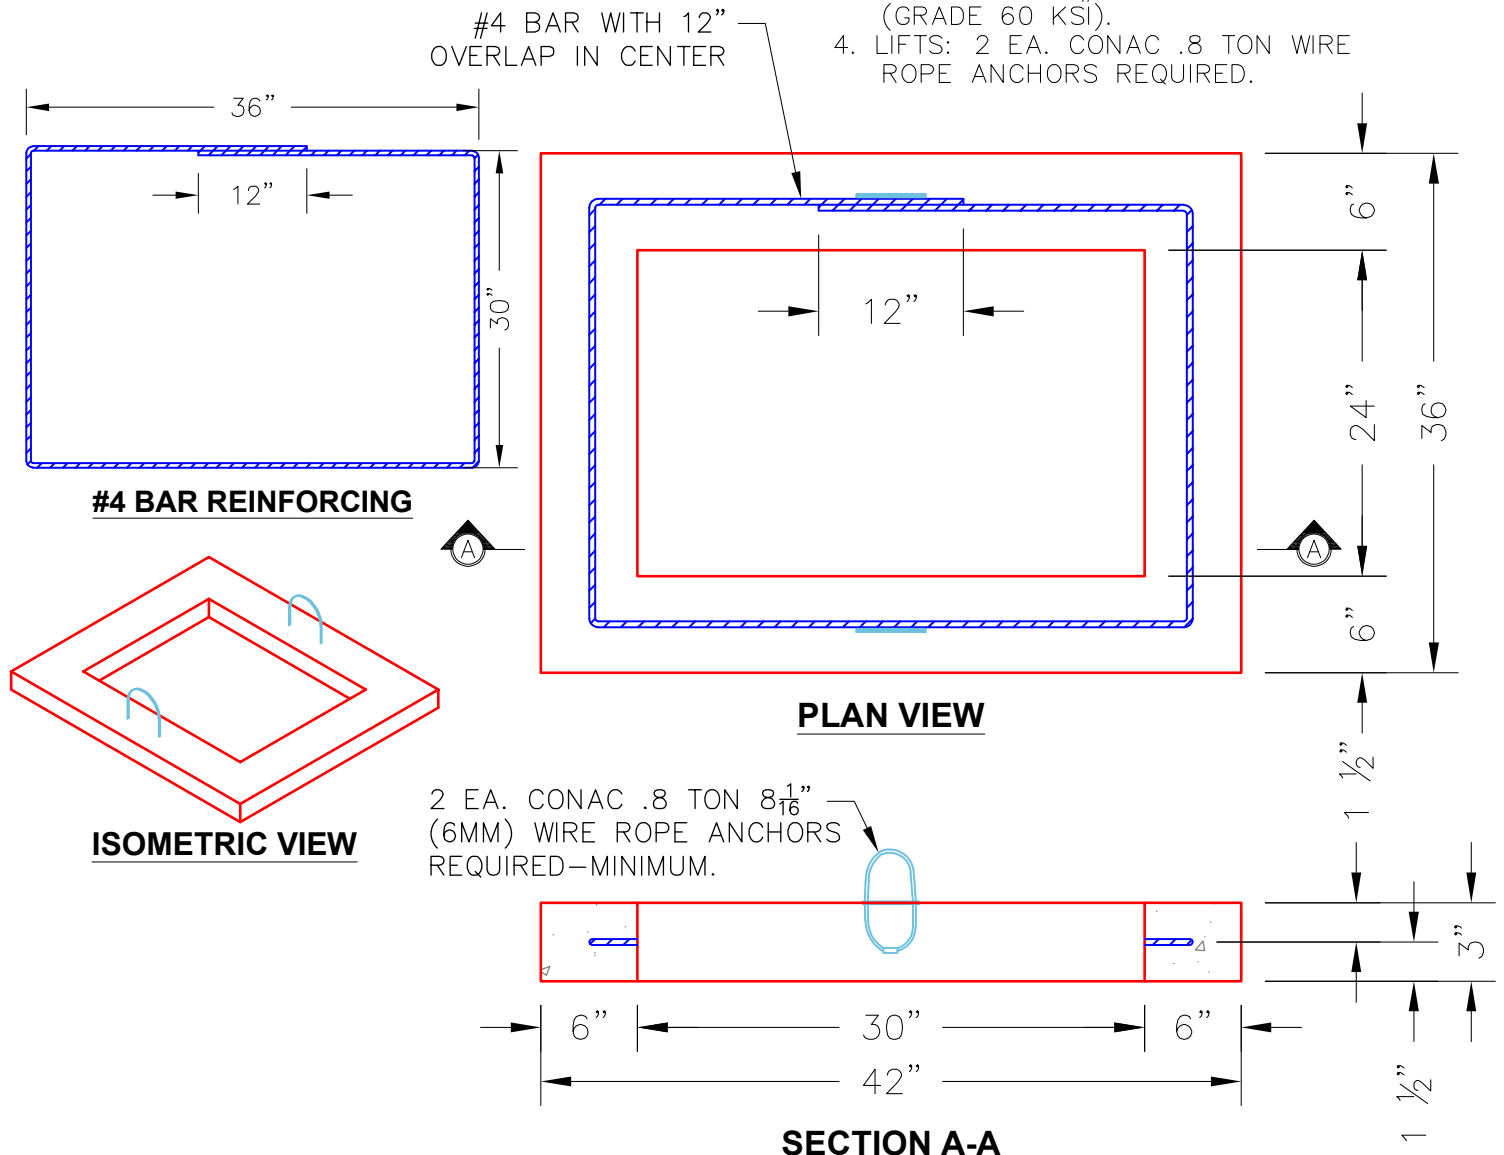

Coating (Int):  
Coating (Ext):

Seam Up: Flat  
Seam Dn: Flat

Wall Thickness: 6"

Height (Ext): 3"

Weight (Net): 217 lb  
Volume (Net): 0.06cu.yd
