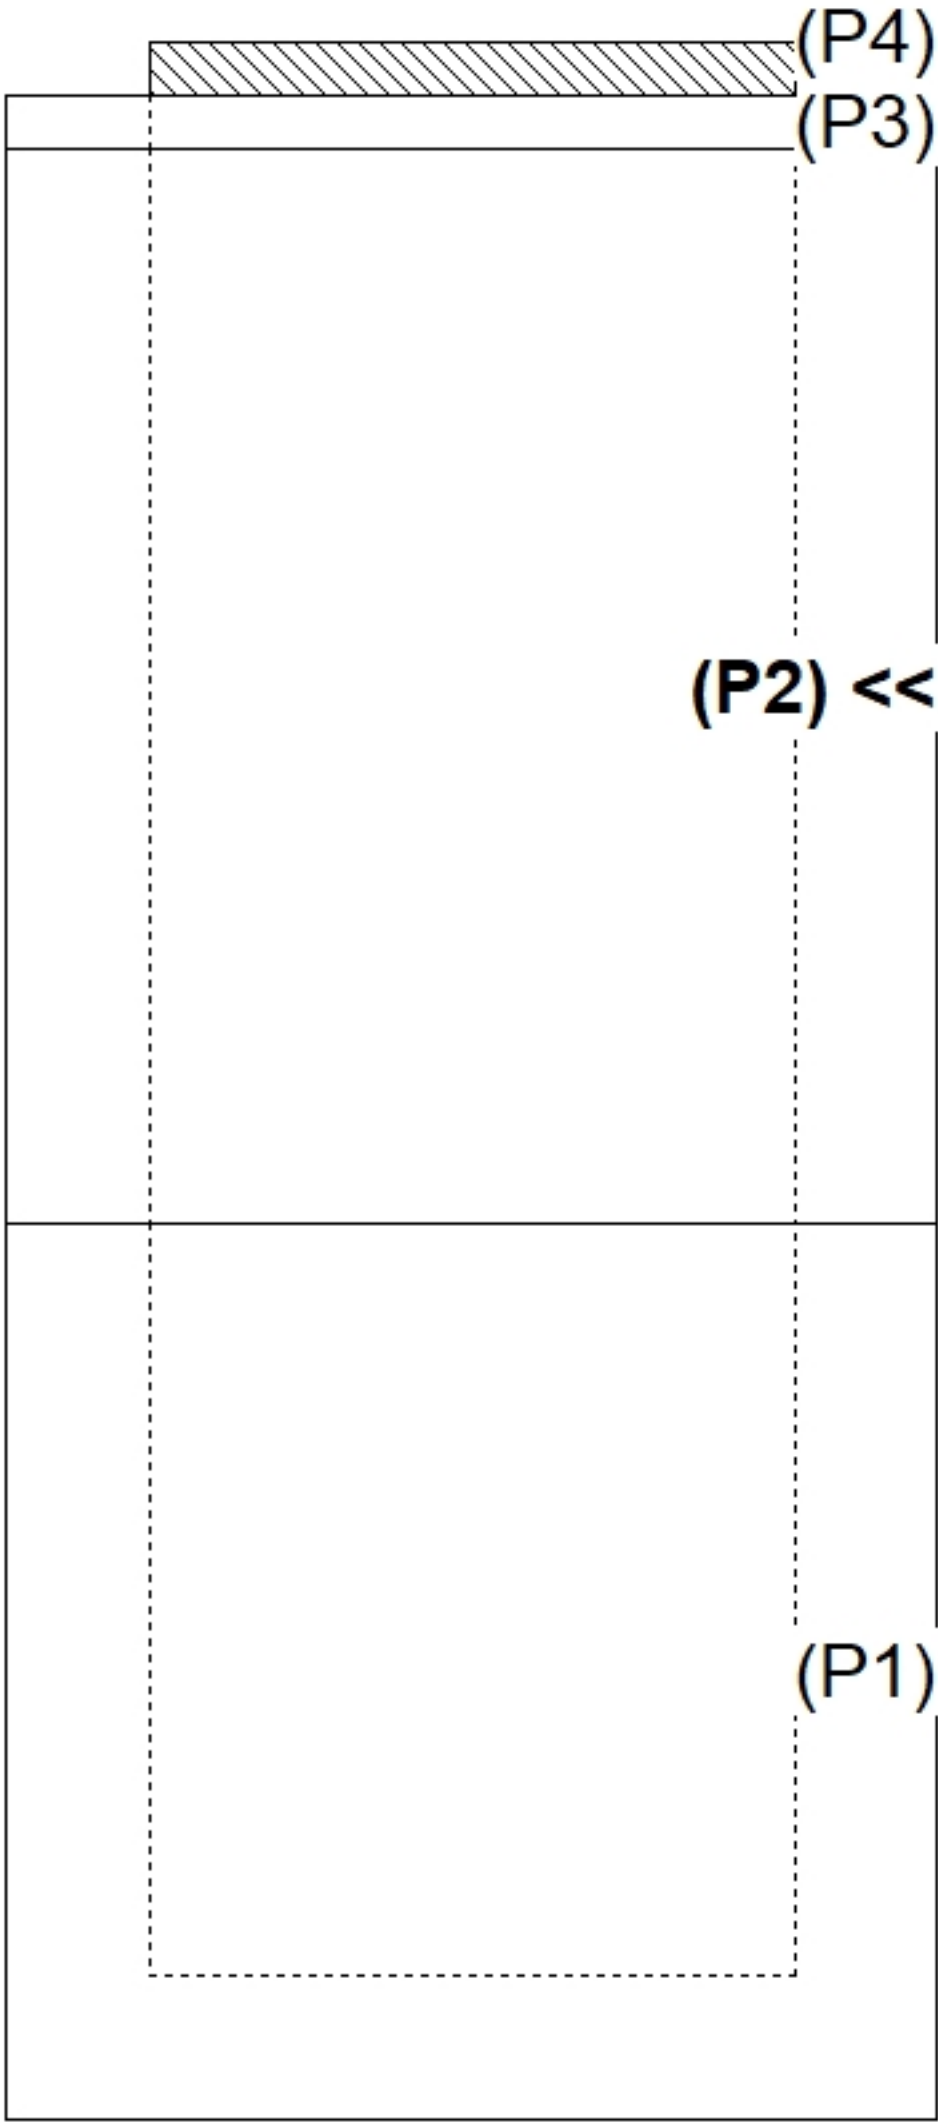
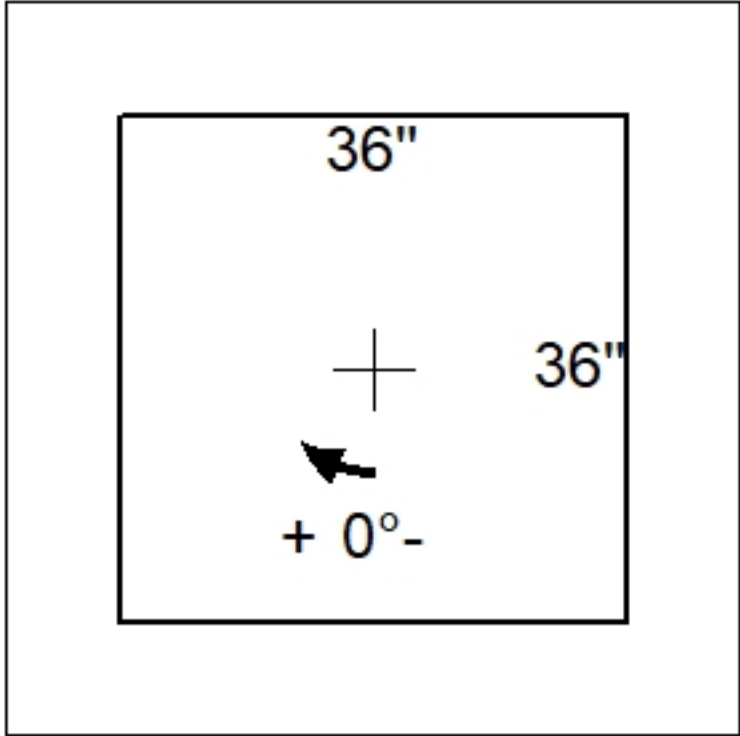


Job Name: 26-3108 Proximo Job Location: Lawrenceburg, IN Contractor: Dave Omara Contractor, Inc.					Plant: Beaver Dam 7/23/2026 11:20:56 AM		Tech: S. Felletter PC: M. Sullivan				
Structure ID: QL1											
P2		BX3636-08R60			BOX RISER 8inW F/F						
P4) 36" x 36" - CASTING HEIGHT - 3" P3) 36" x 36" - GRADE RING F/F - 3" P2) 36" x 36" - BOX RISER 8inW F/F - 60" P1) 36" x 36" - KNOCKOUT BASE 8"W/F - STOCK F/n - 42" 3) 36" x 36" - Conseal CS-102 1.00"						0 lb 354 lb 7089 lb 6777 lb 0 lb ----- Structure Total: 14221 lb		Structure Notes: 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO INVERT CHANNEL. 4. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - WALLS (As .12) #5 BARS AT 12" C.C.E.W. - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.			
Rim: 9'		Rim to Invert: 0'		Slack: 0"		Sump: 108"		Step Position:			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)											
											
		INSIDE WALL DIMENSIONS									
(P2) <<		Front				Right (36")		Back (36")		Left	
											
(P1)		(P2)								EXT 60"	
Coating (Int): Coating (Ext):				Seam Up: Flat Seam Dn: Flat		Wall Thickness: 8" Floor Height: 0"		Height (Int): 60" Height (Ext): 60"		Weight (Net): 7089 lb Volume (Net): 1.81cu.yd	
