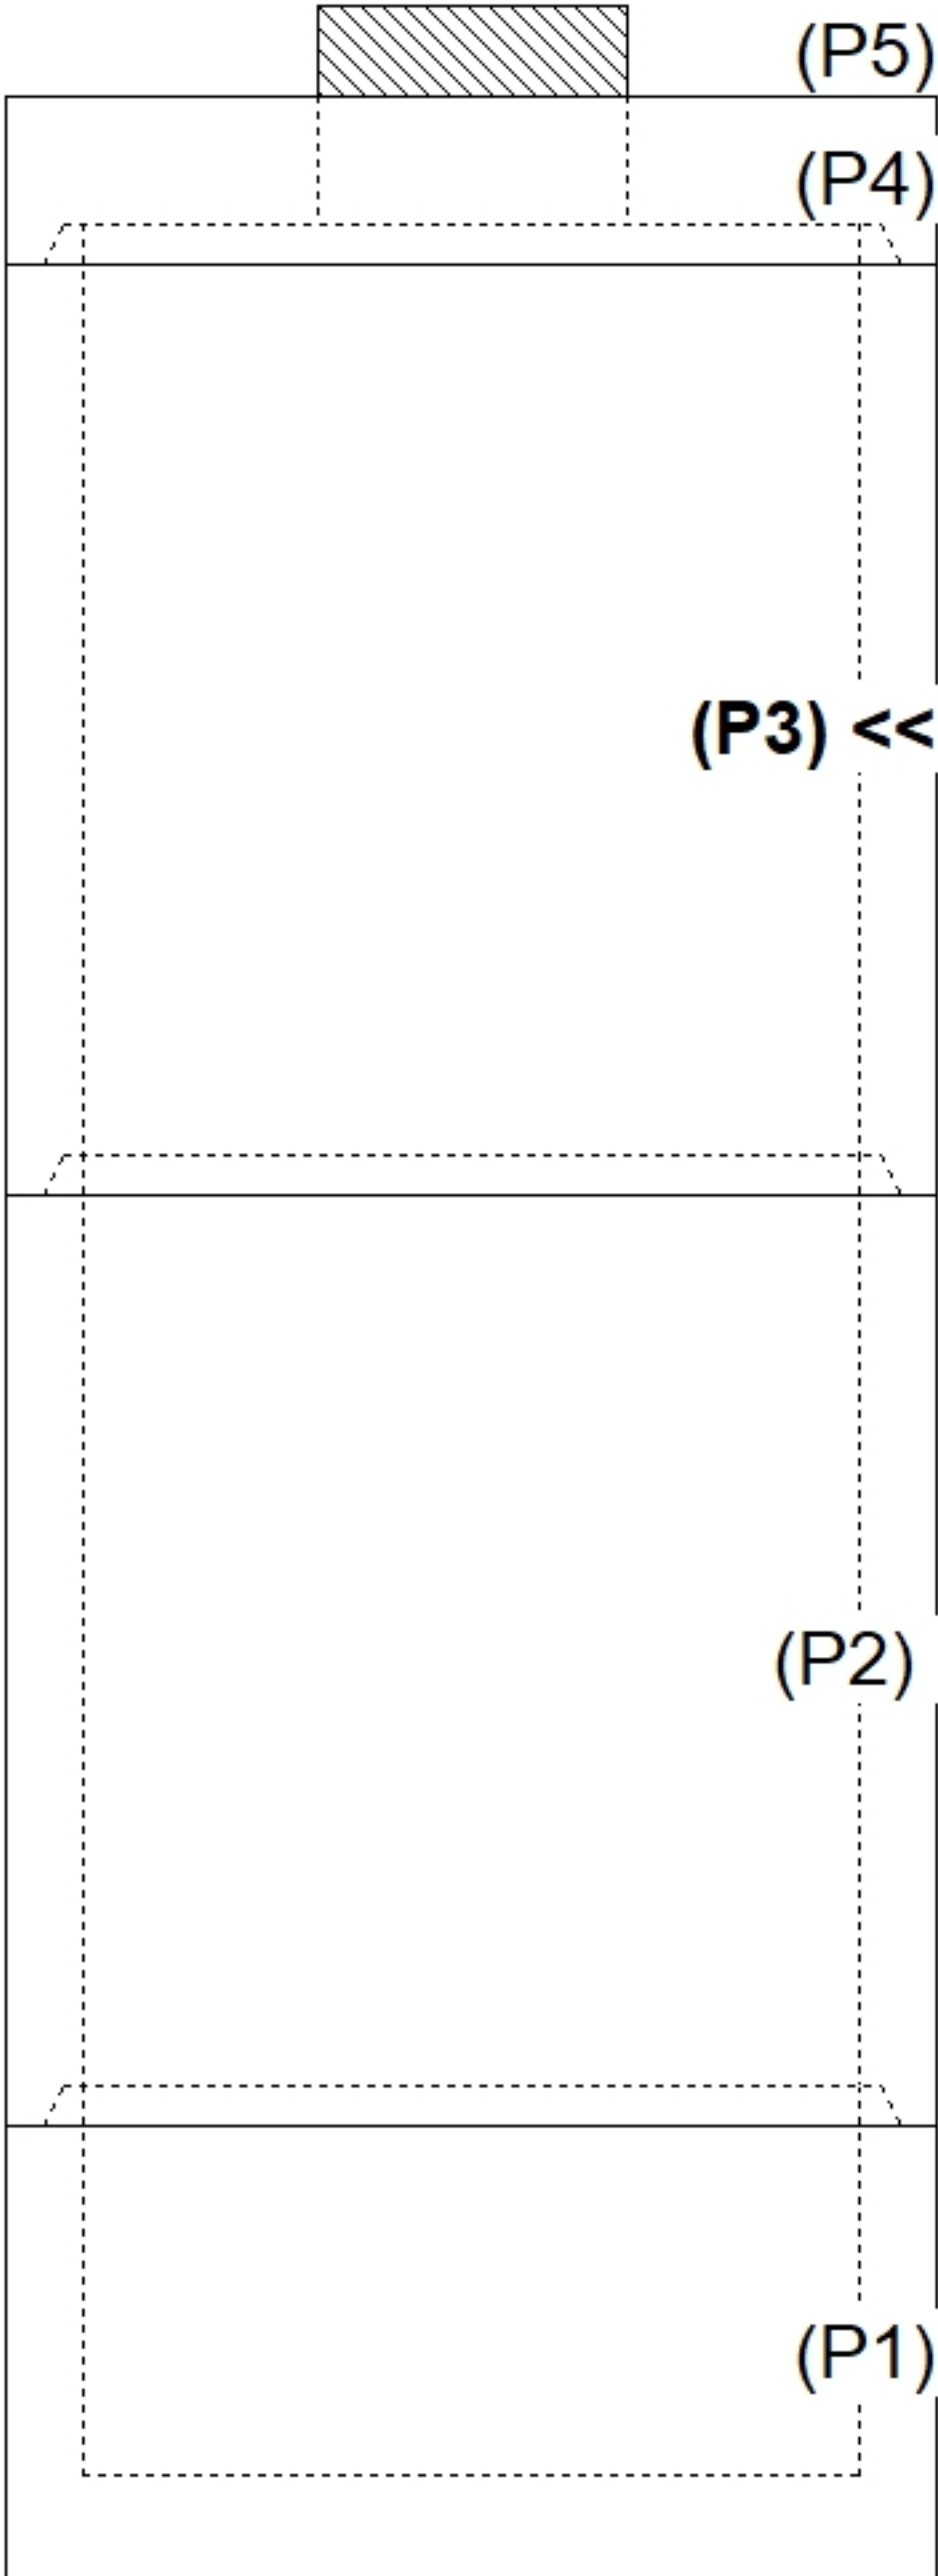
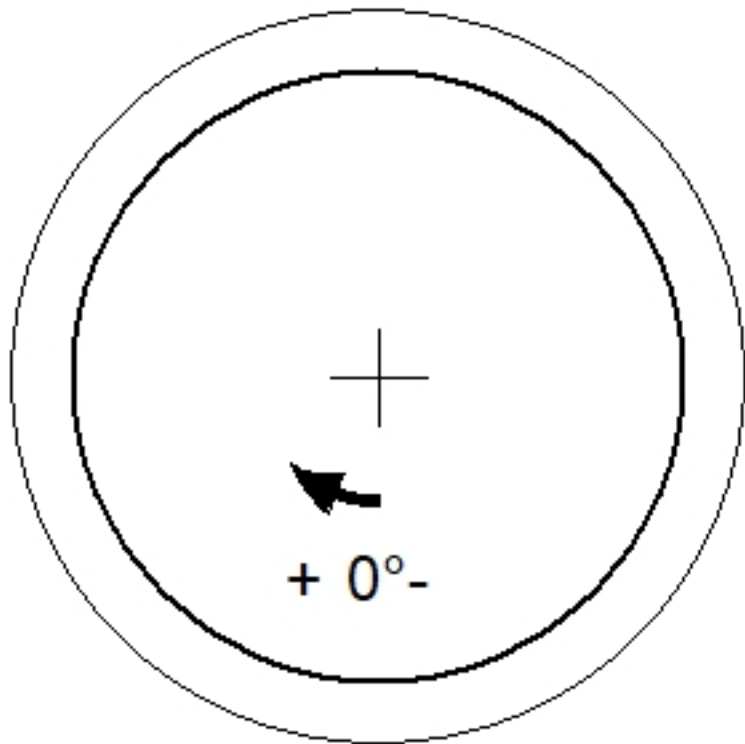
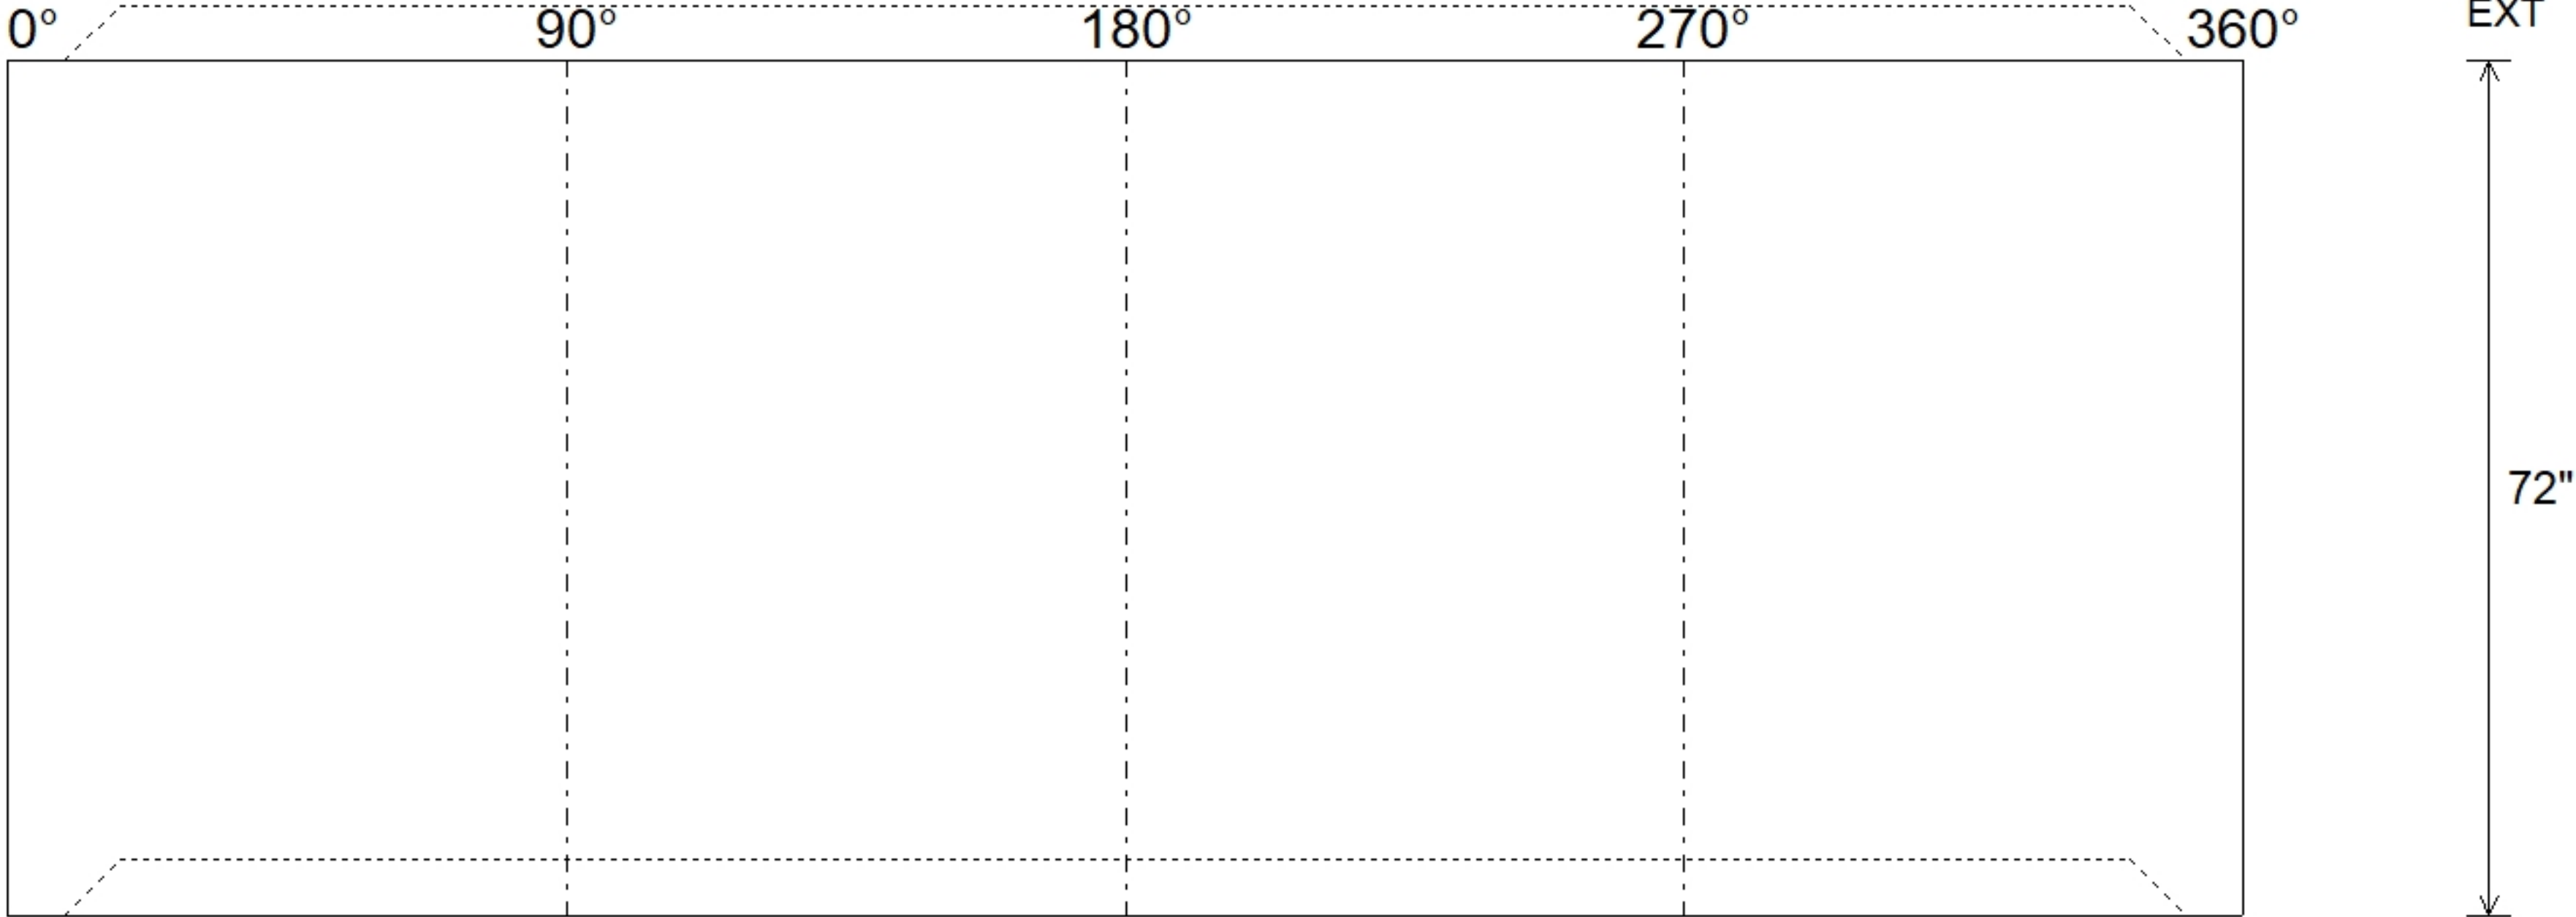


Job Name: 26-3183 ADS Freedom's Way Commons Job Location: Shelbyville, KY Contractor: ADS Advanced Drainage Systems, Inc.					Plant: Beaver Dam 8/14/2026 12:27:27 PM		Tech: S. Felletter PC: T. Ryan						
Structure ID: STR-14													
P3		MH060RS72S		MH RISER NO STEPS T/G									
P5) 24" - CASTING HEIGHT - 7" P4) 60" - MH FLAT TOP w/24" Ctr. Hole F/G - 13" P3) 60" - MH RISER NO STEPS T/G - 72" P2) 60" - MH RISER NO STEPS T/G - 72" P1) 60" - MH BASE Custom Ht T/n - 27" 1) ASSEMBLY REQUIRED 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) CASTING - HOE MC-375 F/C Storm 3) 60" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) Hole - 16						0 lb 2674 lb 7516 lb 7312 lb 5552 lb 0 lb 0 lb 0 lb 271 lb 0 lb 0 lb 0 lb ----- 23325 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-375 F/C "STORM"). 4. LIFTING ANCHORS TO BE INSTALLED ON THE OUTSIDE OF THE STRUCTURE. . REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - RISER/WALLS (As .18) - FLOOR (As .37) #5 BARS AT 10" C.C.E.W.					
Rim: 729.4'		Rim to Invert: 9.35'		Slack: 2.2"		Sump: 81"		Step Position:					
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset			
Invert 1													
Invert 2													
Invert 3													
Invert 4													
Invert 5													
Invert 6													
Invert 7													
Invert 8													
RIGHT-SIDE UP VIEW (int. dimensions)													
													
				INSIDE WALL DIMENSIONS									
													
Coating (Int): Coating (Ext):				Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 6" Floor Height: 0"		Height (Int): 72" Height (Ext): 72"		Weight (Net): 7516 lb Volume (Net): 1.92cu.yd			
