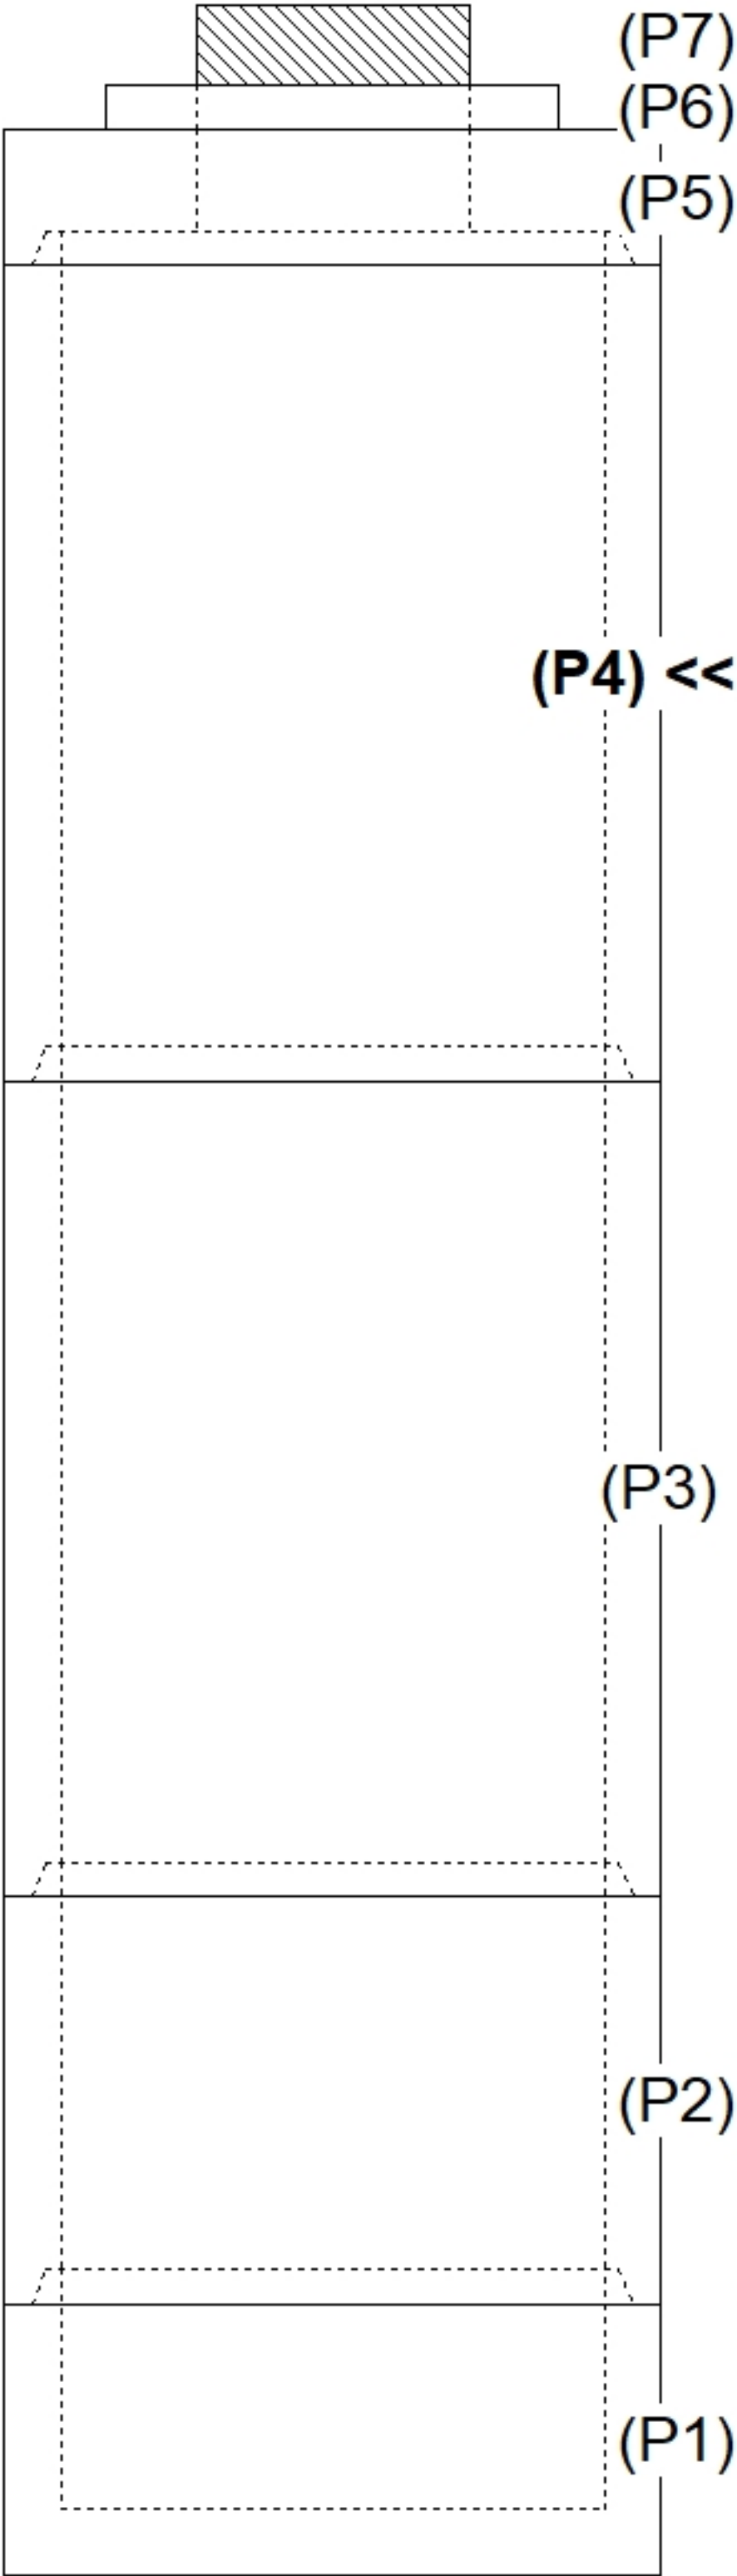
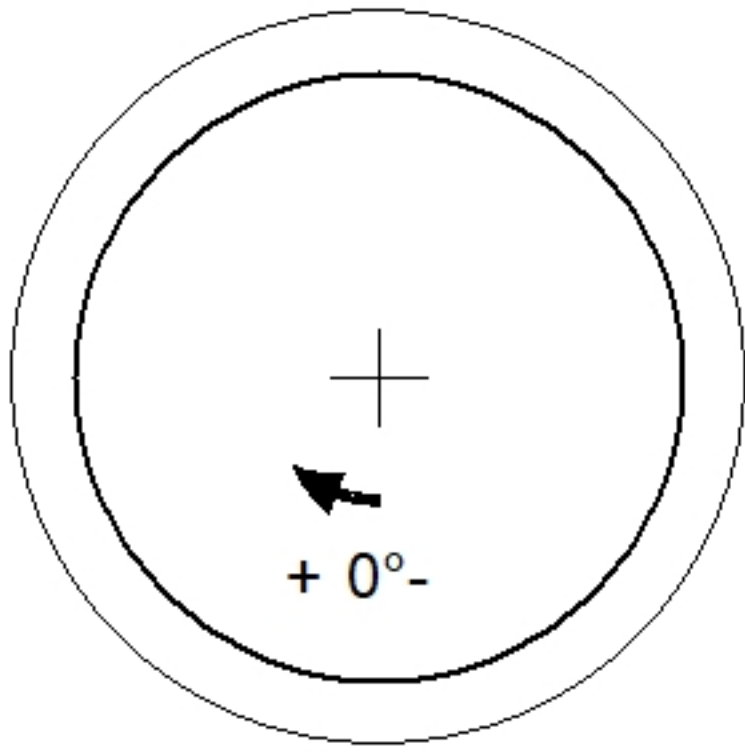
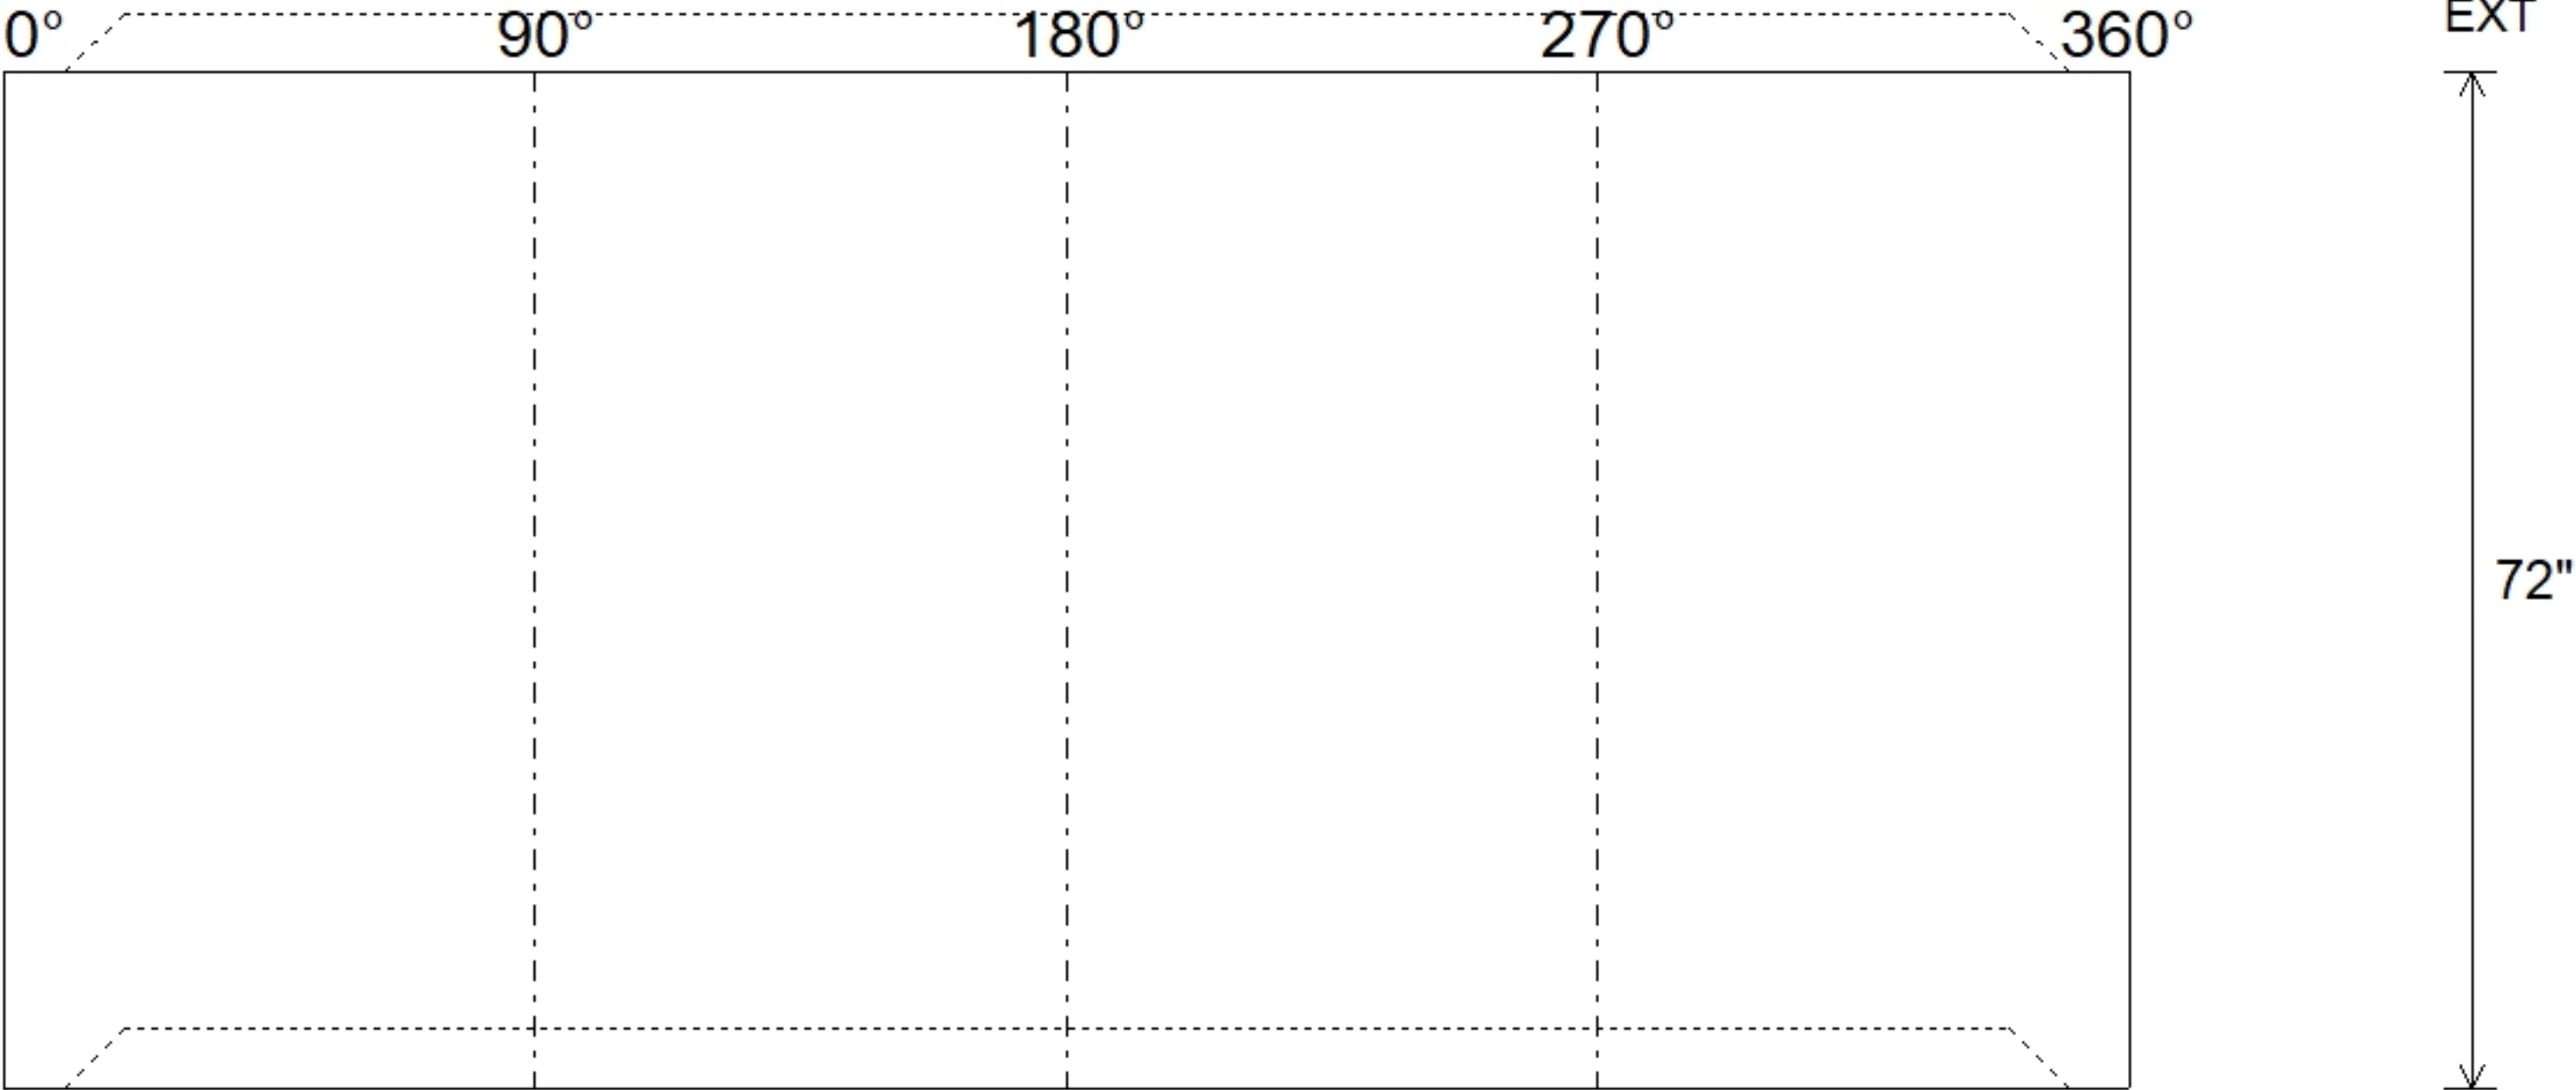


Job Name: 26-3354 ADS Nottingham Flats Job Location: Florence, KY Contractor: ADS Advanced Drainage Systems, Inc.					Plant: Beaver Dam 8/26/2026 10:58:12 AM		Tech: S. Felletter PC: M. Sullivan						
Structure ID: S227													
P4		MH048RS72S		MH RISER NO STEPS T/G									
P7) 24" - CASTING HEIGHT - 7" P6) 24" - GRADE RING F/F - 4" P5) 48" - MH FLAT LID w/24" Center Hole F/G - 12" P4) 48" - MH RISER NO STEPS T/G - 72" P3) 48" - MH RISER SPECIAL T/G - 72" P2) 48" - MH RISER NO STEPS T/G - 36" P1) 48" - MH BASE T/n - 18" 1) ASSEMBLY REQUIRED 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-375 F/C Storm 4) 48" - Conseal CS-102 1.00" 2) 24" - Conseal CS-102 1.00" 2) Hole - 30						0 lb 270 lb 1580 lb 5030 lb 4398 lb 2515 lb 2588 lb 0 lb 0 lb 0 lb 271 lb 0 lb 0 lb 0 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-375 F/C "STORM"). 4. LIFTING ANCHORS TO BE INSTALLED ON THE OUTSIDE OF THE STRUCTURE. 5. P2 & P3 RISERS TO BE MECHANICALLY ATTACHED PRIOR TO INTERNAL INSTALLATION/DELIVERY . REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.					
Rim: 925.03' Rim to Invert: 11.72' Slack: 0.64" Sump: 81" Step Position: 0°						Structure Total: 16651 lb							
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset			
Invert 1													
Invert 2													
Invert 3													
Invert 4													
Invert 5													
Invert 6													
Invert 7													
Invert 8													
RIGHT-SIDE UP VIEW (int. dimensions)													
													
				INSIDE WALL DIMENSIONS									
													
Coating (Int): Coating (Ext):				Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 5" Floor Height: 0"		Height (Int): 72" Height (Ext): 72"		Weight (Net): 5030 lb Volume (Net): 1.28cu.yd			
