

Job Name: 26-3482 892930 Seven Brew Overland MO
Job Location: Overland, MO
Contractor: Contech Engineering Solutions

Plant: Beaver Dam

8/27/2026 11:14:44 AM

Tech: S. Felletter

PC: C. Goff



Structure ID: 10-CS-4

P2 MH048RSVF

MH RISER Custom Ht T/G

P4) 30" - CASTING HEIGHT - 4"
P3) 48" - MH FLAT LID w/30in ECC Hole F/G - 12"
P2) 48" - MH RISER Custom Ht T/G - 44"
P1) 48" - MH BASE T/n - 36"
1) ASSEMBLY REQUIRED
1) CVSTENCILING
2) 48" - Conseal CS-102 1.00"
2) Hole - 16"


Structure Notes:
4" CASTING BY OTHERS
BASE & RISER TO BE MECHANICALLY
ATTACHED PRIOR TO ASSEMBLY
LIFTING ANCHORS TO BE INSTALLED
ON THE OUTSIDE OF THE STRUCTURE
ICAST TO INSTALL THE INTERNALS
CONTECH'S LOGO AS WELL AS THE
INLET AND OUTLET MUST BE
STENCILED ONTO THE STRUCTURE

Structure Total: 8152 lb


Rim: 583.66' Rim to Invert: 4.14' Slack: 1.68" Sump: 48" Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	579.52'	270°	136.659"	12" HDPE	14.5"	Hole 16	16"	16.312"	5.75"	0"
Invert 2	579.54'	212°	97.093"	12" HDPE	14.5"	Hole 16	16"	18.351"	5.99"	-10"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

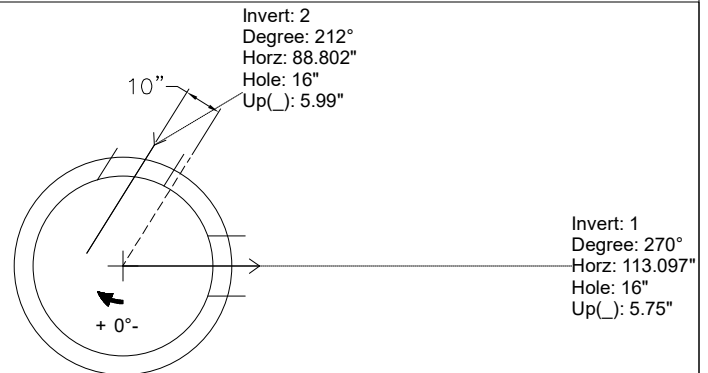

INSIDE WALL DIMENSIONS

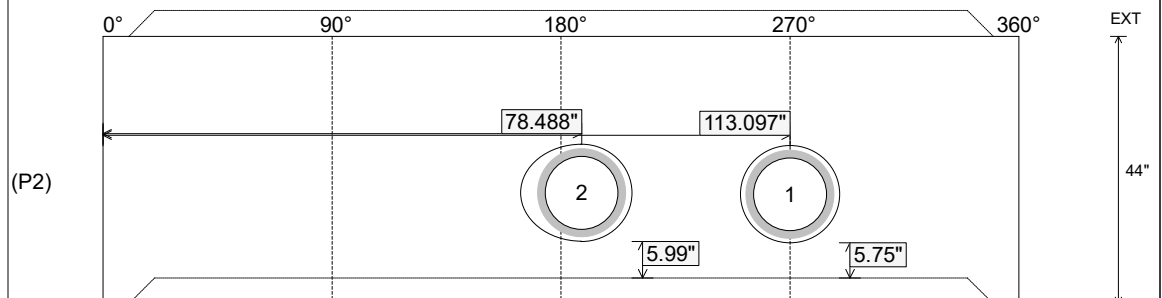

Coating (Int):
Coating (Ext):

Seam Up: Tongue
Seam Dn: Groove

Wall Thickness: 5"
Floor Height: 0"

Height (Int): 44"
Height (Ext): 44"

Weight (Net): 2894 lb
Volume (Net): 0.74cu.yd
