

Job Name: 26-3522 ADS Miller-Blankenbaker Rd. Subdivision
Job Location: Jeffersontown, KY
Contractor: ADS Advanced Drainage Systems, Inc.

Plant: Beaver Dam

9/2/2026 10:50:35 AM

Tech: S. Felletter

PC: M. Sullivan



Structure ID: STR-19

P4 MH036LD10


MH FLAT TOP w/ 24" Ctr. Hole F/G

- P6) 24" - CASTING HEIGHT - 7"
P5) 24" - GRADE RING F/F - 3"
P4) 36" - MH FLAT TOP w/ 24" Ctr. Hole F/G - 10"
P3) 36" - MH RISER T/G - 36"
P2) 36" - MH RISER T/G - 60"
P1) 36" - MH BASE T/n - 18"
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
1) ASSEMBLY REQUIRED
1) CASTING - HOE MC-375 F/C Storm
3) 36" - Conseal CS-102 1.00" (Double)
2) 24" - Conseal CS-102 1.00" (Double)
2) Hole - 12


- 0 lb
202 lb
896 lb
1518 lb
2454 lb
1525 lb
0 lb
0 lb
0 lb
271 lb
0 lb
0 lb
0 lb
0 lb
Structure Total: 6867 lb
- Structure Notes:**
1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. LIFTING ANCHORS TO BE INSTALLED ON THE OUTSIDE OF THE STRUCTURE
4. CASTING BY ICAST (HOE MC-375 F/C "STORM").
REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: #5 BAR @ 6" C.C. E.W. (GRADE 60).

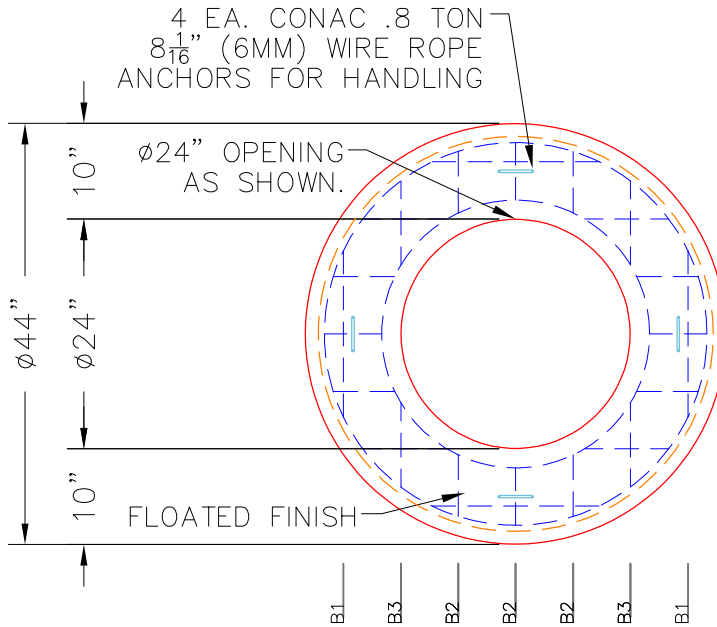

TOP VIEW

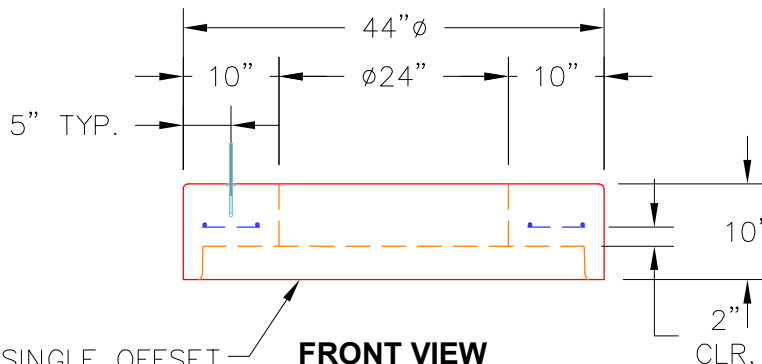

FRONT VIEW

REBAR TAKEOFF SUMMARY

BAR | SIZE | LENGTH | QTY

B1	#5	17 in (1'-5")	4 pcs
B2	#5	6 in (0'-6")	12 pcs
B3	#5	9 in (0'-9")	8 pcs
B4	#5	40 in (3'-4")	1 pcs
B5	#5	28 in (2'-4")	1 pcs

Total Pieces: 26 Pcs
Total Footage: 35.76 LF
Total Weight: 37.29 lbs (0.018 Tons)
TYP SPA = #5 BARS AT 6" C.C.E.W.

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 4"

Height (Ext): 10"

Weight (Net): 896 lb
Volume (Net): 0.23cu.yd
