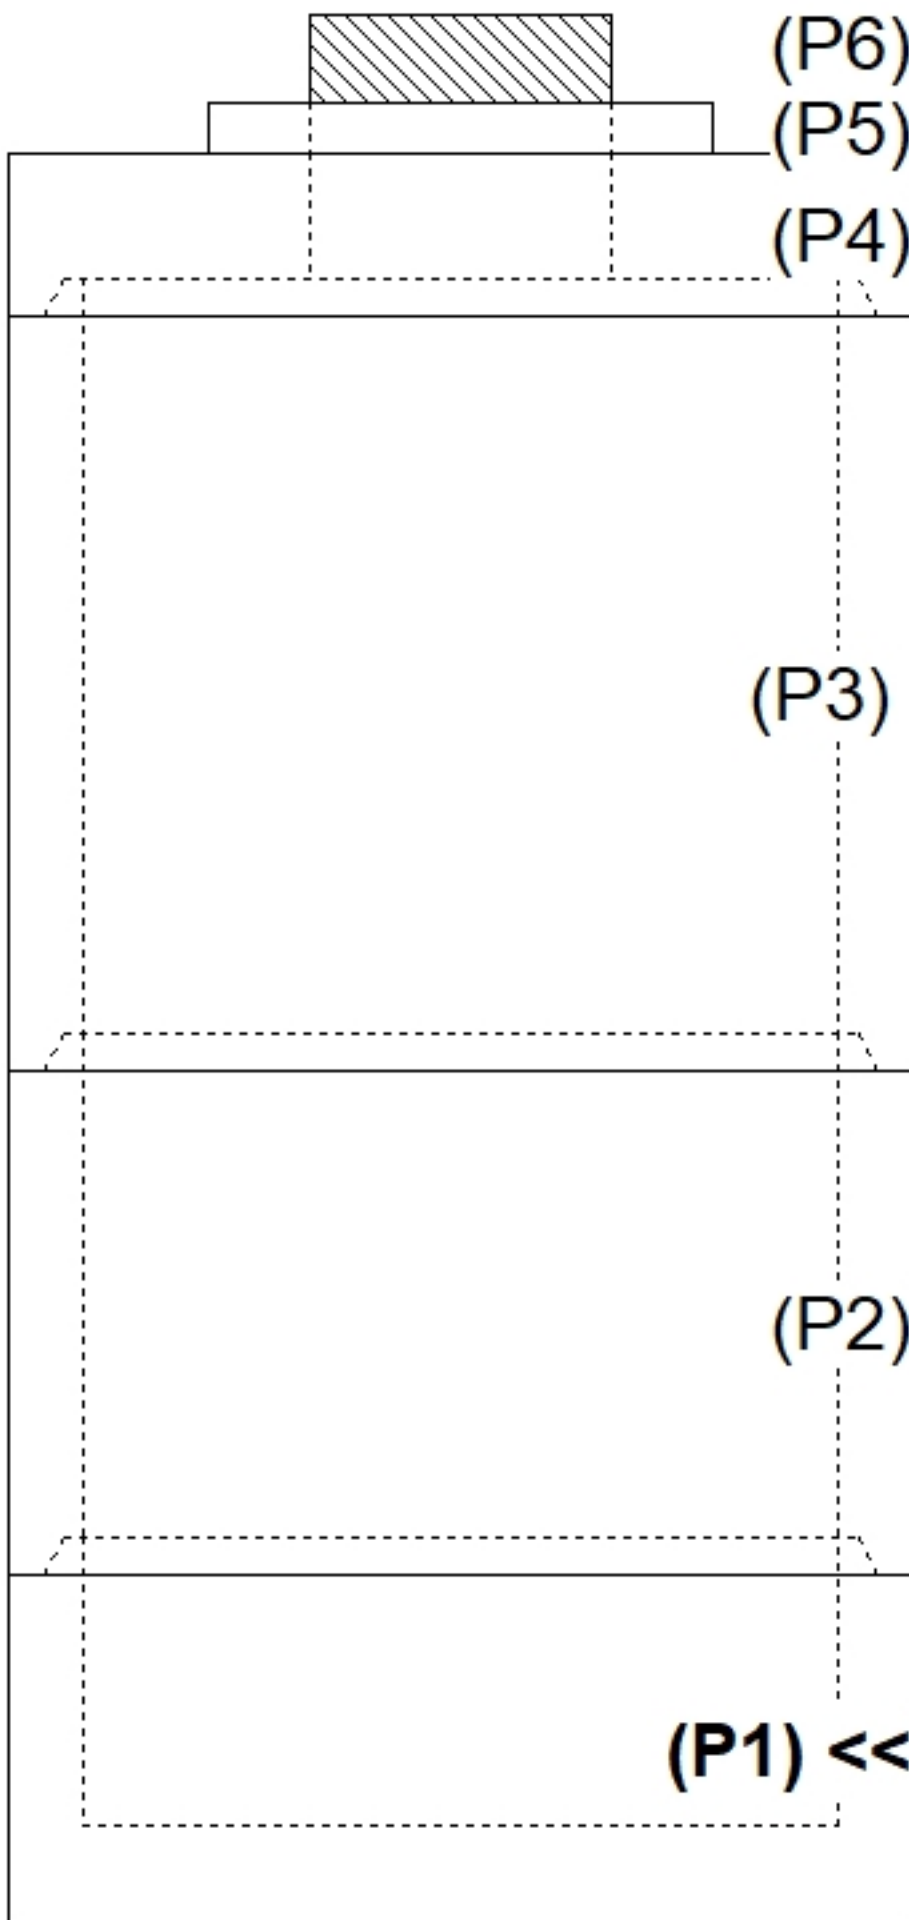
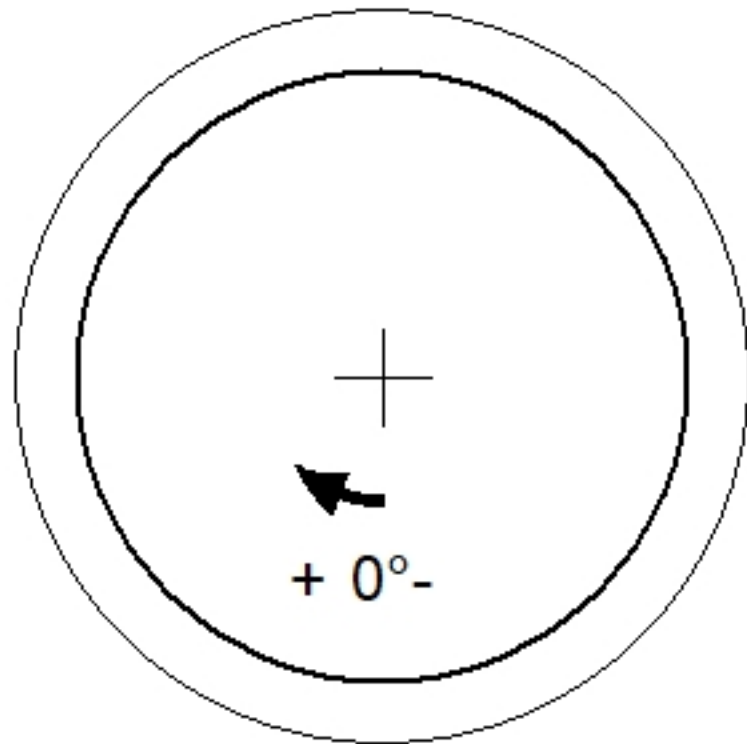
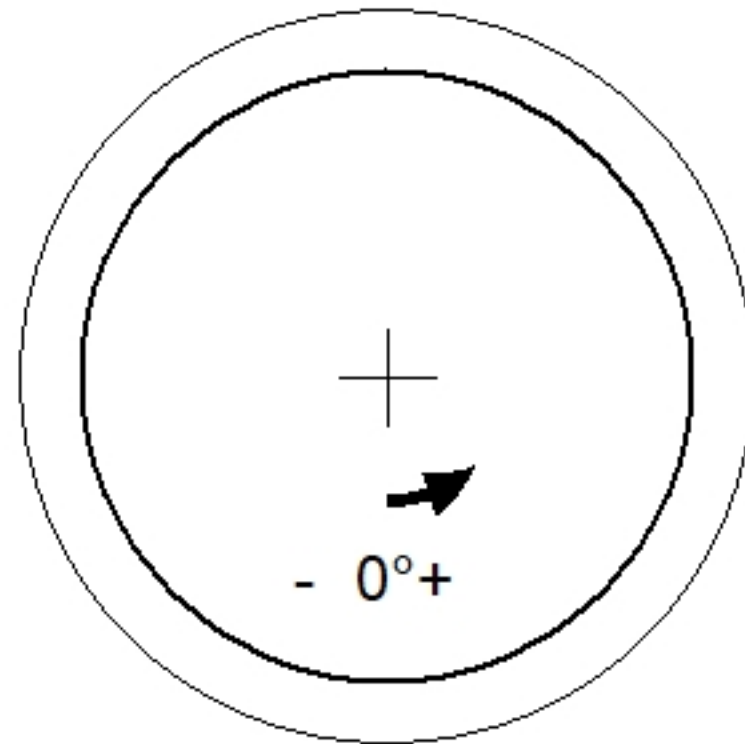
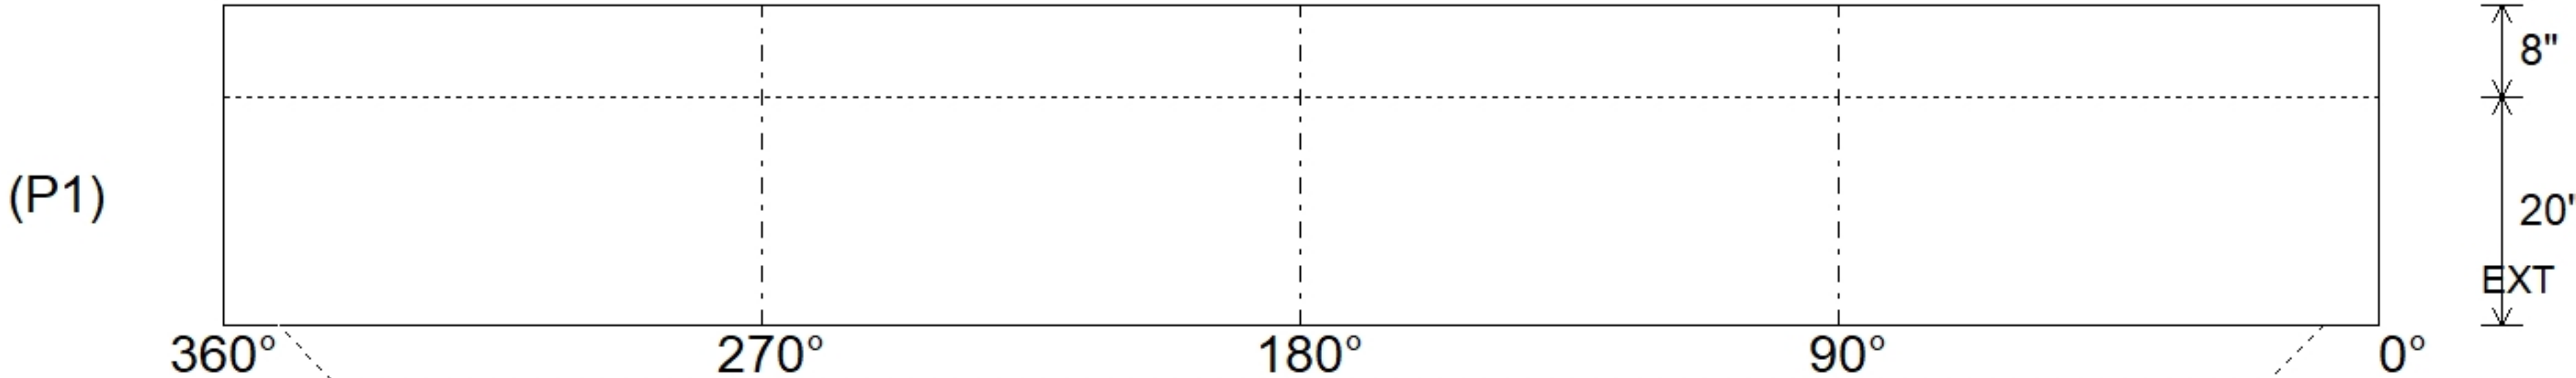


Job Name: 26-3632 ADS Wind Dance Farms Ph.2 Job Location: Fisherville, KY Contractor: ADS Advanced Drainage Systems, Inc.					Plant: Beaver Dam 9/18/2026 8:51:34 AM		Tech: S. Felletter PC: M. Sullivan				
Structure ID: WQU 1											
P1		MH060BAVF		MH BASE Custom Ht T/n							
P6) 24" - CASTING HEIGHT - 7" P5) 24" - GRADE RING F/F - 4" P4) 60" - MH FLAT TOP w/24" Ctr. Hole F/G - 13" P3) 60" - MH RISER SPECIAL T/G - 60" P2) 60" - MH RISER Custom Ht T/G - 40" P1) 60" - MH BASE Custom Ht T/n - 20" 1) ASSEMBLY REQUIRED 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-375 F/C Storm 3) 60" - Conseal CS-102 1.00" (Double) 2) 24" - Conseal CS-102 1.00" (Double) 2) Hole - 16					0 lb 270 lb 2674 lb 6013 lb 4176 lb 4821 lb 0 lb 0 lb 0 lb 271 lb 0 lb 0 lb 0 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-375 F/C "STORM"). 4. LIFTING ANCHORS TO BE INSTALLED ON THE OUTSIDE OF THE STRUCTURE. 5. P2 & P3 RISERS TO BE MECHANICALLY ATTACHED PRIOR TO INTERNALL INSTALLATION/DELIVERY. . REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - RISER/WALLS (As .18) - FLOOR (As .37) #5 BARS AT 10" C.C.E.W.				
Rim: 698.7' Rim to Invert: 5.3' Slack: 0.6" Sump: 81" Step Position: 0°					Structure Total: 18225 lb						
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (⌵)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
					RIGHT-SIDE UP VIEW (int. dimensions)			UPSIDE-DOWN VIEW (int. dimenions)			
											
					INSIDE WALL DIMENSIONS						
											
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: n/a		Wall Thickness: 6" Floor Height: 8"		Height (Int): 20" Height (Ext): 28"		Weight (Net): 4821 lb Volume (Net): 1.23cu.yd		
