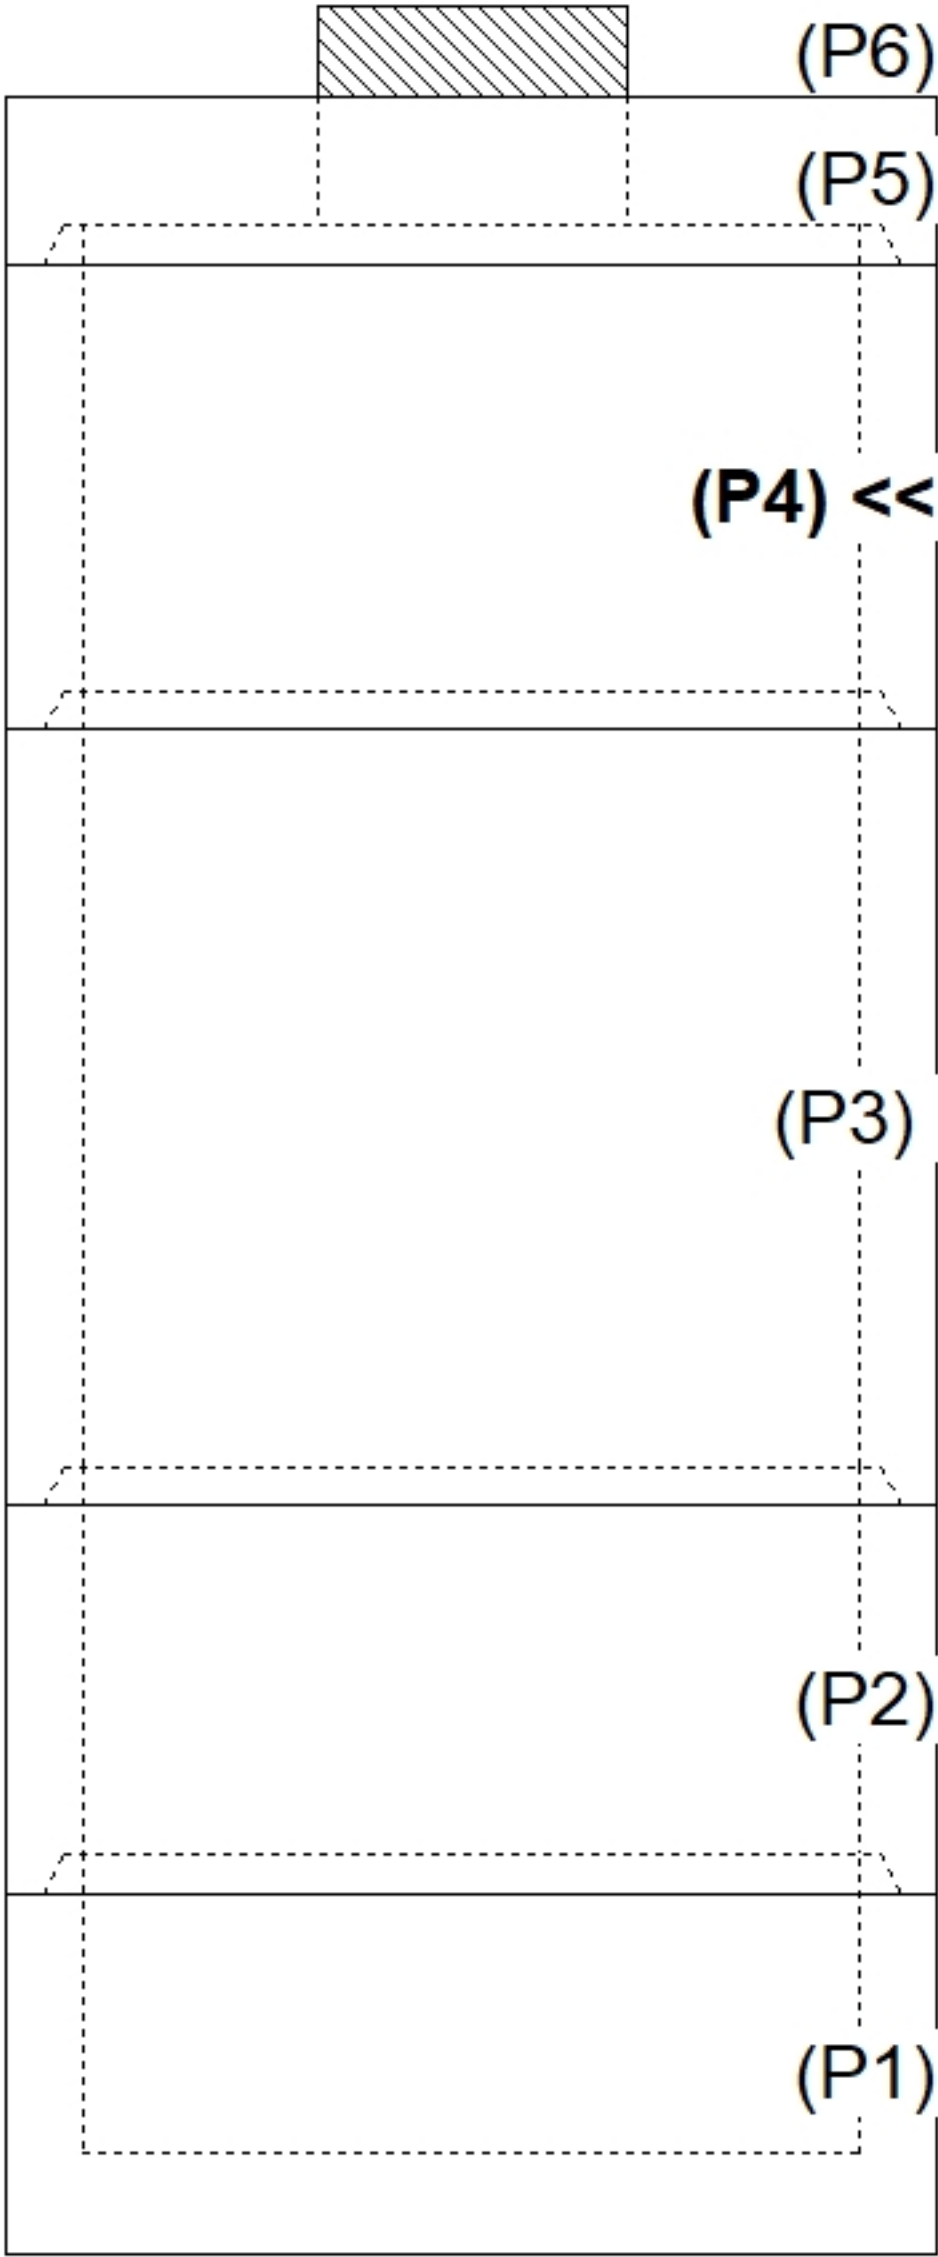
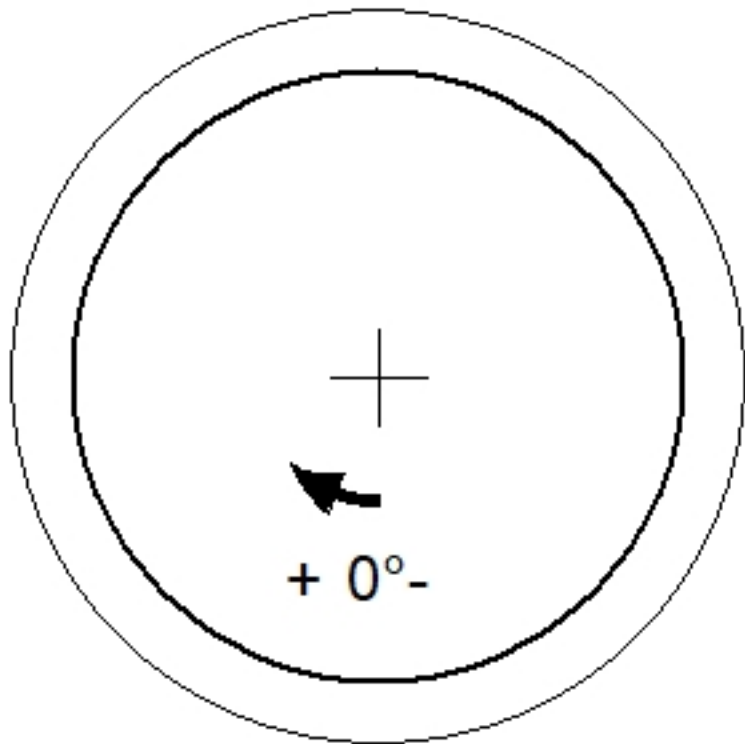
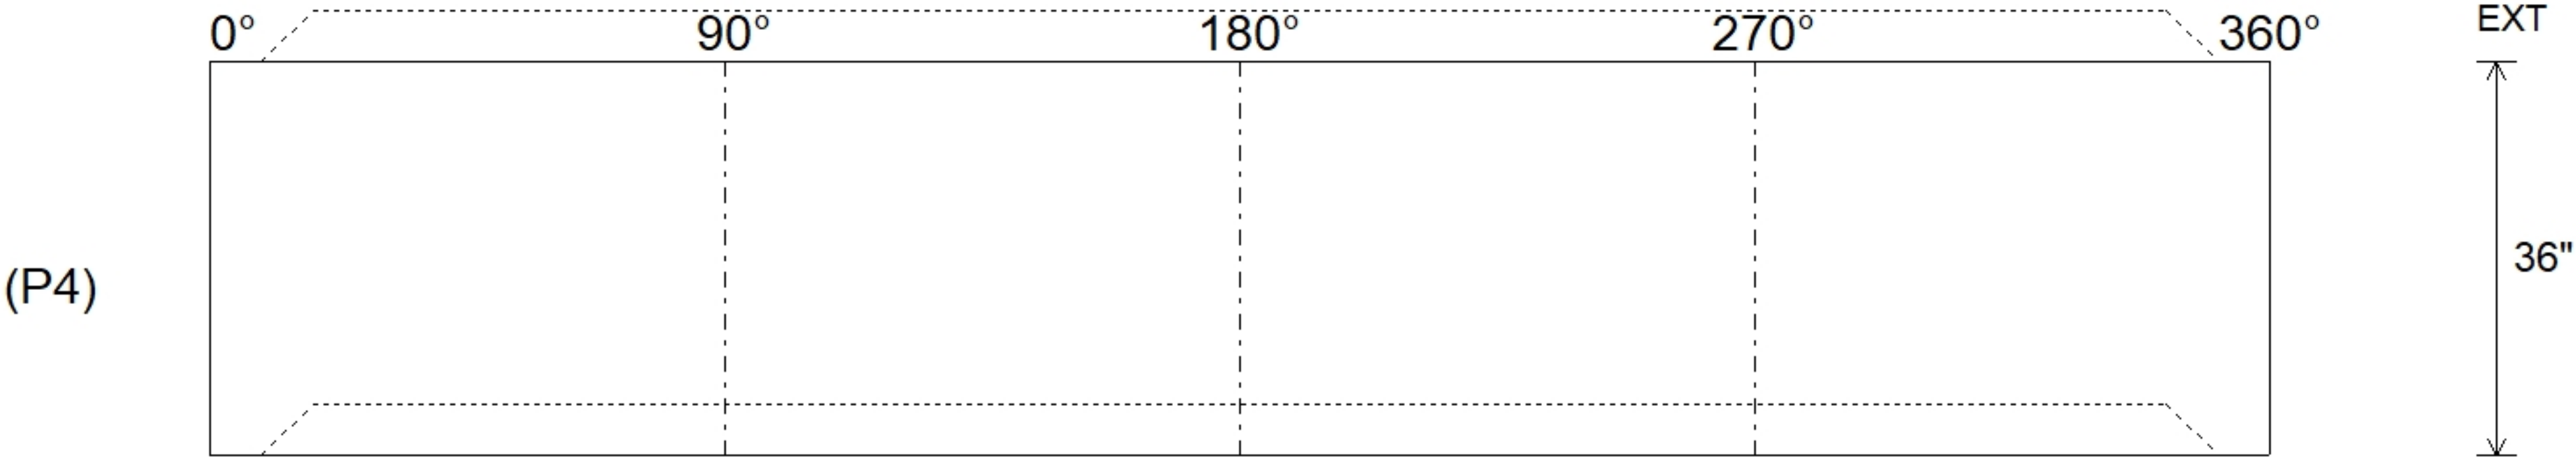


Job Name: 26-3632 ADS Wind Dance Farms Ph.2 Job Location: Fisherville, KY Contractor: ADS Advanced Drainage Systems, Inc.					Plant: Beaver Dam 9/18/2026 8:52:36 AM		Tech: S. Felletter PC: M. Sullivan				
Structure ID: WQU 2											
P4		MH060RS36S		MH RISER SPECIAL T/G							
P6) 24" - CASTING HEIGHT - 7" P5) 60" - MH FLAT TOP w/24" Ctr. Hole F/G - 13" P4) 60" - MH RISER SPECIAL T/G - 36" P3) 60" - MH RISER SPECIAL T/G - 60" P2) 60" - MH RISER SPECIAL T/G - 30" P1) 60" - MH BASE Custom Ht T/n - 20" 1) ASSEMBLY REQUIRED 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-375 F/C Storm 4) 60" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) Hole - 16						0 lb 2674 lb 3758 lb 6013 lb 3132 lb 4821 lb 0 lb 0 lb 0 lb 271 lb 0 lb 0 lb 0 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-375 F/C "STORM"). 4. LIFTING ANCHORS TO BE INSTALLED ON THE OUTSIDE OF THE STRUCTURE. 5. P2 & P3 RISERS TO BE MECHANICALLY ATTACHED PRIOR TO INTERNALL INSTALLATION/DELIVERY. . REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - RISER/WALLS (As .18) - FLOOR (As .37) #5 BARS AT 10" C.C.E.W.			
Rim: 674.5' Rim to Invert: 7.1' Slack: 0.2" Sump: 81" Step Position: 0°						Structure Total: 20669 lb					
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (┘)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)											
											
INSIDE WALL DIMENSIONS											
											
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 6" Floor Height: 0"		Height (Int): 36" Height (Ext): 36"		Weight (Net): 3758 lb Volume (Net): 0.96cu.yd		
